



水務署

Water Supplies Department

Contract No. 13/WSD/17

**Design, Build and Operate First Stage of Tseung Kwan O
Desalination Plant**

**Quarterly EM&A Report No.16
(Period from 1 December 2023 to 29 February
2024)**

Document No.

ASCL	/	200168078	/	QEMA16	/	4
Publisher		Project Code		Sequential No.		Revision Index

	Prepared by:	Reviewed and Certified by:
Name	Alex Leung	Jacky LEUNG
Position	Environmental Team Member	Environmental Team Leader
Signature		
Date:	2 April 2024	2 April 2024



Water Supplies Department
New Works Branch
Consultants Management Division
6/F Sha Tin Government Offices
1 Sheung Wo Che Road
Sha Tin
New Territories

Your reference:

Our reference: HKWSD202/50/109671

Date: 5 April 2024

Attention: Mr Sam Hui/ Mr H L Lai

BY EMAIL & POST
(email: wl_hui@wsd.gov.hk/
jack_hl_lai@wsd.gov.hk)

Dear Sirs

Agreement No. CE 5/2019 (EP)
Independent Environmental Checker for First Stage of
Tseung Kwan O Desalination Plant– Investigation
Verification of Quarterly EM&A Report No.16 (December 2023 – February 2024)

We refer to email of 2 April 2024 attaching Quarterly EM&A Report No.16 (December 2023 – February 2024) for the captioned project prepared by the ET.

We have no further comment and verify the report content between the reporting period of 1 December 2023 and 31 January 2024.

Should you have any queries regarding the above, please do not hesitate to contact the undersigned on 2618 2831.

Yours faithfully
ANEWR CONSULTING LIMITED

Alex Chan
Independent Environmental Checker

CYCA/csym



Our ref.: LES/J2024-01/CS/L003
Date : 3 Apr 2024

By Post and Email

Water Supplies Department
New Works Branch
Consultants Management Division
6/F, Sha Tin Government Offices,
1 Sheung Wo Che Road, Sha Tin,
New Territories

Attn: Mr. Sam Hui/ Mr H L Lai

Dear Sir,

**Independent Environmental Checker (IEC) for Construction and Operation of the
First Stage Desalination Plant at Tseung Kwan O (Quotation Ref. No. TKO1/IEC/003)**

**Verification for the period of 1 February 2024 to 29 February 2024 of Quarterly
Environmental Monitoring and Audit (EM&A) Report No.16 (Period from 1 December
2023 to 29 February 2024) V4**

Referring to the Quarterly Environmental Monitoring and Audit Report No.16 (Period from 1 December 2023 to 29 February 2024)_V4 as submitted by the Environmental Team on 2 April 2024, we hereby verify for the period of 1 February 2024 to 29 February 2024 of the captioned report for further submission to the Director's Representative of the Project.

Should you have any queries, please contact the undersigned at 61496683, or email at serenashk@lamenviro.com.

Yours sincerely,
For and On Behalf Of
Lam Environmental Services Limited

Serena Shek
Independent Environmental Checker

Binnies (Attn.: Raymond Kok)
Aurecon (Attn.: Jacky Leung)

By E-mail
By E-mail

REVISION HISTORY

REV.	DESCRIPTION OF MODIFICATION	DATE
1.	First Issue for Comments	22/03/2024
2.	Revisd according Comments	27/03/2024
3.	Revisd according Comments	28/03/2024
4	Revisd according Comments	02/04/2024

CONTENTS

Executive Summary.....	1
1. Basic Project Information.....	6
2. Noise.....	13
3. Water Quality.....	17
4. Waste	26
5. Landfill Gas Monitoring.....	27
6. Summary of Monitoring Exceedance, Complaints, Notification of Summons and Prosecutions.....	31
7. EM&A Site Inspection.....	33
8. Conclusions and Recommendations	34

Appendix A	Master Programme
Appendix B	Overview of Desalination Plant in Tseung Kwan O
Appendix C	Summary of Implementation Status of Environmental Mitigation
Appendix D	Water Quality Monitoring Graphical Presentation
Appendix E	Summary of Exceedances
Appendix F	Waste Flow Table
Appendix G	Complaint Log
Appendix H	Event/Action Plan for Water Quality Monitoring
Appendix I	Event/Action Plan for Construction Noise Exceedance
Appendix J	Event/Action Plan for Coral Monitoring Exceedance

EXECUTIVE SUMMARY

INTRODUCTION

- A1. The Project, Design, Build and Operate First Stage of Tseung Kwan O Desalination Plant (TKODP), is a Designated Project under the Environmental Impact Assessment Ordinance (Cap. 499) (EIAO) and is currently governed by a Further Environmental Permit (EP No. FEP – 01/503/2015/A) for the construction and operation of the Contract.
- A2. In accordance with the Environmental Monitoring and Audit (EM&A) Manual for the Contract, EM&A works for marine water quality, noise, waste management and ecology should be carried out by Environmental Team (ET), Acuity Sustainability Consulting Limited (ASCL), during the construction phase of the Contract.
- A3. This is the 16th Quarterly EM&A Report, prepared by ASCL, for the Contract summarizing the monitoring results and audit findings of the EM&A programme at and around Tseung Kwan O Area 137 (TKO 137) during the reporting period from 1 December 2023 to 29 February 2024.
- A4. The EM&A programme for this contract has covered environmental monitoring on construction noise level at selected NSRs and Contractor’s environmental performance auditing in the aspects of construction dust, construction noise, water quality, waste management, Landscape and Visual and Ecology.

SUMMARY OF MAIN WORKS UNDERTAKEN & KEY MITIGATION MEASURES IMPLEMENTED

- A5. Key activities carried out in this reporting period for the Project included the followings:

<p>Administration Building</p> <ul style="list-style-type: none">• Carrying out the floor tiles works at G/F• External wall painting works• Construction of block work for pipe duct• Installation of building services, cable laying, electrical switchboard, testing and commissioning
<p>Chemical building</p> <ul style="list-style-type: none">• Installation of leakage collection pit cover• Underground utility construction work• Landscape work at roof• Defect rectification
<p>Main Electrical & Central Chiller Plant Building</p> <ul style="list-style-type: none">• Installation of chillers, building services, electrical switchboard and cable laying• Installation of Roof Tile for Fuel Tank Room

<p>ActiDAFF</p> <ul style="list-style-type: none"> • Underground utility construction work • Installation of access opening cover • Construction of staircase no 2 • Installation of mechanical equipment, piping system, installation of building services, electrical switchboards and cable laying, fiber-reinforced plastic cover Installation
<p>Product Water Storage Tank Building</p> <ul style="list-style-type: none"> • Installation of Cat Ladders in Water Tank A • Sealing slab opening in water Tank A • Re-construction of Wall PW8 in Water Tank A • Installation of metal cladding, building services, cable laying, mechanical equipment, steel pipe • Underground utility construction
<p>OSCG Building</p> <ul style="list-style-type: none"> • Protective Coating for dangerous goods Rooms • Placing Soil Mix at Roof • Installation of Metal Cladding (at East Side) and Roller Shutters and Window • Underground utility construction work • Installation of building services, mechanical equipment and cable laying, testing and commissioning
<p>Reverse Osmosis Building</p> <ul style="list-style-type: none"> • Installation of building services, electrical switchboard, cable laying, Installation of mechanical equipment, steel pipe, Glass Reinforced Plastic pipe, raised floor, testing and commissioning • Installation of metal cladding, handrailing, roller shutters, glass canopy and glass house • Underground utility construction work • Construction of Reinforced Concrete External Wall for Male Toilet
<p>Post Treatment Building</p> <ul style="list-style-type: none"> • Installation of building services, Installation of mechanical equipment and piping system, Pressure Test • Underground utility construction work • Installation of Cat Ladders in Water Tanks • Installation of Metal Cladding • Placing Soil Mix at Roof
<p>Inspection corridor</p> <ul style="list-style-type: none"> • Installation of building services, Lift installation • Construction of roof tiling works and staircases no. 2 • Installation of Movement Joints and glass window

CO₂ Tanks

- Installation of pipes and electrical wiring, testing and commissioning

Combined Shaft and Pump room

- Finishing, Grating; window; louvre installation

Other

- Watermain works at CLP 132 kV Substation
- Staircases construction; Steel Bridge assembly and installation at elevated walkway
- Road Construction, Footpath Construction, Landscape Construction, Irrigation System Construction, Water Pressure Test for Fire Services and Plumbing System in Zone A, B, C
- Structure Construction, steel fence erection of Wave Deflector Wall at seawall area
- Slope work

- A6. The major environmental impacts brought by the above construction works include:
- Construction dust and noise generation from excavation works, construction works, slope works and rock cutting works; and
 - Waste generation from the construction activities
- A7. The key environmental mitigation measures implemented for the Project in this reporting period associated with the above construction works include:
- Dust suppression by regular wetting and water spraying for construction works;
 - Reduction of noise from equipment and machinery on-site and regularly inspection to machinery and plants/vehicles on-site to ensure proper functioning;
 - Sorting and storage of general refuse and construction waste;
 - Deployment of silt curtain at the inshore water outflow; and
 - Deployment protective fencing for trees.

SUMMARY OF EXCEEDANCE & INVESTIGATION & FOLLOW-UP

- A8. No noise monitoring was conducted during the reporting period since there are no project-related construction activities undertaken within a radius of 300m from the monitoring locations. No exceedance of the Action Level was recorded during the reporting period.
- A9. Referring to EM&A Manual, the general water quality monitoring should be carried out when there are marine-related construction activities undertaken. General water quality monitoring at the ten monitoring stations (CE, CF, WSR1, WSR2, WSR3, WSR4, WSR16, WSR33, WSR36 and WSR37) was ceased from 1 September 2023 due to the completion of marine-related construction works.
- A10. The pre-operation (testing and commissioning) phase of desalination plant started in reporting period. The EM&A works for pre-operation phase water quality were conducted during the reporting period in accordance with the EM&A Manual. [Seventy-eight \(78\)](#) of the

pre-operation phase water quality monitoring results of SS obtained had exceeded the Action Level. **Fifty-nine (59)** of the pre-operation phase water quality monitoring results of SS obtained during the reporting period had exceeded the Limit Level. After investigation, all exceedances were concluded unrelated to the Project.

- A11. Dechlorinated effluent monitoring at two sampling locations (Sampling point T1GKC01AA502/manhole 18) during disinfection was carried out by AJCJV on 2 and 3 December 2023 for Total Residual Chlorine monitoring (TRC). **Seven (7)** of dechlorinated effluent sample were taken in Sampling point T1GKC01AA502/manhole 18. No TRC exceedance of action or limit levels was obtained during the discharge of dechlorinated effluent. The dechlorinated effluent monitoring is completed.
- A12. In this reporting period, **216 times** of landfill gas monitoring were recorded at Wan Po Road (Ch0+390 – Ch0+780) and (Ch0+400 - Ch1+200). No action and limit level exceedance for methane, oxygen and carbon dioxide was recorded.
- A13. Pre-operation phase monthly coral monitoring was conducted during the reporting period on **28 December 2023, 30 January 2024 and 23 February 2024**. No sediment, bleaching or increased mortality in the general condition of all other tagged coral colonies were observed during the monthly operation phase monitoring period. No deterioration of the coral community was observed in the ecological monitoring results when compared with the baseline ecological monitoring results. There is no AL/LL exceedance during the monitoring period.
- A14. Pre-operation phase fishery monitoring for dry season was carried out on **17 and 24 February 2024**. The result of the monitoring would be present when it is available.
- A15. Weekly site inspections of the construction works were also carried out by ET to audit the mitigation measures implementation status. **Thirteen (13)** times of weekly Joint site inspections were carried out by ET and IEC.
- A16. A summary of the EM&A activities in this reporting period is listed in **Table I** and summary of the environmental exceedance of the reporting period is tabulated in **Table II**.

Table I Summary Table for EM&A Activities in the Reporting Period

EM&A Activities	Dec 2023	Jan 2024	Feb 2024
Noise Monitoring	N/A	N/A	N/A
Pre-operation Phase Water Quality Monitoring	12, 14, 16, 19, 21, 23, 26, 28 and 20 December 2023	2, 4, 6, 9, 11, 13, 16, 18, 20, 23, 25, 27 and 30 January 2024	1, 3, 5, 7, 9, 12, 15, 17, 20, 22, 24, 27 and 29 February 2024
TRC Monitoring for Main Disinfection	2 and 3 December 2023	N/A	N/A
Pre-operation Phase Coral Monitoring	28 December 2023	30 January 2024	23 February 2024

Pre-operation Phase Fishery Monitoring	N/A	N/A	17 and 24 February 2024
Landfill Gas monitoring	1, 2, 4, 5, 6, 7, 8, 9, 10, 11, 12, 13, 14, 15, 16, 18, 19, 20, 21, 22, 23, 27, 28 and 29 December 2023	2, 8, 9, 10, 11 and 12 January 2024	1, 2, 3, 5, 6, 7, 8, 9, 14, 15, 16, 17, 19, 20, 21, 22, 23, 24, 26, 27, 28 and 29 February 2024
Environmental Site Inspection	5, 12, 19, 27 December 2023	2, 9, 16, 25 and 29 January 2024	7, 16, 20 and 28 February 2024

Table II Summary Table for Exceedance in the Reporting Period

Environmental Monitoring	Parameter	No. of non-Project related exceedance		Total No. of non-Project related exceedance	No. of Project related exceedance		Total No. of Project related exceedance
		AL	LL		AL	LL	
Noise	Leq (30min)	N/A	N/A	N/A	N/A	N/A	N/A
Water	DO	0	0	0	0	0	0
	Turbidity	0	0	0	0	0	0
	SS	78	59	137	0	0	0
	pH	0	0	0	0	0	0
	Salinity	0	0	0	0	0	0
	TRC	0	0	0	0	0	0
Water (Main Disinfection)	TRC	0	0	0	0	0	0
Landfill Gas	O ₂	0	0	0	0	0	0
	CH ₄	0	0	0	0	0	0
	CO ₂	0	0	0	0	0	0

COMPLAINT HANDLING AND PROSECUTION

A17. One (1) environmental complaint was received during the reporting period. No notifications of summons or prosecution was received during the reporting period.

REPORTING CHANGE

A18. There was no change to be reported that may affect the on-going EM&A programme.

1. BASIC PROJECT INFORMATION

1.1. BACKGROUND

The Acciona Agua, S.A. Trading, Jardine Engineering Corporation Limited and China State Construction Engineering (Hong Kong) Limited and as AJC Joint Venture (AJCJV) is contracted to carry out the Design, Build and Operate First Stage of Tseung Kwan O Desalination Plant (DPTKO) under Contract No. 13/WSD/17 (the Contract).

Acuity Sustainability Consulting Limited (ASCL) is commissioned by AJCJV to undertake the Environmental Team (ET) services as required and/or implied, both explicitly and implicitly, in the Environmental Permit (EP), Environmental Impact Assessment Report (EIA Report) (Register No. AEIAR-192/2015) and Environmental Monitoring and Audit Manual (EM&A Manual) for the Contract; and to carry out the Environmental Monitoring and Audit (EM&A) programme in fulfillment of the EIA Report's EM&A requirements and Contract No. 13/WSD/17 Specification requirements.

Pursuant to the Environmental Impact Assessment Ordinance (EIAO), the Director of Environmental Protection granted the Environmental Permit (No. EP-01/503/2015) and Variation of Environmental Permit (No. EP-01/503/2015/A) to Water Supplies Department (WSD); and granted the Further Environmental Permit (No. FEP-01/503/2015/A) to AJCJV for the Contract.

1.2. THE REPORTING SCOPE

This is the 16th Quarterly EM&A Report for the Project which summarizes the key findings of the EM&A programme during the reporting period from 1 December 2023 to 29 February 2024.

1.3. PROJECT ORGANIZATION

The Project Organization structure for Construction Phase is presented in **Figure 1.1**.

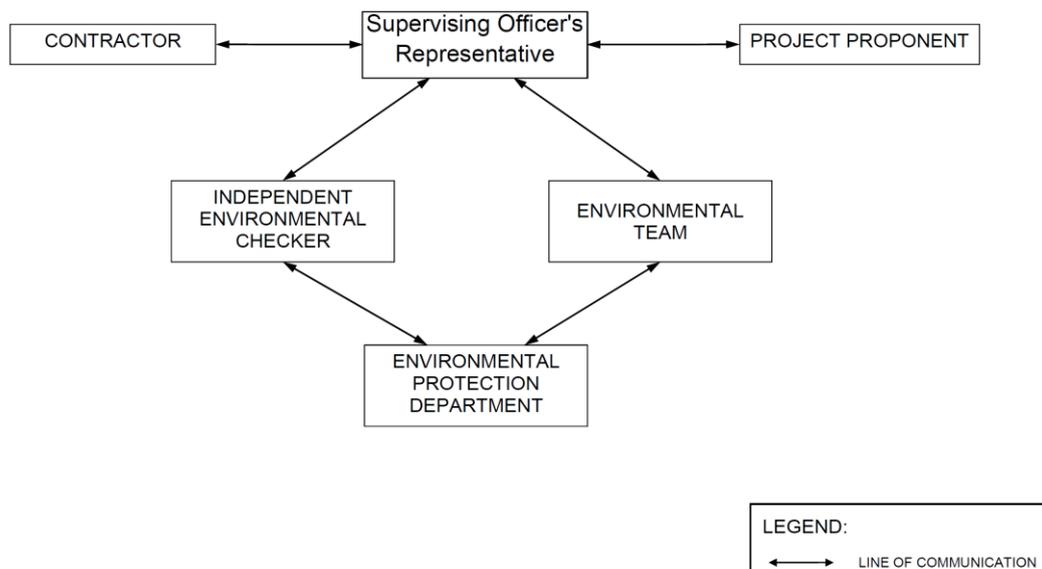


Figure 1.1 Project Organization Chart

Contact details of the key personnel are presented in **Table 1.1** below:

Table 1.1 Contact Details of Key Personnel

Party	Position	Name	Telephone no.	Remark
Project Proponent	SE/CM2	Milton Law	2634-3573	/
Supervising Officer (Binnies Hong Kong Limited)	Project Manager	Christina Ko	2608-7302	/
	Chief Resident Engineer	Roger Wu	6343-1002	/
The Jardine Engineering Corporation, Limited, China State Construction Engineering (Hong Kong) Limited and Acciona Agua, S.A. Trading	Project Manager	Stephen Yeung	2807-4665	/
	Environmental Monitoring Manager	Brian Kam	9456-9541	/
	Environmental Monitoring Manager	Joy Chan	6468-1782	/
Acuity Sustainability Consulting Limited	Environmental Team Leader	Jacky Leung	2698-6833	/
ANewR Consulting Limited	Independent Environmental Checker (IEC)	Alex Chan	2618-2831	(Until the end of January 2024)
Lam Environmental Services Limited	Independent Environmental Checker (IEC)	Serena Shek	6149-6683	(Started from February 2024)

1.4. SUMMARY OF CONSTRUCTION WORKS

Details of the major construction activities undertaken in this reporting period are shown as below. The construction programme is presented in **Appendix A**.

Administration Building

- Carrying out the floor tiles works at G/F
- External wall painting works
- Construction of block work for pipe duct
- Installation of building services, cable laying, electrical switchboard, testing and commissioning

Chemical building

- Installation of leakage collection pit cover
- Underground utility construction work
- Landscape work at roof
- Defect rectification

Main Electrical & Central Chiller Plant Building

- Installation of chillers, building services, electrical switchboard and cable laying
- Installation of Roof Tile for Fuel Tank Room

ActiDAFF

- Underground utility construction work
- Installation of access opening cover
- Construction of staircase no 2
- Installation of mechanical equipment, piping system, installation of building services, electrical switchboards and cable laying, fiber-reinforced plastic cover Installation

Product Water Storage Tank Building

- Installation of Cat Ladders in Water Tank A
- Sealing slab opening in water Tank A
- Re-construction of Wall PW8 in Water Tank A
- Installation of metal cladding, building services, cable laying, mechanical equipment, steel pipe
- Underground utility construction

OSCG Building

- Protective Coating for dangerous goods Rooms
- Placing Soil Mix at Roof
- Installation of Metal Cladding (at East Side) and Roller Shutters and Window
- Underground utility construction work
- Installation of building services, mechanical equipment and cable laying, testing and commissioning

Reverse Osmosis Building

- Installation of building services, electrical switchboard, cable laying, Installation of mechanical equipment, steel pipe, Glass Reinforced Plastic pipe, raised floor, testing and commissioning
- Installation of metal cladding, handrailing, roller shutters, glass canopy and glass house
- Underground utility construction work
- Construction of Reinforced Concrete External Wall for Male Toilet

Post Treatment Building

- Installation of building services, Installation of mechanical equipment and piping system, Pressure Test
- Underground utility construction work
- Installation of Cat Ladders in Water Tanks
- Installation of Metal Cladding
- Placing Soil Mix at Roof

Inspection corridor

- Installation of building services, Lift installation
- Construction of roof tiling works and staircases no. 2
- Installation of Movement Joints and glass window

CO₂ Tanks

- Installation of pipes and electrical wiring, testing and commissioning

Combined Shaft and Pump room

- Finishing, Grating; window; louvre installation

Other

- Watermain works at CLP 132 kV Substation
- Staircases construction; Steel Bridge assembly and installation at elevated walkway
- Road Construction, Footpath Construction, Landscape Construction, Irrigation System Construction, Water Pressure Test for Fire Services and Plumbing System in Zone A, B, C
- Structure Construction, steel fence erection of Wave Deflector Wall at seawall area
- Slope work

1.5. SUMMARY OF ENVIRONMENTAL STATUS

A summary of the valid permits, licences, and /or notifications on environmental protection for this Project is presented in **Table 1.2**.

Table 1.2 Summary of the Status of Valid Environmental Licence, Notification, Permit and Documentations

Permit/ Licences	Valid Period		Status	Remark
	From	To		
Environmental Permit				
EP – 503/2015/A	Throughout the Contract		Valid	-
FEP – 01/503/2015/A	Throughout the Contract		Valid	-
Notification of Construction Works under the Air Pollution Control (Construction Dust) Regulation (Form NA)				
451539	Throughout the Contract		Valid	-
Billing Account for Disposal of Construction Waste				
7036276	Throughout the Contract		Valid	-
Chemical Waste Producer Registration				
5213-839-A2987-01	Throughout the Contract		Valid	-
Wastewater Discharge Licence (Land and Marine works)				
WT00035775-2020	23/08/2021	31/07/2025	Valid	-
WT00044188-2023	16/06/2023	30/06/2025	Valid	-
Construction Noise Permit				
GW-RE0640-23	22/06/2023	21/12/2023	Valid	-
GW-RE1514-23	22/12/2023	21/06/2024	Valid	-

The status for all environmental aspects is presented in **Table 1.3**

Table 1.3 Summary of Status for Key Environmental Aspects under the EM&A Manual

Parameters	Status
Water Quality	
Baseline Monitoring under EM&A Manual	The baseline water quality monitoring was conducted between 12 May 2020 and 6 June 2020
Construction Phase Impact Monitoring	Ceased from 1 September 2023
Pre-operation Phase Impact Monitoring	On-going
TRC Monitoring for Main Disinfection	Completed
Noise	
Baseline Monitoring	The baseline noise monitoring result has been reported in Baseline Monitoring Report and submitted to EPD under EP Condition 3.4
Impact Monitoring	Completed
Waste Management	
Mitigation Measures in Waste Management Plan	On-going
Landfill Gas	
Regular Monitoring when Construction Works are within the 250m Consultation Zone	In this reporting period, 216 times of landfill gas monitoring were recorded at Wan Po Road (Ch0+390 – Ch0+780) and (Ch0+400 - Ch1+200). No exceedance of action or limit level for methane, oxygen and carbon dioxide was observed
Ecology (Coral)	
Pre-operation phase Regular Coral Monitoring (Monthly)	On-going
Ecology (Fishery)	
Pre-operation phase Regular Fishery Monitoring (Seasonally)	On-going
Ecology (Landscape)	
Pre-operation phase Landscape and Visual Site Inspection	On-going
Environmental Audit	
Site Inspection covering Measures of Air Quality, Noise Impact, Water Quality, Waste, Ecological Quality, Fisheries, Landscape and Visual	On-going

Other than the EM&A work by ET, environmental briefings, trainings and regular environmental management meetings were conducted, in order to enhance environmental awareness and closely monitor the environmental performance of the contractors.

The EM&A programme has been implemented in accordance with the recommendations presented in the approved EIA Report and the EM&A Manual. A summary of implementation status of the environmental mitigation measures for the construction phase and pre-operation phase of the Project during the reporting period is provided in **Appendix C**.

2. NOISE

2.1. MONITORING REQUIREMENTS

To ensure no adverse noise impact, construction noise monitoring is recommended to be carried out within 300m radius from the nearby noise sensitive receivers (NSRs), during construction phase. The NSRs selected as monitoring station are (i) NSR4 – Creative Secondary School, (ii) NSR24 – PLK Laws Foundation College, and (iii) NSR31 – School of Continuing and Professional Studies – CUHK respectively.

No impact construction noise monitoring was conducted in the reporting period due to the overly distant monitoring station from the works location, where they were farther than 1 km from the closet monitoring station NSR4 to the works location.

2.2. MONITORING PARAMETERS, FREQUENCY AND DURATION

Construction noise level would be measured in terms of the A-weighted equivalent continuous sound pressure level (LAeq). Leq_{30min} was used as the monitoring parameter for the time period between 0700 and 1900 on normal weekdays. **Table 2.1** summarizes the monitoring parameters, frequency and duration of the impact noise monitoring.

Table 2.1 Noise Monitoring Parameters, Time, Frequency and Duration

Time	Duration	Interval	Parameters
Daytime: 0700-1900	Day time: 0700-1900 (during normal weekdays)	Continuously in Leq _{5min} /Leq _{30min} (average of 6 consecutive Leq _{5min})	Leq _{30min} L _{10 30min} & L _{90 30min}

2.3. MONITORING LOCATIONS

The monitoring locations should normally be made at a point 1m from the exterior of the NSRs building façade and be at a position 1.2m above the ground. A correction of +3dB(A) should be made to the free-field measurements.

According to the environmental findings detailed in the EIA report and Baseline Monitoring Report, the designated locations for the construction noise monitoring are listed in **Table 2.2** below.

Table 2.2 Noise Sensitive Receivers

NSR ID	Noise Sensitive Receivers	Monitoring Location	Position
NSR 4	Creative Secondary School	Roof Floor	1 m from facade
NSR 24	PLK Laws Foundation College	Pedestrian Road on Ground Floor	Free-field
NSR 31	School of Continuing and Professional Studies - CUHK	Roof Floor	1 m from facade

The monitoring locations should normally be made at a point 1m from the exterior of the NSRs building façade and be at a position 1.2m above the ground. A correction of +3dB(A) should be made to the free-field measurements. Three noise monitoring locations for impact monitoring at the nearby sensitive receivers are shown in **Figure 2.1-2.3**.



Figure 2.1 NSR4 Creative Secondary School

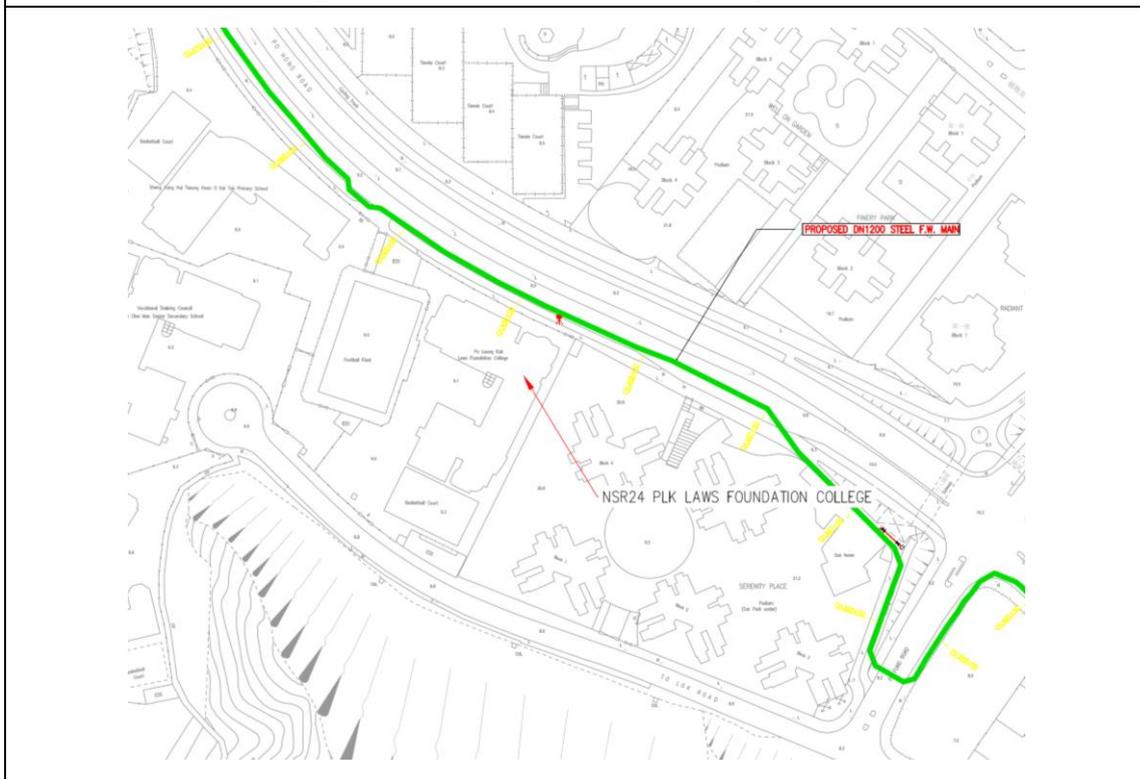


Figure 2.2 NSR24 PLK Laws Foundation College

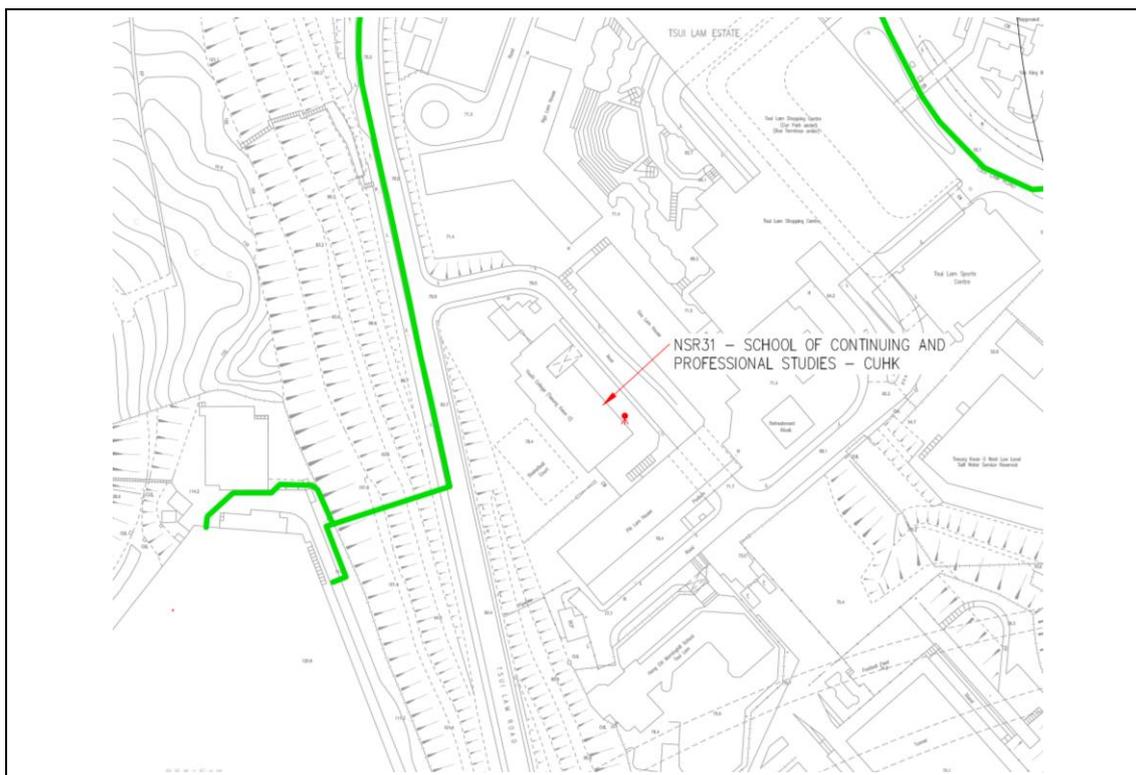


Figure 2.3 NSR31 School of Continuing and Professional Studies - CUHK

2.4. ACTION AND LIMIT LEVELS

The Action/Limit Levels are in line with the criteria of Practice Note for Professional Persons (ProPECC PN 2/93) “Noise from Construction Activities – Non-statutory Controls” and Technical Memorandum on Environmental Impact Assessment Process issued by HKSAR Environmental Protection Department [“EPD”] under the Environmental Impact Assessment Ordinance, Cap 499, S.16 are presented in **Table 2.3**.

Table 2.3 Action and Limit Levels for Construction Noise Monitoring per EM&A Manual

Time Period	Action Level	Limit Level (dB(A))
0700-1900 on normal weekdays	When one documented complaint is received from any one of the noise sensitive receivers	<ul style="list-style-type: none"> • 70 dB(A) for school and • 65 dB(A) during examination period

Notes: Limits specified in the GW-TM and IND-TM for construction and operation noise, respectively.

If exceedances were found during noise monitoring, the actions in accordance with the Event and Action Plan shall be carried out according to **Appendix E**.

2.5. MONITORING RESULTS AND OBSERVATIONS

Referring to EM&A manual Section 4.1.2, the impact noise monitoring should be carried out when there are project-related construction activities undertaken within a radius of 300m from the monitoring stations. As no Contract-related construction activities were undertaken in the reporting period within a radius of 300m from the monitoring stations of the Project site as shown in **Figure 2.4**, no impact noise monitoring was conducted in the reporting period.

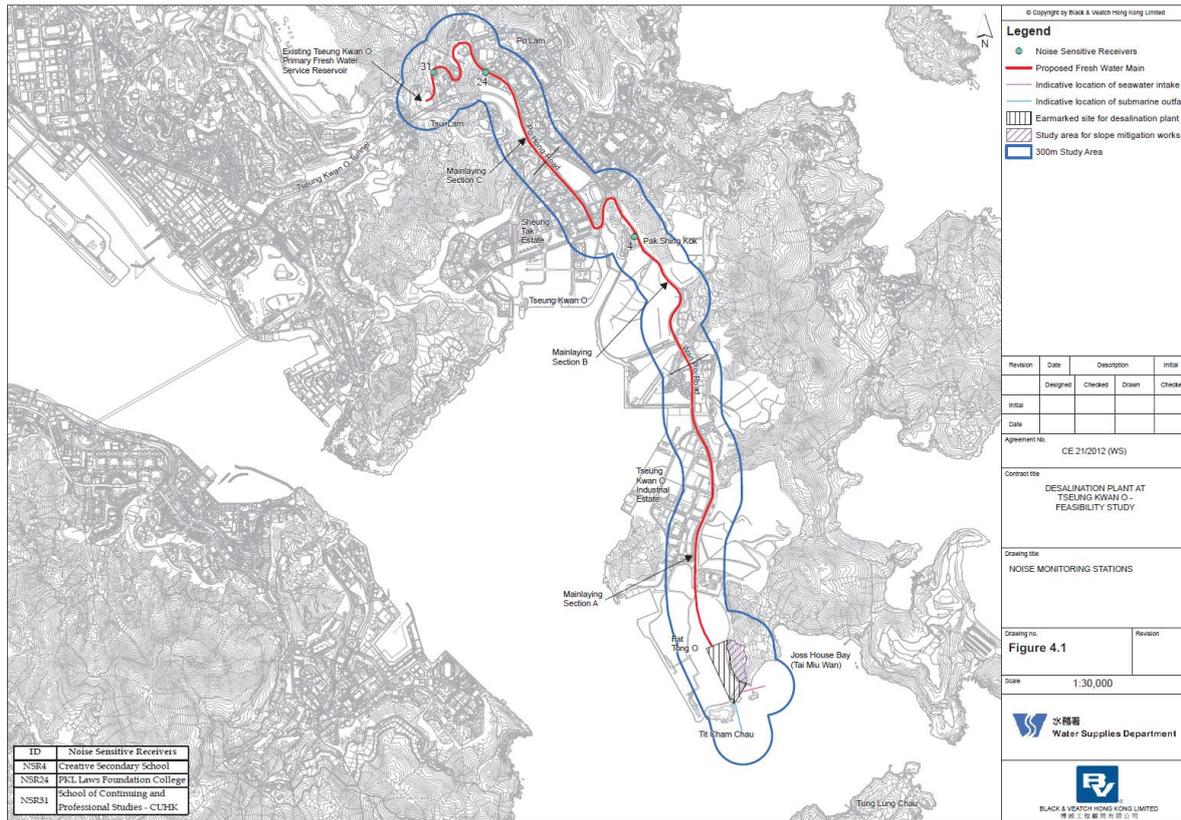


Figure 2.4 Site Layout Plan with Noise Sensitive Receivers and Desalination Plant

3. WATER QUALITY

In accordance with the recommendations of the EIA, water quality monitoring is required during dredging for the submarine pipelines and, during operation phase. In addition, baseline water quality monitoring was conducted prior to the commencement of marine construction activities. Additional water quality monitoring was conducted during pre-operation.

The following Section provides details of the water quality monitoring to be undertaken by the Environmental Team (ET) to verify the distance of sediment and brine plume dispersion and to identify whether the potential exists for any indirect impacts to occur to ecological sensitive receivers. The water quality monitoring programme was carried out to allow any deteriorating water quality to be readily detected and timely action taken to rectify the situation.

Water quality monitoring for the Project can be divided into the following stages:

- Dredging activities during construction phase;
- Discharge of effluent from main disinfection during construction phase;
- Commissioning activities during pre-operation (testing and commissioning) phase
- Operation phase – first year upon operation; and,
- Continuous monitoring of effluent quality.

3.1. WATER QUALITY PARAMETERS

The parameters that have been selected for measurement in situ and in the laboratory are those that were either determined in the EIA to be those with the most potential to be affected by the construction works or are a standard check on water quality conditions. Parameters measured in the impact monitoring are listed in **Table 3.1**

Table 3.1 Parameters measured in the impact marine water quality monitoring

Parameters	Unit	Abbreviation
In-situ measurements		
Dissolved oxygen	mg/L	DO
Temperature	°C	-
pH	-	-
Turbidity	NTU	-
Salinity	‰	-
Total Residual Chlorine	mg/L	TRC
Total Residual Chlorine (Disinfection)	mg/L	TRC
Laboratory measurements		
Suspended Solids	mg/L	SS
Iron	mg/L	
Anti-scalant	mg/L	-

NOTE 1: Monitoring of Total Residual Chlorine (Disinfection) will be conducted when cleaning and sterilization of the new freshwater main is carried out.

In addition to the water quality parameters, other relevant data were measured and recorded in Water Quality Monitoring Logs, including the location of the sampling stations, water depth, time, weather conditions, sea conditions, tidal stage, current direction and velocity, special phenomena and work activities undertaken around the monitoring and works area that may influence the monitoring results.

3.2. MONITORING LOCATIONS

Pre-operation (testing and commissioning) Phase

The impact water quality monitoring locations are detailed in **Table 3.2** and shown in **Figure 3.1** below.

Table 3.2 Location of Impact Water Quality Monitoring Station

Station	Easting	Northing	Description
CE	843550	815243	Upstream control station at ebb tide
CF	846843	810193	Upstream control station at flood tide
WSR1	846864	812014	Ecological sensitive receiver at Tung Lung Chau
WSR2	847645	812993	Fisheries sensitive receiver at Tung Lung Chau
WSR3	848023	813262	Ecological sensitive receiver at Tung Lung Chau
WSR4	847886	814154	Ecological sensitive receiver at Tai Miu Wan
WSR16	845039	815287	Ecological sensitive receiver at Fat Tong Chau
WSR33	847159	814488	Ecological sensitive receiver at Tai Miu Wan
WSR36	846878	814081	Ecological sensitive receiver at Kwun Tsai
WSR37	846655	813810	Ecological sensitive receiver at Tit Cham Chau
NF1	846542	813614	Edge of mixing zone, ~ 200m west of outfall diffuser
NF2	846942	813614	Edge of mixing zone, ~ 200m east of outfall diffuser
NF3	846742	813414	Edge of mixing zone, ~ 200m south of outfall diffuser

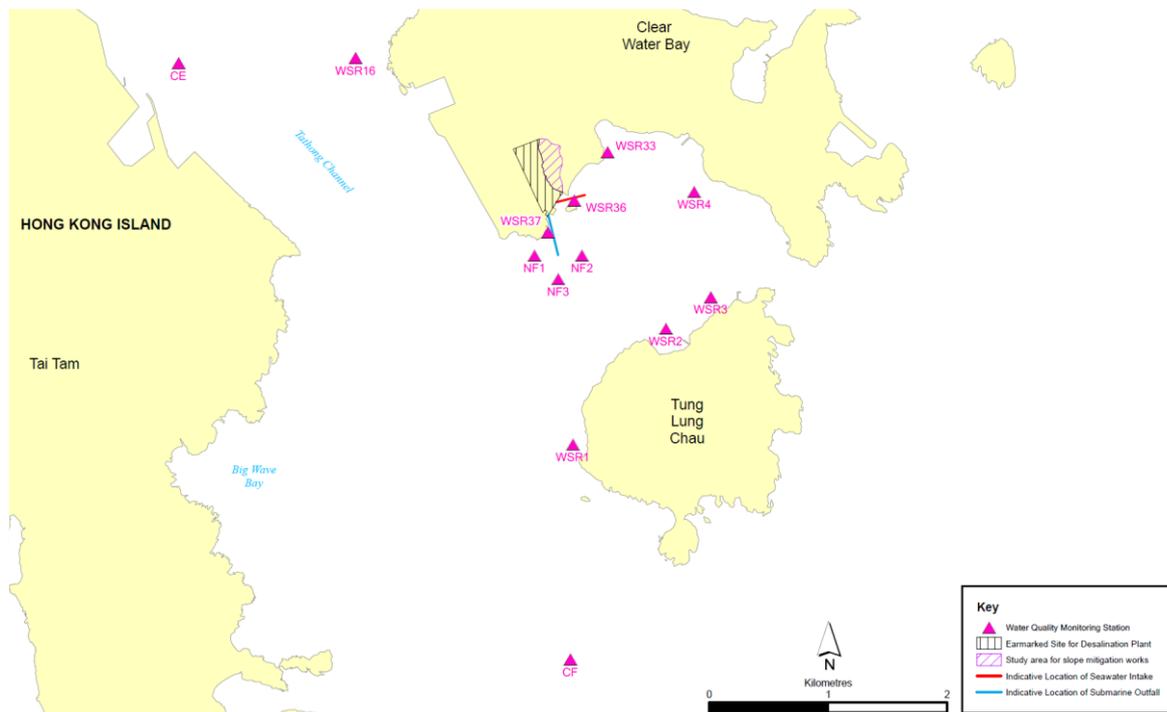


Figure 3.1 Impact Water Quality Monitoring Locations under EM&A Manual

Main Disinfection

According to the approved Flushing and Disinfection Procedure and Supplementary of the Disinfection Procedure for Desalination Plant at Tseung Kwan O, the sampling point of the dechlorinated effluent was located at Contact tank/Product Water Tank (PWT) and T1GKC01AA502/manhole 18.

The approved sampling location was shown in **Table 3.3, Figure 3.2 and Figure 3.3** below.

Table 3.3 Sampling location of dechlorinated effluent

System/Loop	Discharge location	Sampling Location	Parameter
Contact tank/ Product Water Tank (PWT)	Culvert	Contact tank/PWT	TRC
Connection to dist. network	Manhole 18 in connection point	Sampling point T1GKC01AA502/manhole 18	

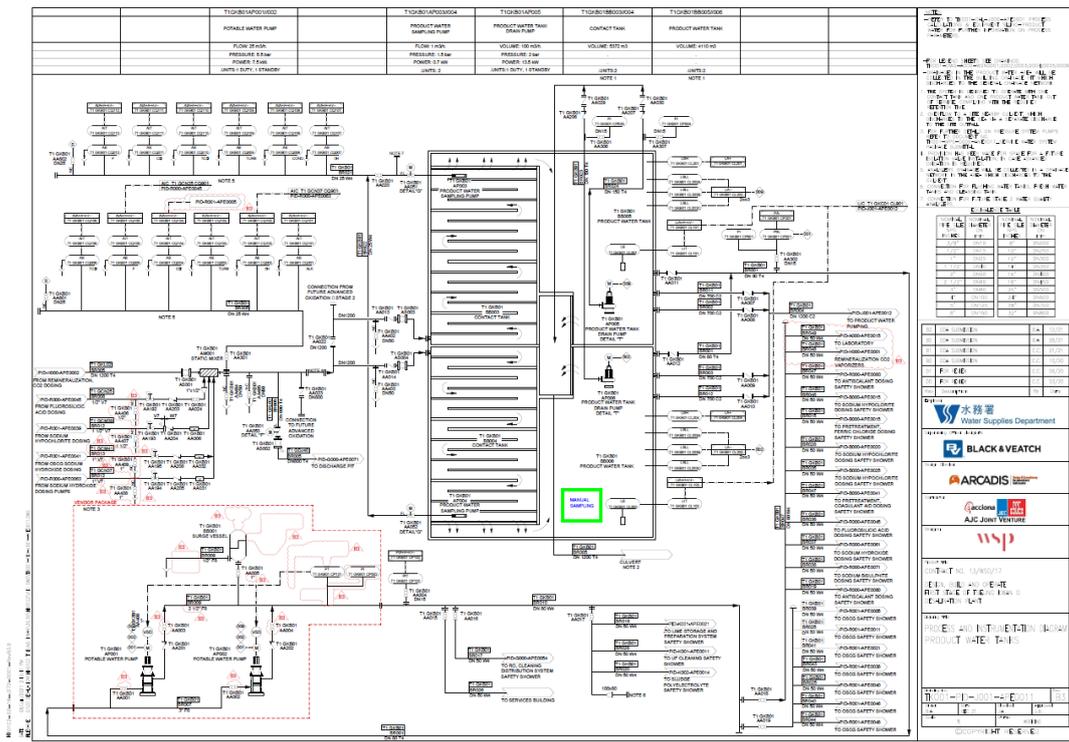


Figure 3.2 Impact water quality monitoring point for dechlorinated effluent (Contact tank/PWT)

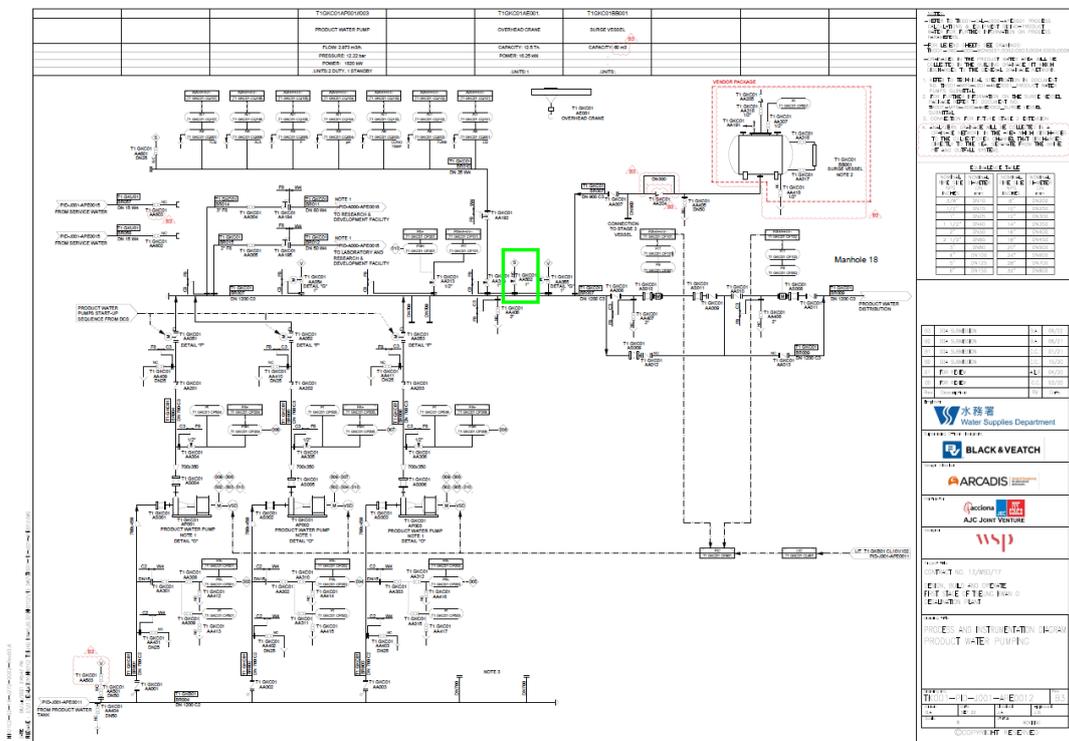


Figure 3.3 Impact water quality monitoring point for dechlorinated effluent (Sampling point T1GKC01AA502/manhole 18)

3.3. MONITORING EQUIPMENT, METHODOLOGY AND QA/QC PROCEDURES

The monitoring methodology, equipment used, and QA/QC procedures could be referred to Section 3.1.2 -3.1.4, 3.1.6-3.1.7 and 3.2 of the Monthly EM&A Report.

3.4. ACTION AND LIMIT LEVELS

The Action and Limit Levels have been set based on the derivation criteria specified in the EM&A Manual and based on the baseline water quality monitoring data and the derivation criteria, the Action/Limit Levels have been derived and are presented in **Table 3.4**.

Table 3.4 Derived Action and Limit Levels for Water Quality

Parameters	Action	Limit
Pre-Operation (Testing and Commissioning) Phase Impact Monitoring		
DO in mg/L	<u>Surface and Middle</u> 7.30 mg L ⁻¹ <u>Bottom</u> 7.31 mg L ⁻¹ <u>Tung Lung Chau Fish Culture Zone</u> 5.1 mgL ⁻¹ or level at control station (Whichever the lower)	<u>Surface and Middle</u> 4 mg L ⁻¹ <u>Bottom</u> 2 mg L ⁻¹ <u>Tung Lung Chau Fish Culture Zone</u> 5.0 mgL ⁻¹ or level at control station (Whichever the lower)
SS in mg/L (Depth-averaged)	5.00 mg L ⁻¹ or 20% exceedance of value at any impact station compared with corresponding data from control station	6.00 mg L ⁻¹ or 30% exceedance of value at any impact station compared with corresponding data from control station
Turbidity in NTU (Depth-averaged)	2.41 NTU or 20% exceedance of value at any impact station compared with corresponding data from control station	2.84 NTU or 30% exceedance of value at any impact station compared with corresponding data from control station
Salinity in PSU (Depth-averaged)	34.28 PSU or 9% exceedance of value at any impact station compared with corresponding data from control station	34.60 PSU or 10% exceedance of value at any impact station compared with corresponding data from control station
Iron in mg/L (Depth-averaged)	0.3 mg/L	0.3 mg/L
Total residual chlorine in mg/L	0.01 mg/L	0.01 mg/L
Total residual chlorine in mg/L (Disinfection)	0.1 mg/L	0.1 mg/L

Notes:

- i. "Depth-averaged" is calculated by taking the arithmetic means of reading of all three depths.
- ii. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
- iii. For Turbidity, SS, iron and Salinity, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.

3.5. MONITORING RESULTS AND OBSERVATIONS

Construction Phase

Referring to EM&A Manual, the general water quality monitoring should be carried out when there are marine-related construction activities undertaken. General water quality monitoring at the ten monitoring stations (CE, CF, WSR1, WSR2, WSR3, WSR4, WSR16, WSR33, WSR36 and WSR37) was ceased from 1 September 2023 due to the completion of marine-related construction works.

Pre-operation (testing and commissioning) Phase

Considering the first pre-operation phase of Tseung Kwan O Desalination Plant was started in the reporting period, additional marine water quality monitoring was conducted at the thirteen monitoring stations (CE, CF, WSR1, WSR2, WSR3, WSR4, WSR16, WSR33, WSR36, WSR37, NF1, NF2 and NF3) from 12 December 2023. The Action and Limit Level would be referred to the approved EM&A Manual Table 5.4 First-year Operation Phase Marine Water Monitoring.

The additional marine water quality monitoring was conducted at the thirteen monitoring stations on 12, 14, 16, 19, 21, 23, 26, 28 and 20 December 2023, 2, 4, 6, 9, 11, 13, 16, 18, 20, 23, 25, 27 and 30 January 2024 and 1, 3, 5, 7, 9, 12, 15, 17, 20, 22, 24, 27 and 29 February 2024 during the reporting quarter. The result of the reporting quarterly is presented in **Table 3.5**.

Seventy-eight (78) of the pre-operation phase water quality monitoring results of SS obtained had exceeded the Action Level. **Fifty-nine (59)** of the pre-operation phase water quality monitoring results of SS obtained during the reporting period had exceeded the Limit Level.

Investigation on the reason of exceedance has been carried out, where the exceedances of SS were concluded to be unrelated to the Contract as detailed in the Incident Reports on Action Level or Limit Level. Summary of the exceedance is presented in **Appendix E**.

Table 3.5 Summary of Impact Water Quality Monitoring Results

Location		Parameter																											
		Salinity (ppt)			Dissolved Oxygen (mg/L)						pH			Turbidity (NTU)			Suspended Solids (mg/L)			Temp. (°C)			TRC (mg/L)			Iron (mg/L)			
					Surface & Middle			Bottom																					
		Dec	Jan	Feb	Dec	Jan	Feb	Dec	Jan	Feb	Dec	Jan	Feb	Dec	Jan	Feb	Dec	Jan	Feb	Dec	Jan	Feb	Dec	Jan	Feb	Dec	Jan	Feb	
CE	Avg.	33.1	32.9	33.5	9.1	9.1	8.5	9.0	9.1	8.5	7.2	7.3	7.6	3.0	2.4	2.4	3.9	4.0	3.3	21.8	23.3	21.9	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
	Min.	32.1	32.2	32.6	7.4	8.5	7.7	7.4	8.4	7.7	6.6	7.1	7.2	2.2	1.7	2.0	3.0	2.5	2.5	21.0	21.7	20.1	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
	Max.	34.5	33.8	34.2	10.1	9.5	9.3	10.1	9.5	9.4	7.6	7.4	8.0	3.8	3.2	2.7	6.0	7.0	8.0	22.4	24.4	23.1	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
CF	Avg.	33.0	32.7	33.2	9.2	9.1	8.5	9.2	9.1	8.6	7.1	7.3	7.6	3.2	2.4	2.6	3.8	3.9	3.2	21.9	23.3	21.9	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
	Min.	32.3	31.8	32.7	7.9	8.7	7.8	7.8	8.7	7.8	6.6	7.1	7.1	2.5	1.8	2.1	2.5	2.5	2.5	20.9	21.9	20.1	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
	Max.	34.2	33.9	34.0	10.0	9.8	9.2	10.1	9.8	9.1	7.4	7.4	8.0	4.0	3.0	3.1	7.0	7.0	9.0	22.6	24.4	23.4	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
WSR1	Avg.	33.2	32.8	33.2	9.0	8.9	8.4	9.1	8.9	8.4	7.2	7.3	7.6	2.2	2.0	1.9	4.0	4.1	3.4	21.9	23.3	21.9	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
	Min.	32.3	31.4	32.4	7.8	8.3	7.9	7.9	8.2	7.9	6.6	7.1	7.1	1.7	1.5	1.4	2.5	2.5	2.5	21.2	21.6	20.1	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
	Max.	34.4	34.0	34.0	10.3	9.4	9.2	10.3	9.4	9.2	7.4	7.4	7.9	2.5	2.3	2.4	6.0	9.0	10.0	22.8	24.4	23.4	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
WSR2	Avg.	33.0	32.8	33.0	9.0	8.9	8.5	8.9	8.9	8.5	7.5	7.3	7.6	2.2	2.0	1.9	3.8	4.0	2.9	23.7	23.3	21.9	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
	Min.	32.1	31.7	32.3	7.7	8.4	7.5	7.6	8.4	7.6	6.7	7.1	7.2	1.4	1.5	1.3	2.5	2.5	2.5	21.1	21.7	20.0	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
	Max.	33.7	34.0	33.9	9.9	9.6	9.3	9.9	9.6	9.2	8.4	7.4	8.0	2.6	2.4	2.4	8.0	9.0	7.0	28.0	24.3	23.2	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
WSR3	Avg.	33.1	32.9	33.2	9.2	8.9	8.5	9.3	8.9	8.5	7.2	7.3	7.6	2.1	1.9	2.0	4.1	3.9	3.4	21.9	23.4	22.0	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
	Min.	32.5	31.9	32.3	7.8	8.4	7.9	7.9	8.4	7.9	6.7	7.1	7.1	1.2	1.5	1.6	2.5	2.5	2.5	21.1	22.0	20.0	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
	Max.	33.5	33.8	34.0	10.1	9.5	9.2	10.1	9.6	9.2	7.4	7.4	8.0	2.6	2.3	2.3	7.0	7.0	13.0	22.6	24.4	23.2	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
WSR4	Avg.	33.1	33.0	33.3	9.1	9.1	8.5	9.0	9.1	8.5	7.1	7.2	7.6	2.0	2.0	2.0	4.0	3.7	3.5	22.0	23.3	22.0	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
	Min.	32.4	31.7	32.2	7.3	8.4	7.5	7.3	8.4	7.5	6.6	7.1	7.1	1.2	1.5	1.5	2.5	2.5	2.5	21.2	21.8	20.0	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
	Max.	34.2	33.7	34.2	10.5	9.9	9.0	10.4	9.9	9.1	7.5	7.4	7.9	2.5	2.4	2.3	7.0	6.0	14.0	22.8	24.3	23.2	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
WSR16	Avg.	33.1	32.6	33.3	9.1	9.0	8.5	9.2	9.0	8.5	7.1	7.3	7.6	2.1	2.0	1.9	4.3	3.8	3.2	22.0	23.3	22.0	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
	Min.	32.3	31.6	32.7	8.4	8.0	7.9	8.4	8.0	7.9	6.6	7.1	7.2	1.1	1.6	1.1	2.5	2.5	2.5	21.1	21.8	20.3	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
	Max.	34.2	33.5	34.1	10.4	9.6	9.0	10.4	9.7	9.0	7.4	7.4	8.0	2.8	2.3	2.3	10.0	7.0	6.0	22.7	24.3	23.2	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
WSR33	Avg.	33.1	32.8	33.4	9.0	8.9	8.5	8.9	8.9	8.5	7.2	7.3	7.6	2.2	2.1	1.9	3.9	4.0	3.1	22.0	23.3	21.9	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
	Min.	32.3	32.0	32.2	8.2	8.4	7.4	8.2	8.4	7.5	6.8	7.2	7.1	1.9	1.7	1.3	2.5	2.5	2.5	21.2	21.8	20.1	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
	Max.	33.7	33.6	34.0	10.1	9.7	9.5	10.1	9.7	9.5	7.4	7.4	7.9	2.8	2.4	2.3	7.0	10.0	6.0	22.7	24.4	23.3	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
WSR36	Avg.	33.5	32.8	33.3	9.2	9.0	8.5	9.2	9.1	8.5	7.2	7.3	7.6	2.4	2.0	2.0	4.1	4.0	3.0	21.9	23.3	21.9	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
	Min.	32.7	31.7	32.7	8.2	8.3	7.6	8.2	8.3	7.6	6.7	7.1	7.1	2.1	1.5	1.3	2.5	2.5	2.5	21.1	21.6	20.1	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
	Max.	34.6	34.1	34.0	10.3	9.8	9.3	10.5	9.8	9.3	7.5	7.4	8.1	2.6	2.4	2.4	8.0	8.0	5.0	22.6	24.5	23.1	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
WSR37	Avg.	33.0	32.9	33.4	9.0	9.2	8.3	9.0	9.1	8.3	7.5	7.3	7.6	2.2	2.2	2.0	4.1	4.1	3.3	23.7	23.3	22.0	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
	Min.	31.8	32.1	32.4	7.5	8.4	7.6	7.5	8.5	7.6	6.7	7.1	7.1	1.8	1.6	1.5	2.5	2.5	2.5	21.1	21.5	20.2	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	
	Max.	33.8	33.6	34.2	10.3	9.9	9.0	10.2	9.9	9.1	8.4	7.4	8.0	2.5	2.4	2.4	9.0	9.0	7.0	28.0	24.6	23.3	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1	

Location		Parameter																										
		Salinity (ppt)			Dissolved Oxygen (mg/L)						pH			Turbidity (NTU)			Suspended Solids (mg/L)			Temp. (°C)			TRC (mg/L)			Iron (mg/L)		
					Surface & Middle			Bottom																				
		Dec	Jan	Feb	Dec	Jan	Feb	Dec	Jan	Feb	Dec	Jan	Feb	Dec	Jan	Feb	Dec	Jan	Feb	Dec	Jan	Feb	Dec	Jan	Feb	Dec	Jan	Feb
NF1	Avg.	33.1	33.1	33.2	9.0	9.0	8.3	9.0	9.0	8.3	7.2	7.2	7.6	2.2	1.9	2.0	4.1	3.7	3.4	21.9	23.3	21.9	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1
	Min.	32.5	32.3	32.5	8.2	8.2	7.9	8.2	8.2	7.8	6.7	7.1	7.1	1.6	1.5	1.5	2.5	2.5	2.5	20.9	21.8	20.2	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1
	Max..	33.6	34.3	34.2	9.8	9.6	8.9	10.1	9.6	8.9	7.4	7.5	8.0	2.5	2.4	2.4	8.0	6.0	9.0	22.8	24.4	23.1	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1
NF2	Avg.	32.9	33.0	33.3	9.0	8.7	8.3	9.0	8.7	8.3	7.1	7.3	7.6	2.0	1.9	2.0	4.0	3.9	3.1	21.8	23.3	21.9	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1
	Min.	32.3	32.1	32.3	7.4	8.4	7.4	7.4	8.4	7.4	6.5	7.1	7.1	1.3	1.7	1.5	2.5	2.5	2.5	20.9	21.6	19.9	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1
	Max..	33.5	33.8	33.9	10.1	9.2	9.1	10.1	9.2	9.0	7.4	7.5	7.9	2.6	2.2	2.4	7.0	7.0	7.0	22.6	24.4	23.2	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1
NF3	Avg.	33.0	32.9	33.0	9.0	8.9	8.4	8.8	8.9	8.4	7.2	7.2	7.6	2.1	2.0	2.0	4.1	3.7	3.4	21.9	23.3	21.9	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1
	Min.	32.3	31.8	32.3	7.6	8.3	7.6	7.6	8.3	7.5	6.6	7.1	7.1	1.3	1.5	1.4	2.5	2.5	2.5	20.9	21.7	20.0	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1
	Max..	34.0	33.6	33.9	10.1	9.6	9.6	10.0	9.4	9.6	7.5	7.4	8.0	2.6	2.3	2.4	8.0	8.0	7.0	22.8	24.3	23.1	<0.01	<0.01	<0.01	<0.1	<0.1	<0.1

Main Disinfection

Dechlorinated effluent monitoring at sampling locations (T1GKC01AA502/manhole 18) during discharge was carried out by AJCJV on 2 & 3 December 2023 for Total Residual Chlorine monitoring (TRC). **Seven (7)** of dechlorinated effluent sample were taken in T1GKC01AA502/manhole 18.

No TRC exceedance of action or limit levels was obtained during the discharge of dechlorinated effluent. The dechlorinated effluent monitoring is completed.

Monitoring results of TRC in this reporting month summarized in **Table 3.6**.

Table 3.6 Summary of dechlorinated effluent Monitoring Results

Location	Contact Tank / Product Water Tank flushing after neutralization						
Date	02 Dec 2023	03 Dec 2023	03 Dec 2023	03 Dec 2023	03 Dec 2023	03 Dec 2023	03 Dec 2023
Time	23:59	01:00	02:00	03:00	04:00	05:00	06:00
TRC (mg/L)	0.04	0.04	0.03	0.02	0.01	0.00	0.01

4. WASTE

The waste generated from this Project includes inert construction and demolition (C&D) materials, and non-inert C&D materials. Non-inert C&D materials are made up of general refuse, vegetative wastes, and recyclable wastes such as plastics and paper/cardboard packaging waste. Steel materials generated from the project are also grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials. With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting period are summarized in **Table 4.1**. Details of cumulative waste management data are presented as a waste flow table in **Appendix F**.

Table 4.1 Quantities of Waste Generated from the Project during reporting period

Reporting Months	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper / cardboard packaging	Plastics ⁽¹⁾	Chemical Waste	Others, e.g. general refuse
	(in ,000kg)	(in ,000kg)	(in ,000kg)	(in ,000kg)	(in ,000kg)	(in ,000kg)	(in ,000kg)	(in ,000kg)	(in ,000kg)	(in ,000kg)	(in ,000kg)
December 2023	215.229	0.000	0.000	0.000	215.220	0.000	0.000	0.000	0.000	0.000	79.680
January 2024	4978.345	0.000	0.000	4667.745	310.600	0.000	0.000	0.000	0.000	0.000	77.800
February 2024	*22448.146	0.000	0.000	21883.006	*565.14	0.000	0.000	0.000	0.000	0.000	*39.58

Notes: (1) Plastics refer to plastic bottles / containers, plastic sheets / foam from packaging material

(*) The record in EPD Transaction Records system was up to 22/02/2024, the data from 23/02 to 29/02 will be updated in next reporting period.

5. LANDFILL GAS MONITORING

5.1. MONITORING REQUIREMENT

In accordance with Section 11 of the EM&A Manual, monitoring of landfill gas is required for construction works within the 250m Consultation Zone. Part of the desalination plant and the indicative area of natural slope mitigation works fall within the SENT Landfill Extension Consultation Zone; and part of the 1,200 mm diameter fresh water mains along Wan Po Road falls within the SENT Landfill and SENT Landfill Extension Consultation Zones, TKO Stage II/III Restored Landfill and TKO Stage I Restored Landfill Consultation Zones.

5.2. MONITORING LOCATION

Monitoring of oxygen, methane, carbon dioxide and barometric pressure was performed for excavations at 1m depth or more within the consultation Zone.

During construction of works within the consultation zones, excavations of 1m depth or more was monitored:

- At the ground surface before excavation commences;
- Immediately before any worker enters the excavation;
- At the beginning of each working day for the entire period the excavation remains open; and
- Periodically through the working day whilst workers are in the excavation.

For excavations between 300mm and 1m deep, measurements should be carried out:

- Directly after the excavation has been completed; and
- Periodically whilst the excavation remains open.

5.3. MONITORING PARAMETERS

LFG monitoring was carried out to identify any migration between the landfill and the Project and to ensure the safety of the construction, operation and maintenance personnel working on-site, visitors and any other person within the Project area.

The following parameters were monitored:

- Methane.
- Oxygen.
- Carbon Dioxide.
- Barometric Pressure.

5.4. MONITORING LOCATION

The area required to be monitored for landfill gas in the reporting period is shown in **Figure 5.1**.

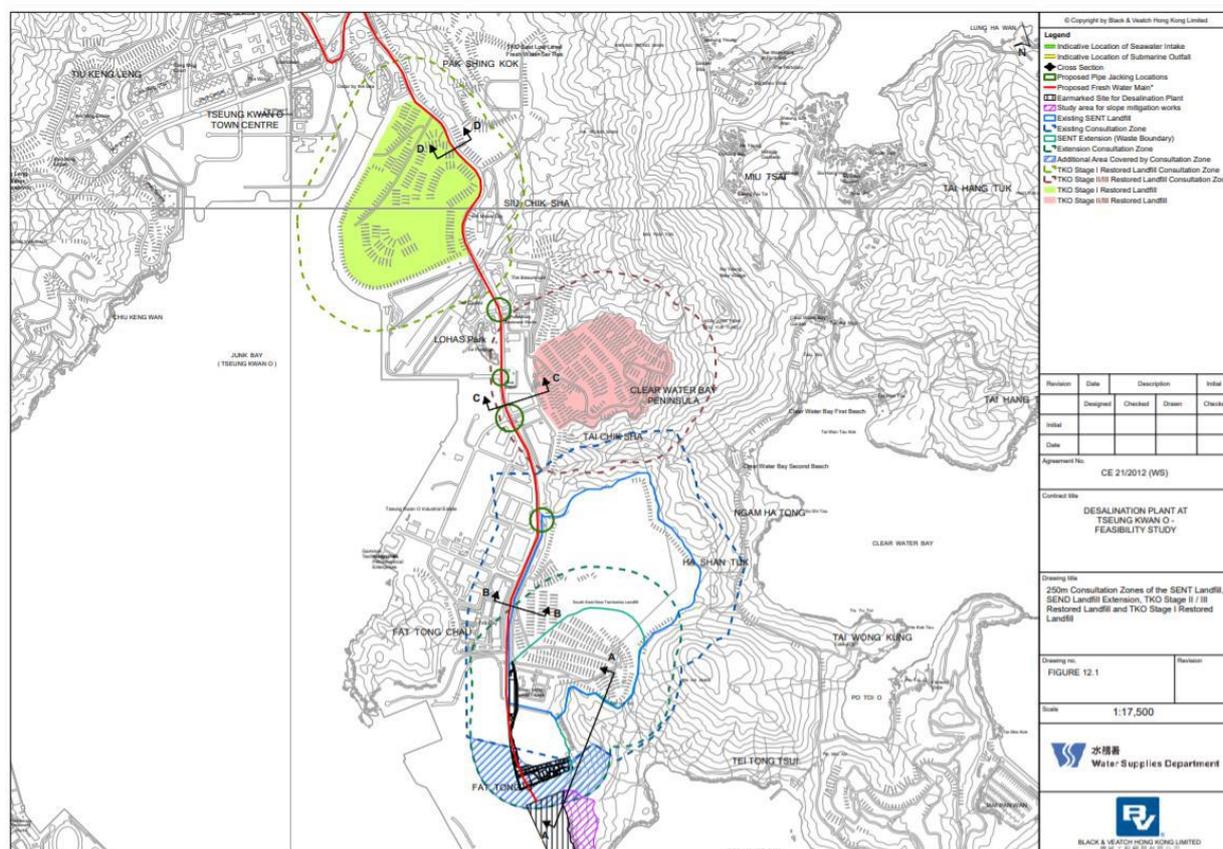


Figure 5.1 Overview of the SENT Extension Consultation Zone and the Project Site Area

5.5. ACTION AND LIMIT LEVEL

Action and Limit Level are provided in **Table 5.1**.

Table 5.1 Action and Limit Level for Landfill Gas Monitoring

Parameters	Action Level	Limit Level
Oxygen (O ₂)	<19% O ₂	<19% O ₂
Methane (CH ₄)	>10% LEL	>20% LEL
Carbon Dioxide (CO ₂)	>0.5% CO ₂	>1.5% CO ₂

5.6. MONITORING EQUIPMENT

The monitoring equipment used in the reporting period could be referring to Section 5.10 – 5.11 of the Monthly EM&A Report.

5.7. MONITORING RESULTS AND OBSERVATIONS

In this reporting period, **216 times** of landfill gas monitoring were recorded at Wan Po Road (Ch0+390 – Ch0+780) and (Ch0+400 - Ch1+200). No exceedance of action and limit levels for methane, oxygen and carbon dioxide was observed. Monitoring was conducted during

excavations at 1m depth or more within the consultation zone and whenever workers entered the excavation on the day. The Location Map for Landfill Gas Monitoring at TKO Area 137 are shown in **Figure 5.2** and **5.3**.

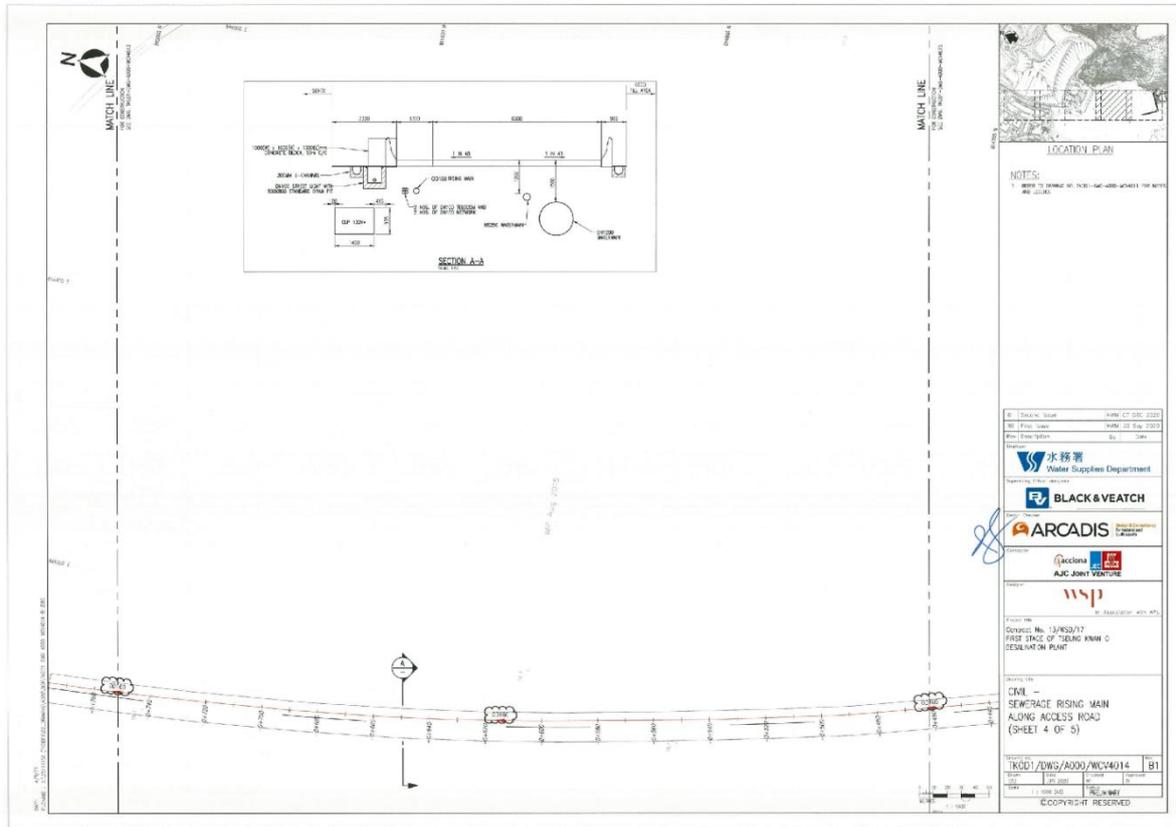


Figure 5.2 Location Map for Landfill Gas Monitoring at TKO Area 137 (-0+440 – -0+760)

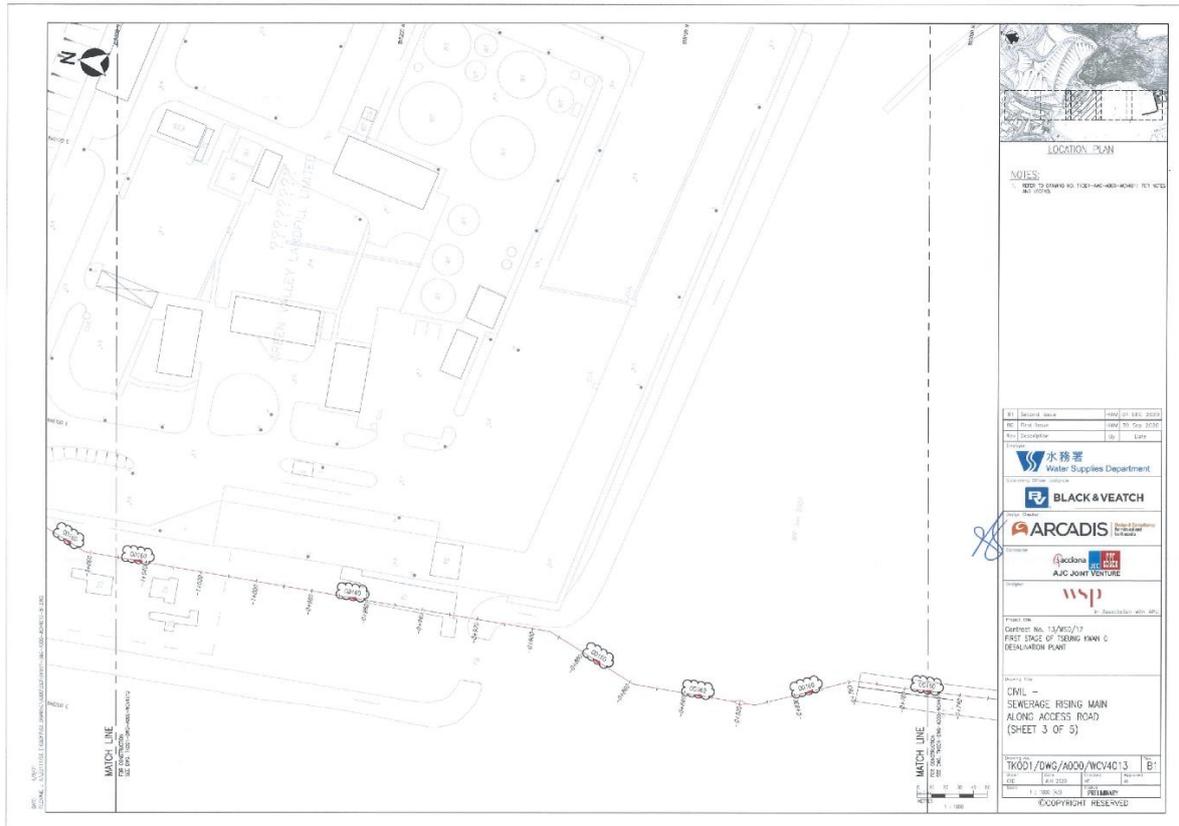


Figure 5.3 Location Map for Landfill Gas Monitoring at TKO Area 137 (-0+740 - -1+060)

6. SUMMARY OF EXCEEDANCE, COMPLAINT, NOTIFICATION OF SUMMONS AND PROSECUTIONS

The Environmental Complaint Handling Procedure is shown in below **Figure 6.1**:

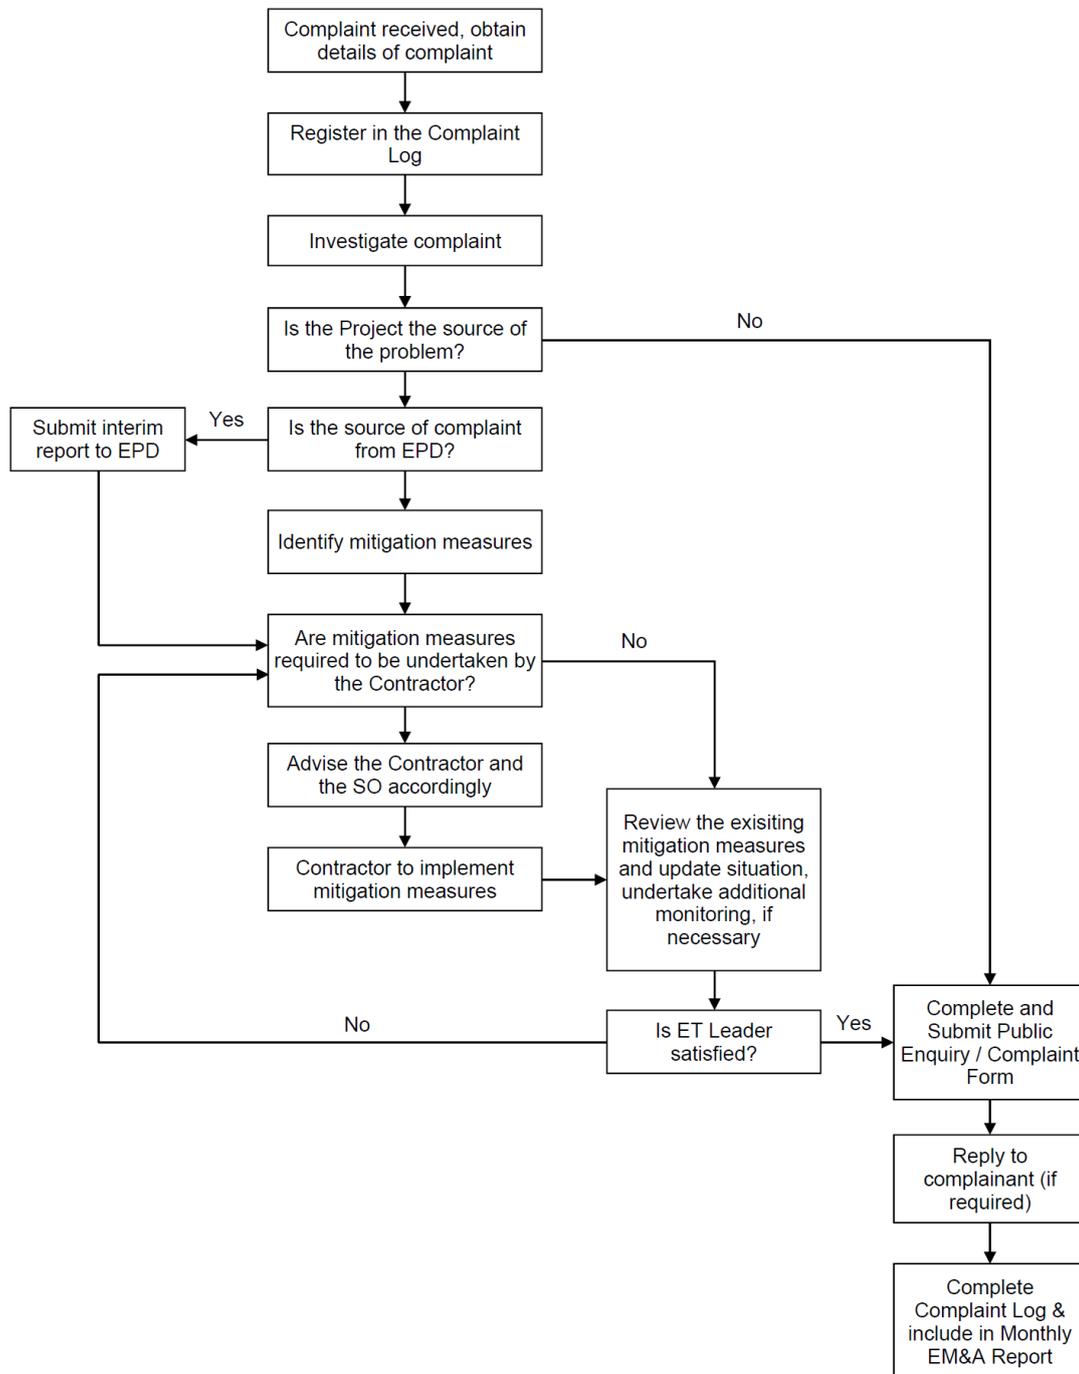


Figure 6.1 Environmental Complaint Handling Procedures

No noise monitoring was conducted during the reporting period since there are no Contract-related construction activities undertaken within a radius of 300m from the monitoring locations. No Action Level exceedance was recorded during the reporting period.

Referring to EM&A Manual, the general water quality monitoring should be carried out when there are marine-related construction activities undertaken. General water quality monitoring at the ten monitoring stations (CE, CF, WSR1, WSR2, WSR3, WSR4, WSR16, WSR33, WSR36 and WSR37) was ceased from 1 September 2023 due to the completion of marine-related construction works.

The EM&A works for pre-operation phase water quality were conducted during the reporting period in accordance with the EM&A Manual

Seventy-eight (78) of the pre-operation phase water quality monitoring results of SS obtained had exceeded the Action Level. **Fifty-nine (59)** of the pre-operation phase water quality monitoring results of SS obtained during the reporting period had exceeded the Limit Level. After investigation, all exceedances were considered non-project related.

Dechlorinated effluent monitoring at sampling locations (T1GKC01AA502/manhole 18) during discharge was carried out by AJCJV on 2 & 3 December 2023 for Total Residual Chlorine monitoring (TRC). **Seven (7)** of dechlorinated effluent sample were taken in T1GKC01AA502/manhole 18. No TRC exceedance was recorded in the reporting period. The dechlorinated effluent monitoring is completed.

In this reporting period, **216 times** of landfill gas monitoring were recorded at Wan Po Road (Ch0+390 – Ch0+780) and (Ch0+400 - Ch1+200). No exceedance of action and limit levels for methane, oxygen and carbon dioxide was observed. Monitoring was conducted during excavations at 1m depth or more within the consultation zone and whenever workers entered the excavation on the day.

Pre-operation phase monthly coral monitoring was conducted during the reporting period on **28 December 2023, 30 January 2024 and 23 February 2024**. No sediment, bleaching or increased mortality in the general condition of all other tagged coral colonies were observed during the monthly operation phase monitoring period. No deterioration of the coral community was observed in the ecological monitoring results when compared with the baseline ecological monitoring results. There is no AL/LL exceedance during the monitoring period.

Pre-operation phase fishery monitoring for dry season was carried out on **17 and 24 February 2024**. The result of the monitoring would be present when it is available.

ET will keep closely monitoring the performance of Contractor, implementation of water quality mitigation measure and other contamination issue around the Project site, to ensure the EM&A requirement is properly implemented.

One (1) environmental complaint was received in the reporting period. No notification of summons and prosecution was received in the reporting period. The details of the complaint could be referred to Appendix J of the Monthly EM&A Report for Jan 24

Statistics on complaints and regulatory compliance are summarized in **Appendix G**.

7. EM&A SITE INSPECTION

Site inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures under the Contract.

ET weekly site inspections were carried out by ET on 5, 12, 19 and 27 December 2023, 2, 9, 16, 25 and 29 January 2024 and 7, 16, 20 and 28 February 2024.

Joint site inspections were also carried out by ET and IEC on 12 and 27 December 2023, 09, 16, 25 and 29 January 2024, and 7, 16, 20 and 28 February 2024.

Minor deficiencies were observed during weekly site inspection. Key observations during the site inspections are summarized below:

- A chemical container found near RO Building without a drip tray, the contractors are reminded to provide a drip tray or proper storage for the chemical containers.

The Contractor has rectified the observations identified during environmental site inspections in the reporting period.

According to the EIA Study Report, Environmental Permit, contract documents and EM&A Manual, the mitigation measures detailed in the documents should be implemented as much as practical during the reporting period. An updated Implementation Status of Environmental Mitigation Measures (EMIS) is provided in **Appendix C**.

8. CONCLUSIONS AND RECOMMENDATIONS

This is the 16th Quarterly EM&A Report for the Project which summarizes the key findings of the EM&A programme during the reporting period from 1 December 2023 to 29 February 2024, in accordance with the EM&A Manual and the requirement under FEP-01/503/2015/A.

No noise monitoring was conducted in the reporting period due to the over distant monitoring station from the works location.

Referring to EM&A Manual, the general water quality monitoring should be carried out when there are marine-related construction activities undertaken. General water quality monitoring at the ten monitoring stations (CE, CF, WSR1, WSR2, WSR3, WSR4, WSR16, WSR33, WSR36 and WSR37) was ceased from 1 September 2023 due to the completion of marine-related construction works.

The EM&A works for pre-operation phase water quality were conducted during the reporting period in accordance with the EM&A Manual [Seventy-eight \(78\)](#) of the pre-operation phase water quality monitoring results of SS obtained had exceeded the Action Level. [Fifty-nine \(59\)](#) of the pre-operation phase water quality monitoring results of SS obtained during the reporting period had exceeded the Limit Level. After investigation, all exceedances were considered non-project related.

Dechlorinated effluent monitoring at sampling locations (T1GKC01AA502/manhole 18) during discharge was carried out by AJCJV on 2 & 3 December 2023 for Total Residual Chlorine monitoring (TRC). [Seven \(7\)](#) of dechlorinated effluent sample were taken in T1GKC01AA502/manhole 18. No TRC exceedance was recorded in the reporting period. The dechlorinated effluent monitoring is completed.

In this reporting period, [216 times](#) of landfill gas monitoring were recorded at Wan Po Road (Ch0+390 – Ch0+780) and (Ch0+400 - Ch1+200). No exceedance of action and limit levels for methane, oxygen and carbon dioxide was observed. Monitoring was conducted during excavations at 1m depth or more within the consultation zone and whenever workers entered the excavation on the day.

Pre-operation phase monthly coral monitoring was conducted during the reporting period on [28 December 2023, 30 January 2024 and 23 February 2024](#). No sediment, bleaching or increased mortality in the general condition of all other tagged coral colonies were observed during the monthly operation phase monitoring period. No deterioration of the coral community was observed in the ecological monitoring results when compared with the baseline ecological monitoring results. There is no AL/LL exceedance during the monitoring period.

Pre-operation phase fishery monitoring for dry season was carried out on [17 and 24 February 2024](#). The result is of the monitoring would be present when it is available.

Weekly environmental site inspection was conducted during the reporting period. Minor deficiency was observed during site inspection and was rectified. The environmental performance of the project was therefore considered satisfactory.

According to the environmental site inspections performed in the reporting period, the Contractor is reminded to pay attention on maintaining proper materials storage.


Two (2) [environmental complaint](#) was received of the Contract since commencement of the Contract. No notification of summons or prosecution was received of the Contract since commencement of the Contract quarter.

The ET will keep track on the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures.

Appendix A

Master Programme

Activity ID	Activity Name	Baseline Duration	Baseline Start	Baseline Finish	Remaining Duration	Actual / Planned Start	Actual / Planned Finish	Actual % Complete	Variance Finish Date	Total Float	2020												2021												2022												2023												2024											
											N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	J	Jul	A	S	O
Project Programme (Level 2) Updated as at 31 Jan 2024																																																																						
Key Dates																																																																						
Commencement and Completion Date																																																																						
KD0000100	Letter of Acceptance	0	15-Nov-19		0	15-Nov-19 A		100%	0		◆ Letter of Acceptance																																																											
KD0000110	Commencement of the Works	0	30-Dec-19		0	30-Dec-19 A		100%	0		◆ Commencement of the Works																																																											
KD0000120	Completion of the Works (1170 Days)	0		13-Mar-23	0		13-Mar-23 A	100%	0		◆ Completion of the Works (1170 Days)																																																											
KD0000130	Revised Completion of the Works (324 Days EOT Granted)	0			0	14-Mar-23 A	31-Jan-24 A	100%			◆ Revised Completion of the Works																																																											
KD0000510	Planned Completion of the Works	0			0		10-Aug-24	0%	-192		◆ Planned Completion of the Works																																																											
KD0000520	Target Completion of the Works (Best Endeavour)	0			0		19-Dec-23 A	100%			◆ Target Completion of the Works																																																											
Executive Summaries																																																																						
Preliminary Setup																																																																						
ES0001000	Mobilization and Preliminary Set Up	191	30-Dec-19	07-Jul-20	0	30-Dec-19 A	20-Jul-20 A	100%	-13		Mobilization and Preliminary Set Up																																																											
Civil Design AIP and DDA																																																																						
ES0001010	AIP Civil Design Submission and Approval	330	30-Dec-19	23-Nov-20	0	30-Dec-19 A	31-Aug-20 A	100%	84		AIP Civil Design Submission and Approval																																																											
ES0001020	DDA Civil Design Submission and Approval	414	28-Feb-20	16-Apr-21	0	22-Jan-20 A	01-Sep-21 A	100%	-138		DDA Civil Design Submission and Approval																																																											
M&E Design AIP and DDA																																																																						
ES0002000	M&E AIP Process Mechanical Submission and Approval	477	30-Dec-19	19-Apr-21	0	30-Dec-19 A	22-Dec-20 A	100%	118		M&E AIP Process Mechanical Submission and Approval																																																											
ES0002010	M&E DDA Process Mechanical Submission and Approval	679	08-Feb-20	17-Dec-21	0	21-Jul-20 A	02-Sep-21 A	100%	106		M&E DDA Process Mechanical Submission and Approval																																																											
ES0002020	M&E AIP Instrumentation & Control Submission and Approval	607	31-Jan-20	28-Sep-21	0	04-Feb-20 A	25-Feb-20 A	100%	581		M&E AIP Instrumentation & Control Submission and Approval																																																											
ES0002030	M&E DDA Instrumentation & Control Submission and Approval	514	22-Jul-20	17-Dec-21	0	13-Feb-21 A	14-Apr-23 A	100%	-483		M&E DDA Instrumentation & Control Submission and Approval																																																											
ES0002050	M&E DDA Electrical and Renewable Energy Submission and Approval	382	16-Aug-20	01-Sep-21	0	17-Aug-20 A	31-Dec-20 A	100%	244		M&E DDA Electrical and Renewable Energy Submission and Approval																																																											
ES0002060	M&E AIP Building Services Submission and Approval	226	30-Dec-19	11-Aug-20	0	30-Dec-19 A	30-Oct-20 A	100%	-80		M&E AIP Building Services Submission and Approval																																																											
ES0002065	M&E Design Basis & Civil Guidance Dwg	112	30-Dec-19	19-Apr-20	0	30-Dec-19 A	24-Jul-20 A	100%	-96		M&E Design Basis & Civil Guidance Dwg																																																											
ES0002070	M&E DDA Building Services Submission and Approval	306	28-Feb-20	29-Dec-20	0	01-Mar-20 A	30-Jun-21 A	100%	-183		M&E DDA Building Services Submission and Approval																																																											
ES0002085	M&E AIP Site Electrical Submission and Approval	155	09-Jun-20	10-Nov-20	0	21-Mar-20 A	22-Jul-20 A	100%	111		M&E AIP Site Electrical Submission and Approval																																																											
ES0002090	M&E DDA Lift Submission and Approval	140	27-Aug-20	13-Jan-21	0	01-Oct-20 A	12-May-21 A	100%	-119		M&E DDA Lift Submission and Approval																																																											
ES0002095	M&E DDA Site Electrical Submission and Approval	140	11-Nov-20	30-Mar-21	0	23-Jul-20 A	04-Jun-21 A	100%	-66		M&E DDA Site Electrical Submission and Approval																																																											
ES0002100	M&E DDA T&C Design Submission and Approval	155	29-Mar-22	30-Aug-22	0	01-Aug-21 A	05-Oct-23 A	100%	-401		M&E DDA T&C Design Submission and Approval																																																											
Procurement of Major Plant & Equipment Schedule																																																																						
ES0002320	M&E Procurement of Major Plant, Equipment, Material and Delivery	901	14-Mar-20	31-Aug-22	0	04-Feb-20 A	16-Jan-23 A	100%	-138		M&E Procurement of Major Plant, Equipment, Material and Delivery																																																											
ES2420	M&E Procurement of Mechanical Equipment - Intake Pumps	595	18-May-20	02-Jan-22	0	04-Feb-20 A	11-May-22 A	100%	-129		M&E Procurement of Mechanical Equipment - Intake Pumps																																																											
ES2430	M&E Procurement of Mechanical Equipment - ActiDAFF Underdrain	333	30-Oct-20	27-Sep-21	0	02-Aug-20 A	14-Mar-22 A	100%	-168		M&E Procurement of Mechanical Equipment - ActiDAFF Underdrain																																																											
ES2440	M&E Procurement of Mechanical Equipment - ActiDAFF Media	298	15-Mar-21	06-Jan-22	0	23-Jul-20 A	14-Oct-22 A	100%	-281		M&E Procurement of Mechanical Equipment - ActiDAFF Media																																																											
ES2450	M&E Procurement of Mechanical Equipment - RO and ERD Rack	274	22-Feb-21	22-Nov-21	0	22-Jul-20 A	28-Dec-21 A	100%	-36		M&E Procurement of Mechanical Equipment - RO and ERD Rack																																																											
ES2460	M&E Procurement of Mechanical Equipment - RO Membrane	755	29-Mar-20	22-Apr-22	0	12-Feb-20 A	28-Dec-22 A	100%	-250		M&E Procurement of Mechanical Equipment - RO Membrane																																																											
ES2470	M&E Procurement of Electrical Equipment - CLP Substation for LV Switchboard / Genset / Building Services	300	14-Mar-20	07-Jan-21	0	14-Mar-20 A	28-Feb-21 A	100%	-52		M&E Procurement of Electrical Equipment - CLP Substation for LV Switchboard / Genset / Building Services																																																											
132kV Substation																																																																						
ES0001460	Excavation and Formation Works for 132kV Substation	15	16-Mar-20	30-Mar-20	0	19-Feb-20 A	23-Apr-20 A	100%	-24		Excavation and Formation Works for 132kV Substation																																																											
ES0001470	Construction of 132kV Substation	233	31-Mar-20	18-Nov-20	0	27-Apr-20 A	30-Dec-20 A	100%	-42		Construction of 132kV Substation																																																											

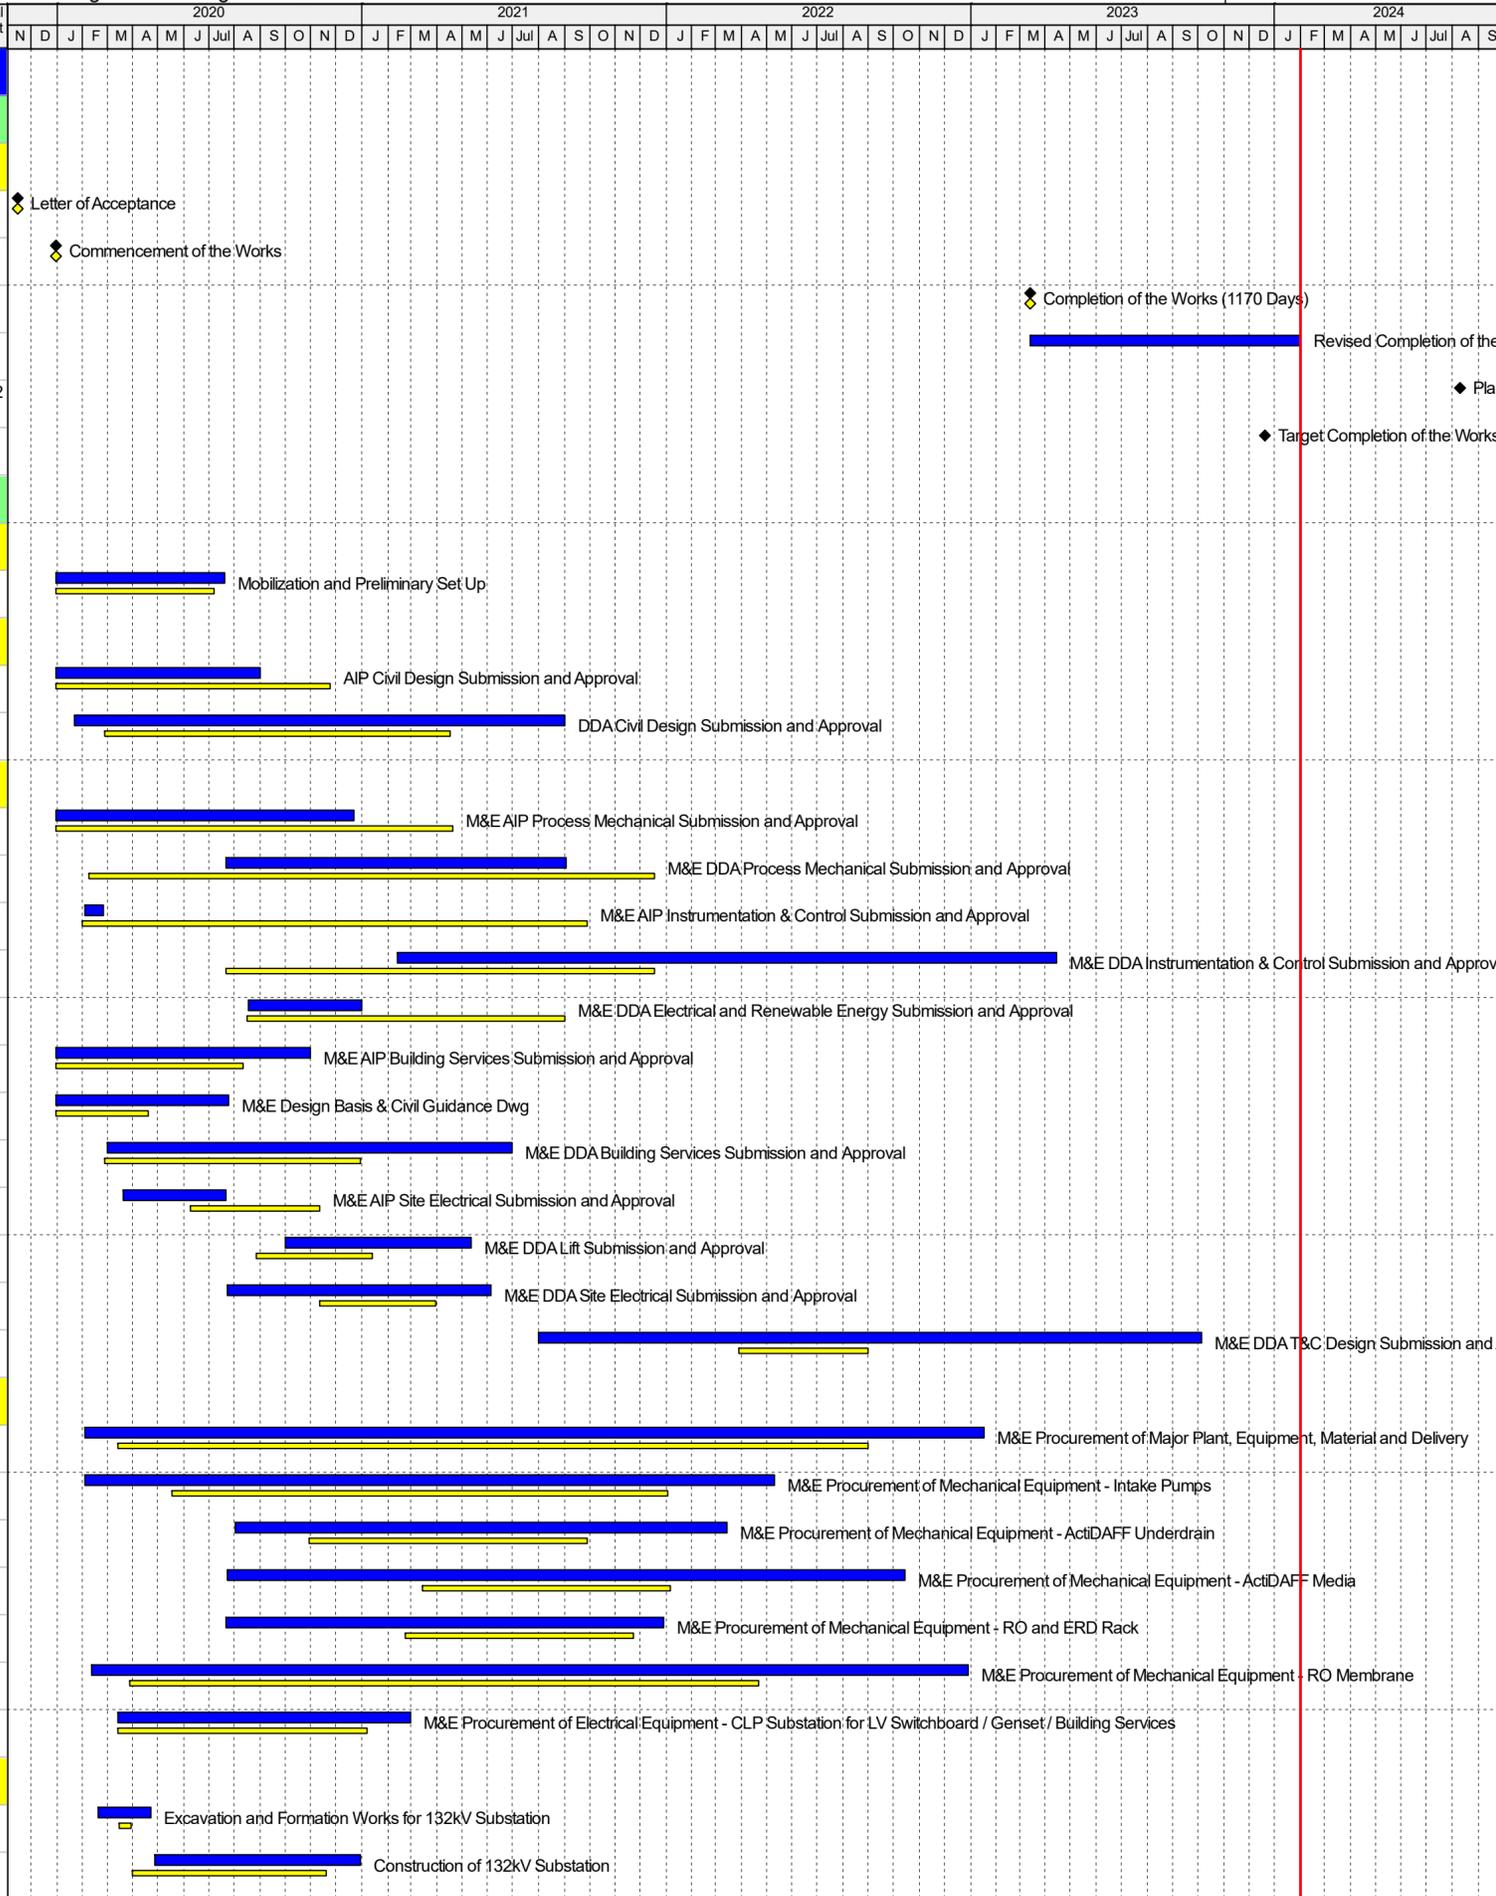

Appendix B


Overview of Desalination Plant in Tseung Kwan O

LEGEND:

- BOUNDARY OF SENT LANDFILL EXTENSION
- BOUNDARY OF WORKS AREA FOR TKO DESALINATION PLANT
- SITE PHASING
- ALLOCATED LAND BOUNDARIES

NOTE:

TEMPORARY WORKS AREA 1 WILL BE HANDED OVER AT +6 MPD WITH A TOLERANCE OF ±500mm.

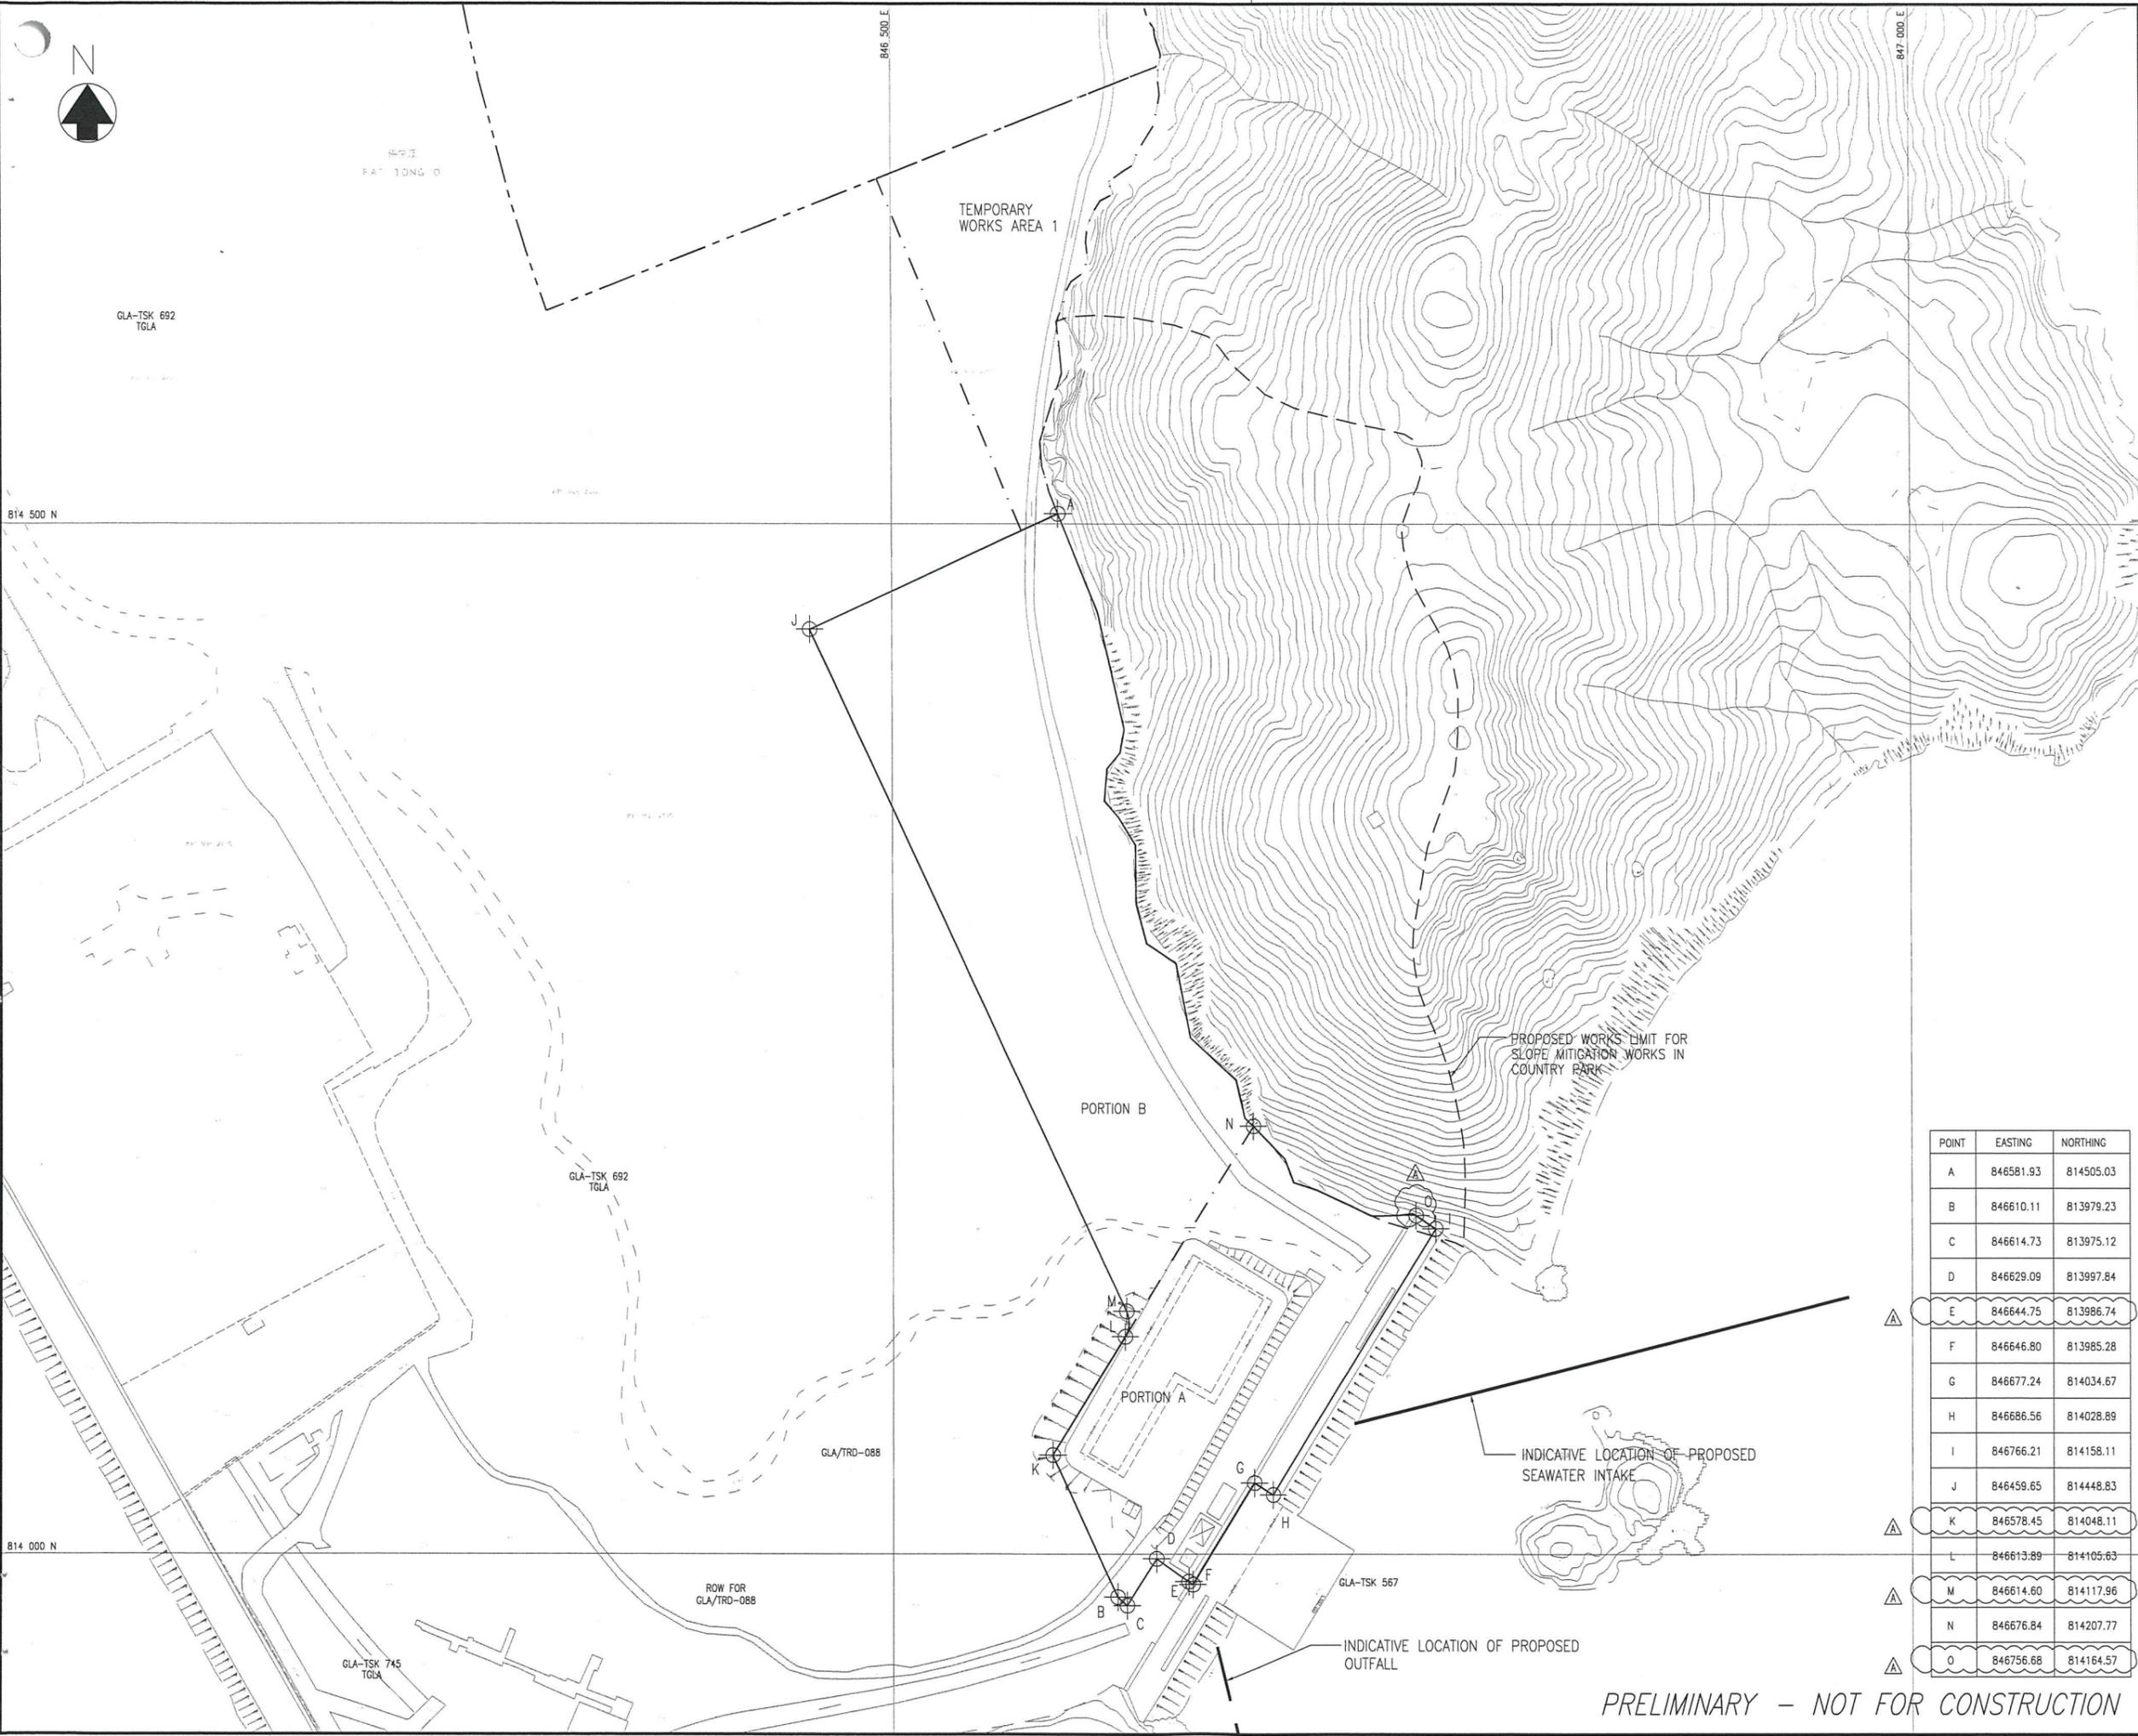

B	10/03	UPDATE NOTES	YLC
A	07/18	UPDATE COORDINATES	YLC
Revision	Date	Description	Initial
	Designed	Checked	Drawn
Initial	YLC	CKH	SZ
Date	02/18	02/18	02/18

Approved
Christina Go

Agreement No. CE 8/2015 (WS)

Contract No. 13/WSD/17

Contract Title
DESIGN, BUILD AND OPERATE FIRST STAGE OF TSEUNG KWAN O DESALINATION PLANT

Drawing Title
SITE HANDOVER WORKS AREAS

Drawing No.	Revision
190495/K/TEND/10/0003	B

Scale A1 1 : 1500
A3 1 : 3000



BLACK & VEATCH HONG KONG LIMITED
博威工程顧問有限公司

POINT	EASTING	NORTHING
A	846581.93	814505.03
B	846610.11	813979.23
C	846614.73	813975.12
D	846629.09	813997.84
E	846644.75	813986.74
F	846646.80	813985.28
G	846677.24	814034.67
H	846686.56	814028.89
I	846766.21	814158.11
J	846459.65	814448.83
K	846578.45	814048.11
L	846613.89	814105.63
M	846614.60	814117.96
N	846676.84	814207.77
O	846756.68	814164.57

PRELIMINARY - NOT FOR CONSTRUCTION

BUILDINGS IN FIRST STAGE

CODE	NAME OF BUILDING	TOTAL G.F.A. (m ²)	SITE COVERAGE (m ²)
B	COMBINE SHAFT	759,876	759,876
C	ACTIDAFF	10027,547	5455,346
G	REVERSE OSMOSIS BUILDING AND ELECTRICAL BUILDING	4511,455	5367,935
H	CO2 TANKS AREA	-	-
J	PRODUCT WATER STORAGE TANK, PUMP STATION AND ELECTRICAL BUILDING	1974,610	2933,980
K	SLUDGE TREATMENT BUILDING, TANK AND PUMP ROOM	2531,044	1228,361
M	ADMINISTRATION BUILDING & ELECTRICAL BUILDING C	2450,713	1114,062
N	MAIN ELECTRICAL AND CENTRAL CHILLER PLANT BUILDING	-	499,893
R1	ELECTROCHLORINATION BUILDING & ELECTRICAL BUILDING A	657,992	825,776
S	132 KV SUBSTATION	-	943,560
T	IRRIGATION WATER TANK AND PUMP ROOM	-	156,148
R2	CHEMICAL BUILDING	813,056	813,056
V	VISITOR GALLERY	1330,410	1330,410
X1	GUARD HOUSE AND FS CONTROL ROOM	39,585	39,585
X2	GUARD HOUSE	22,035	22,035
Y	R + D OUTDOOR	-	-
Z	WASTE WATER TREATMENT PLANT	48,000	48,000
TOTAL =		25175,323	21490,023

LEGEND / ABBREVIATION


- H.L. WINDOW HIGH LEVEL WINDOW
- M.L. METAL LOUVRES
- C.L. CAT LADDER
- A.U.T. ACCESSIBLE UNISEX TOILET
- ⊕ PROPOSED FINISH FLOOR LEVEL IN METER ABOVE P.D.
- ⊖ STRUCTURAL FLOOR LEVEL IN METER ABOVE P.D.
- M.V.I.A.L. MECHANICAL VENTILATION & ARTIFICIAL LIGHTING
- F.E. 4.5kg CO₂ FIRE EXTINGUISHER
- H.R. HOSE REEL
- ⊙ FIREMANS LIFT
- ⊕ LIFT FOR THE BARRIER FREE ACCESS
- P.D. PIPE DUCT

PLOT RATIO & SITE COVERAGE CALCULATION:

SITE AREA OF THE FIRST STAGE	=	56108 m ²
TOTAL G.F.A.	=	25092.141 m ²
TOTAL SITE COVERAGE	=	21414.841 m ²
PLOT RATIO	=	25092.141 / 56108
	=	0.447 < PERMITTED
SITE COVERAGE	=	21414.841 / 56108 x 100
	=	38.167%


SITE LOCATION PLAN

1 : 5000

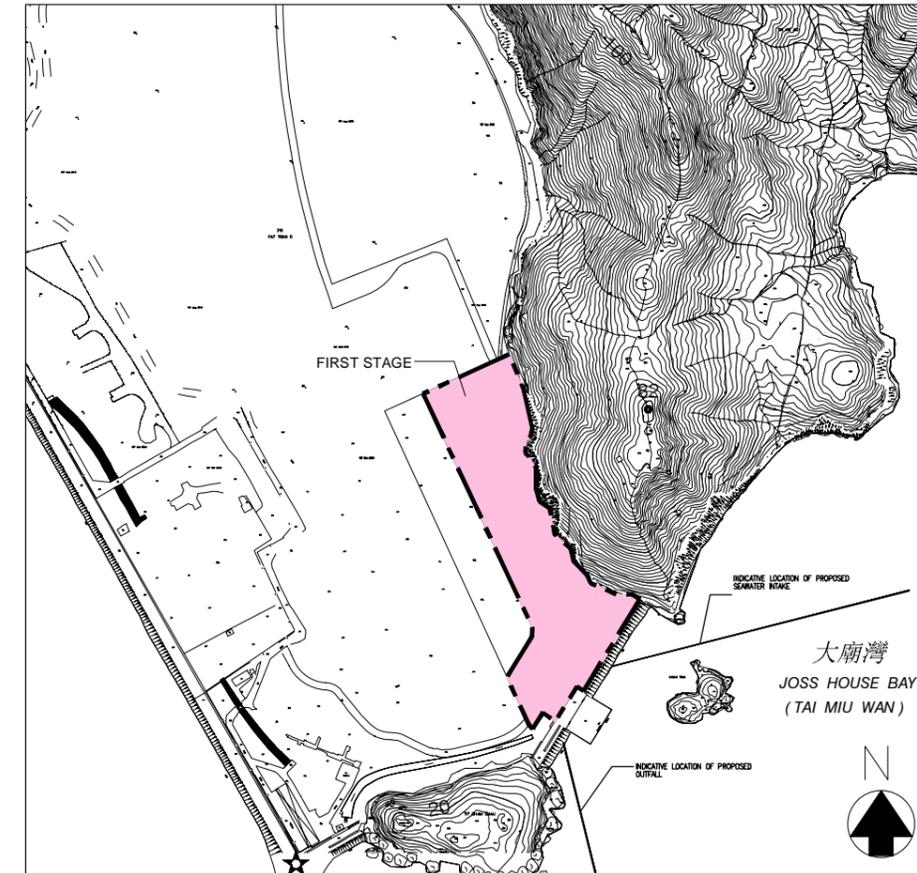

FIRST STAGE OF TSEUNG KWAN O DESALINATION PLANT

1 : 1000

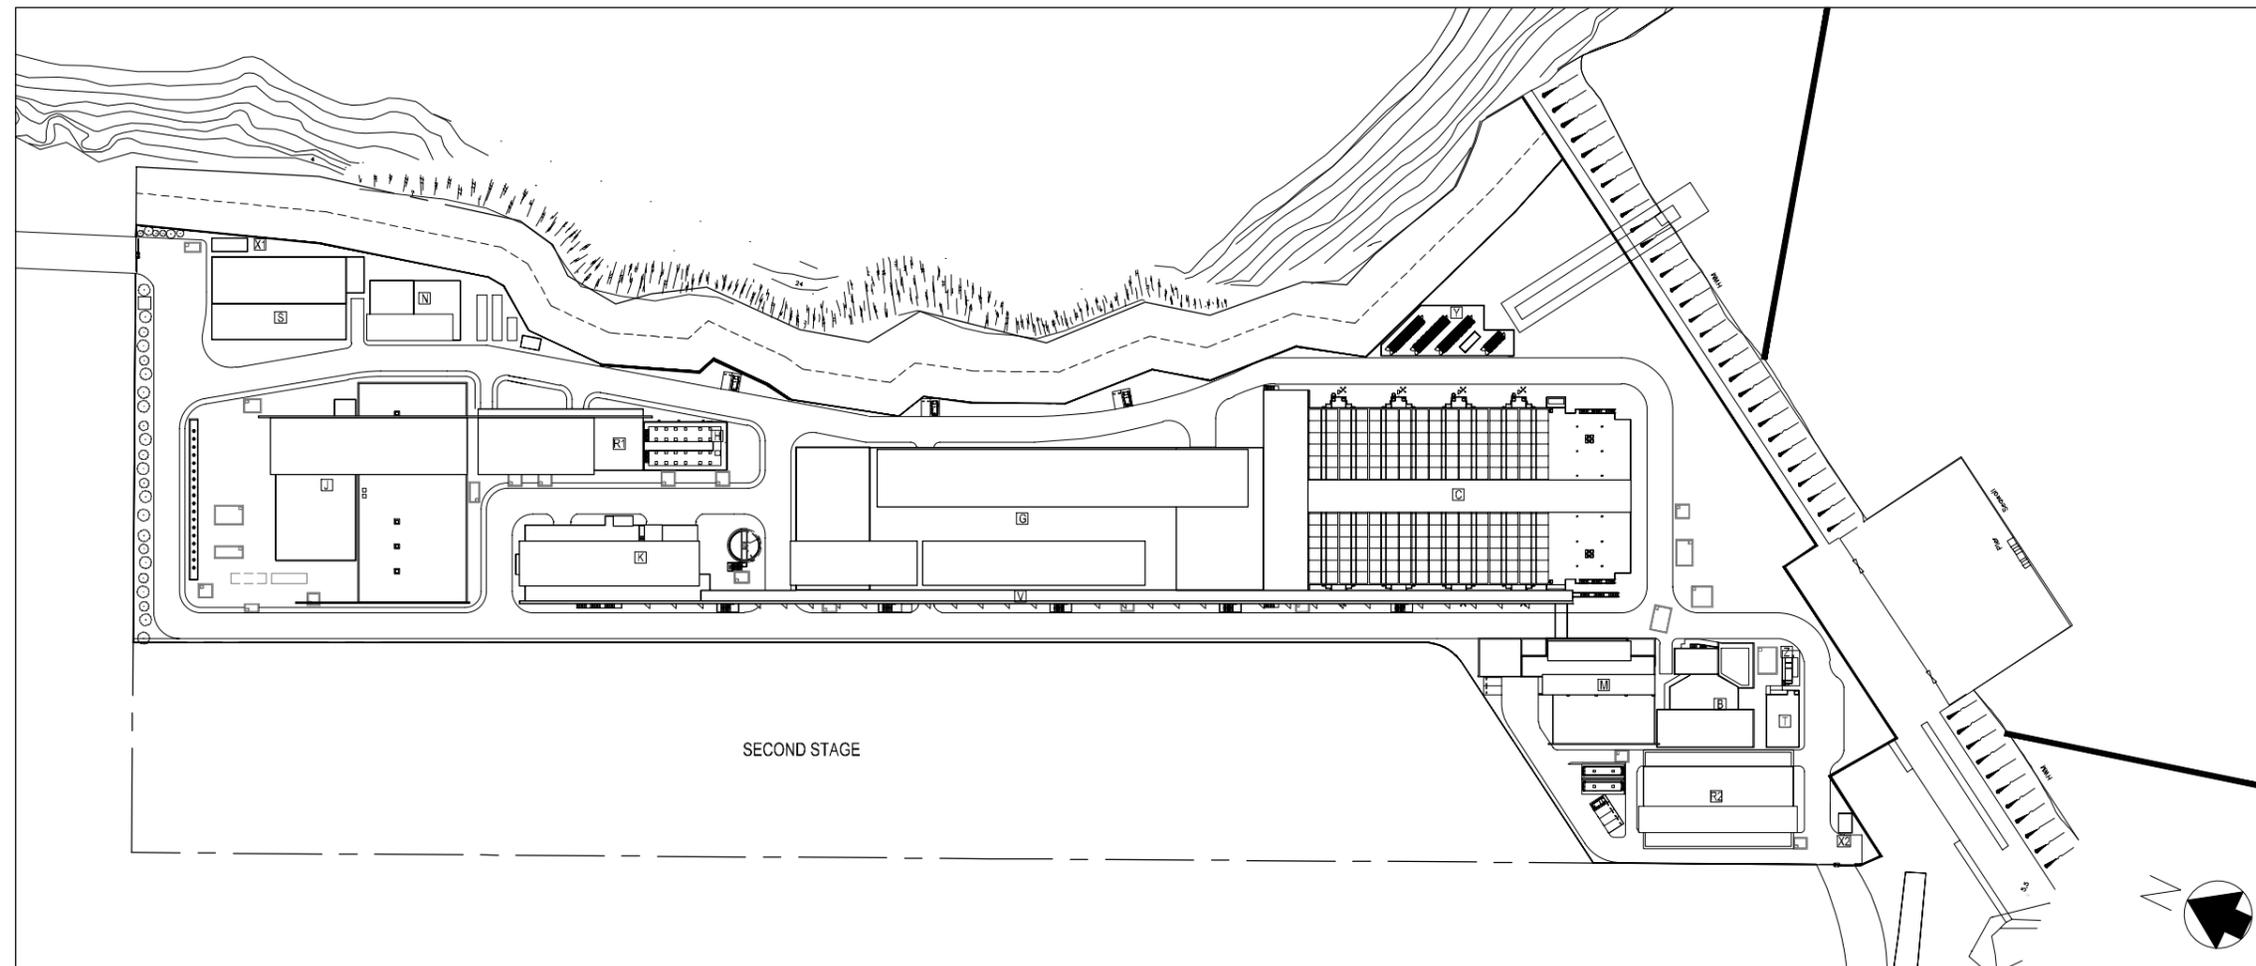

0	TENDER SUBMISSION	CAD	JAN 19
Rev	Description	By	Date
Employer			
Employer's Consultant			
Tenderer			
Designer			
Project title			
CONTRACT NO. 13/WSD/17			
DESIGN, BUILD AND OPERATE FIRST STAGE OF TSEUNG KWAN O DESALINATION PLANT			
Drawing title			
ARCHITECTURAL – PLOT RATIO AND SITE COVERAGE CALCULATION, LEGEND ABBREVIATION			
Drawing no.		Rev.	
TKO/AJC/W/A000/AR/001		0	
Drawn	Date	Checked	Approved
OKAL	JAN 19	S.C.	T.C.
Scale	N.T.S.	Status	-

Appendix C

Summary of Implementation Status of Environmental Mitigation

EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
Air Quality								
S4.8.1	Impervious dust screen or sheeting will be provided to enclose scaffolding from the ground floor level of building for construction of superstructure of the new buildings.	Land site/ During Construction	Contractor(s)		✓		Implemented	Air Pollution Control (Construction Dust)
S4.8.1	Impervious sheet will be provided for skip hoist for material transport.	Land site/ During Construction	Contractor(s)		✓		NA	-
S4.8.1	The area where dusty work takes place should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after dusty activities as far as practicable.	Land site/ During Construction	Contractor(s)		✓		Implemented	-
S4.8.1	All dusty materials should be sprayed with water or a dust suppression chemical immediately prior to any loading, unloading or transfer operation.	Land site/ During Construction	Contractor(s)		✓		Implemented	-
S4.8.1	Dropping heights for excavated materials should be controlled to a practical height to minimize the fugitive dust arising from unloading.	Land site/ During Construction	Contractor(s)		✓		Implemented	-
S4.8.1	During transportation by truck, materials should not be loaded to a level higher than the side and tail boards and should be dampened or covered before transport.	Land site/ During Construction	Contractor(s)		✓		Implemented	-
S4.8.1	Wheel washing device should be provided at the exits of the work sites. Immediately before leaving a construction site, every vehicle shall be washed to remove any dusty material from its body and wheels as far as practicable.	Land site/ During Construction	Contractor(s)		✓		Implemented	-
S4.8.1	Road sections between vehicle-wash areas and vehicular entrance will be paved.	Land site/ During Construction	Contractor(s)		✓		Implemented	-
S4.8.1	Hoarding of not less than 2.4m high from ground level will be provided along the length of the Project Site boundary.	Land site/ During construction	Contractor(s)	✓	✓		N/A	-
S4.8.1	Haul roads will be kept clear of dusty materials and will be sprayed with water so as to maintain the entire road surface wet at all times.	Land site/ During construction	Contractor(s)		✓		Implemented after reminder	-
S4.8.1	Temporary stockpiles of dusty materials will be either covered entirely by impervious sheets or sprayed with water to maintain the entire surface wet all the time.	Land site/ During construction	Contractor(s)		✓		Implemented after reminder	-

EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S4.8.1	Stockpiles of more than 20 bags of cement, dry pulverized fuel ash and dusty construction materials will be covered entirely by impervious sheeting sheltered on top and 3-sides.	Land site/ During construction	Contractor(s)		✓		N/A	-
S4.8.1	All exposed areas will be kept wet always to minimize dust emission.	Land site/ During construction	Contractor(s)		✓		Implemented after reminder	-
S4.8.1	Ultra-low-Sulphur diesel (ULSD) will be used for all construction plant on-site, as defined as diesel fuel containing not more than 0.005% Sulphur by weight) as stipulated in Environment, Transport and Works Bureau Technical Circular (ETWB-TC(W)) No 19/2005 on Environmental Management on Construction Sites.	Land site/ During construction/ During Operation	Contractor(s)		✓	✓	Implemented	Environment, Transport and Works Bureau Technical Circular (ETWB-TC(W)) No 19/2005 on Environmental Management on Construction Sites
S4.8.1	The engine of the construction equipment during idling will be switched off.	Land site/ During construction	Contractor(s)		✓		Implemented	-
S4.8.1	Concrete batching plant will be required on site. control measures recommended in the Guidance Note on a Best Practicable Means for Cement Works (Concrete Batching Plant) (BPM 3/2 (93)) will be implemented. The control measures recommended in the Guidance Note on a Best Practicable Means for Cement Works (Concrete Batching Plant) (BPM 3/2 (93)) will be implemented.	Land site/ During construction	Contractor(s)		✓		N/A	-
S4.8.1	Regular maintenance of construction equipment deployed on-site will be conducted to prevent black smoke emission.	Land site/ During construction	Contractor(s)		✓		Implemented	-
S4.10	To ensure proper implementation of the recommended dust mitigation measures and good construction site practices during the construction phase, environmental site audits on weekly basis is recommended throughout the construction period.	Land site/ During construction	Contractor(s)/ Environmental Team (ET) & Independent Environmental Checker (IEC)		✓		Implemented	-
Noise								
S5.7	Only well-maintained plant will be operated on-site, and plant will be serviced regularly during the construction phase.	All area/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works A Practical Guide for the Reduction of Noise from Construction Works

EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S5.7	Silencers or mufflers on construction equipment will be utilized and will be properly maintained during the construction phase.	Noise control/ During construction	Contractor(s)		✓		N/A	-
S5.7	Mobile plant, if any, will be sited as far away from NSRs as possible.	Noise control/ During construction	Contractor(s)		✓		N/A	-
S5.7	Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum.	Noise control/ During construction	Contractor(s)		✓		Implemented	-
S5.7	Plants known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.	Noise control/ During construction	Contractor(s)		✓		N/A	-
S5.7	Material stockpiles and other structures will be effectively utilized, wherever practicable, in screening noise from on-site construction activities.	Noise control/ During construction	Contractor(s)		✓		N/A	-
S5.7	Use of Quiet Powered Mechanical Equipment (QPME).	Noise control/ During construction	Contractor(s)		✓		Implemented	-
S5.7	Movable noise barriers of 3m in height with skid footing should be used and located within a few meters of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater than its height. The noise barrier material should have a superficial surface density of at least 7 kg m ⁻² and have no or gappeningss.	Noise control/ During construction	Contractor(s)		✓		N/A	-
S5.7	The noise insulating sheet should be deployed such that there would be no opening or gaps on the joints.	Noise control/ During construction	Contractor(s)		✓		N/A	-
S5.7	Construction activities (e.g., excavation/shoring, reinstatement (asphalt), and pipe jacking) will be planned and carried out in sequence, such that items of PME proposed for these activities will not be operated simultaneously.	Noise control/ During construction	Contractor(s)	✓	✓		Implemented	-
S5.7	PMEs will not be used at the works areas near educational institutions with residual impact (i.e., the "influence area" within a radius of 40m) during school hours in order to reduce impact to the educational institutions.	Noise control / During construction	Contractor(s)		✓		N/A	-

EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S5.7	Noise enclosures or acoustic sheds would be used to cover stationary PME such as generators. Portable/Movable noise enclosure made of material with superficial surface density of at least 7 kg m-2 may be used for screening the noise from operation of the saw/groover, concrete.	Noise control/ Pre-construction/ During construction	Contractor(s)	✓	✓		N/A	-
5.9	Sawcutting pavement, breaking up of pavement, excavation /shoring, pipe laying, backfilling, reinstatement (concrete) and pipe jacking shall be scheduled outside the examination period.	Noise control/ Pre-construction/ During construction	Contractor(s)	✓	✓		N/A	-
S5.9	In view the duration of noise exceedance at Creative Secondary School, PLK Laws Foundation College, TKO Kei Tak Primary School and School of Continuing and Professional Studies-CUHK is limited to 8 weeks, the construction work in the influence areas near the four schools shall be scheduled during long school holidays (eg summer holiday, Easter holiday or Christmas holiday, etc) as far as practicable. Scheduling the construction work for the four schools.	Noise control/ Pre-construction/ During construction	Contractor(s)	✓	✓		N/A	-
S5.10	A noise monitoring programme shall be implemented for the construction phase.	Designated monitoring stations as defined in EM&A Manual/During construction phase	Environmental Team		✓		N/A	-
S5.10	The effectiveness of on-site control measures could also be evaluated through the regular site audits.	All facilities/ During construction	Contractor(s)/ ET & IEC		✓		Implemented	-
Water Quality								
S6.9	Dredged marine sediment will be disposed of in a gazette marine disposal area in accordance with marine dumping permit conditions of the Dumping at Sea Ordinance (DASO).	Marine Dredging/ During construction	Contractor(s)		✓		Implemented	Dumping at Sea Ordinance (DASO)
S6.9	Disposal vessels will be fitted with tight bottom seals in order to prevent leakage of material during transport.	Marine Dredging/ During construction	Contractor(s)		✓		Implemented	-
S6.9	Barges will be filled to a level, which ensures that material does not spill over during transport to the disposal site and that adequate freeboard is maintained to ensure that the decks are not washed by wave action.	Marine Dredging/ During construction	Contractor(s)		✓		Implemented	-
S6.9	After dredging, any excess materials will be cleaned from decks and exposed fittings before the vessel is moved from the dredging area.	Marine Dredging/ During construction	Contractor(s)		✓		Implemented	-

EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S6.9	All vessels should be well maintained and inspected before use to limit any potential discharges to the marine environment.	Marine Dredging/ During construction	Contractor(s)		✓		Implemented	-
S6.9	All vessels must have a clean ballast system.	Marine Dredging/ During construction	Contractor(s)		✓		Implemented	-
S6.9	No discharge of sewage/grey wastewater should be allowed. Wastewater from potentially contaminated area on working vessels should be minimized and collected. These kinds of wastewater should be brought back to port and discharged at appropriate collection and treatment system.	Marine Dredging/ During construction	Contractor(s)		✓		Implemented	
S6.9	No soil waste is allowed to be disposed overboard.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	
S6.9	Silt removal facilities such as silt traps or sedimentation facilities will be provided to remove silt particles from runoff to meet the requirements of the TM standard under the WPCO. The design of silt removal facilities will be based on the guidelines provided in ProPECC PN 1/94. All drainage facilities and erosion and sediment control structures will be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit will be removed regularly.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented	ProPECC PN 1/94 TM Standard under the WPCO
S6.9	Earthworks to form the final surfaces will be followed up with surface protection and drainage works to prevent erosion caused by rainstorms.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented	-
S6.9	Appropriate surface drainage will be designed and provided where necessary.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented	-
S6.9	The precautions to be taken at any time of year when rainstorms are likely together with the actions to be taken when a rainstorm is imminent or forecasted and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94.	Land site & drainage/ During construction	Contractor(s)	✓	✓		Implemented	ProPECC PN 1/94
S6.9	Oil interceptors will be provided in the drainage system where necessary and regularly emptied to prevent the release of oil and grease into the storm water drainage system after accidental spillages.	Land site & drainage/ During construction	Contractor(s)		✓		N/A	-

EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S6.9	Temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge, if any, will be adequately designed for the controlled release of storm flows.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented	-
S6.9	The temporary diverted drainage, if any, will be reinstated to the original condition when the construction work has finished or when the temporary diversion is no longer required.	Land site & drainage/ During construction	Contractor(s)		✓		N/A	-
S6.9	Appropriate numbers of portable toilets shall be provided by a licensed contractor to serve the construction workers over the construction site to prevent direct disposal of sewage into the water environment.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented	-
S6.9 and S6.12	The sterilization water should be dechlorinated with total residual chlorine (TRC) level below 1 mg/L before discharge to public sewer. In situ testing of TRC should also be conducted for the discharge of chlorinated water for pipeline disinfection to ensure sufficient dechlorination before discharge to public sewer.	Sterilization of water mains prior to commissioning	Contractor(s)		✓	✓	N/A	Technical Memorandum for Effluents Discharged into Drainage and Sewerage Systems Inland and Coastal Waters
S6.9	The cleaning and flushing water should also be treated and desilted to the relevant discharge requirement stipulated in TM-DSS before discharging.	Sterilization of water mains prior to commissioning	Contractor(s)		✓	✓	Implemented	
S6.9	Site drainage should be well maintained, and good construction practices should be observed to ensure that oil, fuels, solvents and other chemicals are managed, stored and handled properly and do not enter the nearby water streams.	Land site & drainage/ During construction/ During operation	Contractor(s)		✓	✓	Implemented after reminder	-
S6.12	Regular site inspections will be carried out in order to confirm that regulatory requirements are being met and that contractors are implementing the standard site practice and mitigation measures as proposed to reduce potential impacts to water quality.	During construction	Contractor(s)/ ET & IEC		✓		Implemented	-
Waste Management								
S8.5	Nomination of approved personnel to be responsible for standard site practices, arrangements for collection and effective disposal to an appropriate facility of all wastes generated at the site.	Contract mobilization/ During construction	Contractor(s)		✓		Implemented	-

EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S8.5	Training of site personnel in proper waste management and chemical handling procedures. Training will be provided to workers on the concepts of site cleanliness and appropriate waste management procedures, including waste reduction, reuse and recycling at the beginning of the construction works.	Contract mobilization/ During construction	Contractor(s)		✓		Implemented	-
S8.5	Provision of sufficient waste disposal points and regular collection for disposal.	All area/ During construction/ During operation	Contractor(s)		✓	✓	Implemented	DEVB TC(W) No. 8/2010, Enhanced Specification for Site Cleanliness and Tidiness.
S8.5	Appropriate measures to reduce windblown litter and dust transportation of waste by either covering trucks or by transporting wastes in enclosed containers.	All area/ During construction	Contractor(s)		✓		Implemented	
S8.5	A waste management plan (WMP) as stated in the "ETWB TC(W) No. 19/2005, Environmental Management on Construction Sites" for the amount of waste generated, recycled and disposed of (including the disposal sites) will be established and implemented during the construction phase as part of the Environmental Management Plan (EMP). The Contractor will be required to prepare the EMP and submits it to the Architect/ Engineer under the Contract for approval prior to implementation.	All area/ During construction	Contractor(s)		✓		Implemented	ETWB TC(W) No. 19/2005, Environmental Management on Construction Sites
S8.5	Separation of chemical wastes for special handling and appropriate treatment at the Chemical Waste Treatment Centre at Tsing Yi.	All area/ During construction	Contractor(s)		✓		Implemented	Chapters 2 & 3 Code of Practice on the Packaging, Labelling & Storage of Chemical Wastes published under the Waste Disposal Ordinance (Cap 354),
S8.5	Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors.	Land site/ During construction	Contractor(s)		✓		Implemented	Waste Disposal Ordinance (Cap 354)
S8.5	A recording system for the amount of waste generated/ recycled and disposal sites. The trip- ticket system will be included as one of the contractual requirements and implemented by the contractor(s).	Land site/ During construction	Contractor(s)		✓		Implemented	DEVB TC(W) No. 6/2010, Trip Ticket System for Disposal of Construction &
S8.5	Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of material and their proper disposal.	Land site/ During construction/ During operation	Contractor(s)		✓		Implemented	WBTC 32/92, The Use of Tropical Hard Wood on Construction Site

EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S8.5	Encourage collection of aluminium cans and wastepaper by individual collectors during construction with separate labelled bins provided to segregate these wastes from other general refuse by the workforce.	Land site/ During construction	Contractor(s)		✓		Implemented	ETWB TCW No. 33/2002, Management of Construction and
S8.5	Any unused chemicals and those with remaining functional capacity will be recycled as far as possible.	Land site/ During construction	Contractor(s)		✓		N/A	-
S8.5	Use of reusable non-timber formwork to reduce the amount of C&D materials.	All areas/ During construction	Contractor(s)		✓		Implemented	WBTC 32/92, The Use of Tropical Hard Wood on Construction Site
S8.5	Prior to disposal of construction waste, wood, steel and other metals will be separated to the extent practical, for re-use and/or recycling to reduce the quantity of waste to be disposed of to landfill.	All areas/ During construction	Contractor(s)		✓		Implemented	DEVB TC(W) No. 6/2010, Trip Ticket System for Disposal of Construction & Demolition Materials
S8.5	Proper storage and site practices to reduce the potential for damage or contamination of construction materials.	All areas/ During construction	Contractor(s)		✓		Implemented	-
S8.5	Plan and stock construction materials carefully to reduce amount of waste generated and avoid unnecessary generation of waste.	All areas/ During construction	Contractor(s)		✓		Implemented	-
S8.5	A Sediment Quality Report (SQR) for sampling and chemical testing of the sediment will be prepared and submitted to the EPD for approval. The approved detailed sampling and chemical testing will be carried out prior to the commencement of the dredging activities to confirm the sediment disposal method.	Marine works/ During construction	Contractor(s)		✓		N/A	ETWB TC(W) No. 34/2002 and Dumping at Sea Ordinance (DASO)
S8.5	The management of dredged/ excavated sediment management requirement from ETWB TC(W) No. 34/2002 will be incorporated in the Specification of the Contract Documents.	Marine works/ During construction	WSD/ Contractor(s)		✓		Implemented	ETWB TC(W) No. 34/2002 and Dumping at Sea Ordinance (DASO)
S8.5	The contractor will open a billing account with EPD in accordance with the Waste Disposal (Charges for Disposal of Construction Waste) Regulation for the payment of disposal charges.	Contract mobilization/ During construction	Contractor(s)		✓		Implemented	Cap 354N Waste Disposal (Charges for Disposal of Construction Waste) Regulation
S8.5	A trip-ticket system will be established in accordance with DEVB TC(W) No. 6/2010 to monitor the reuse of surplus excavated materials off-site and disposal of construction waste and general refuse at transfer facilities/ landfills, and to control fly-tipping.	Contract mobilization/ During construction	Contractor(s)		✓		Implemented	DEVB TC(W) No. 6/2010, Trip Ticket System for Disposal of Construction & Demolition Materials

EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S8.5	The project proponent will also conduct regular inspection of the waste management measures implemented on site as described in the Waste Management Plan.	All area/ During construction	Contractor(s)/ Environmental Team (ET) & Independent Environmental Checker (IEC)		✓		Implemented	ETWB TC(W) No. 19/2005, Environmental Management on Construction Sites
S8.5	A recording system (similar to summary table as shown in Annex 5 and Annex 6 of Appendix G of ETWB TC(W) No. 19/2005) for the amount of waste generated, recycled and disposed of (including the disposal sites) will be established during the construction phase.	All area/ During construction	Contractor(s)		✓		Implemented	Annex 5 and Annex 6 of Appendix G of ETWB TC(W) No. 19/2005
S8.5	Inert C&D materials (public fill) will be reused within the Project as far as practicable.	All area/ During construction	Contractor(s)		✓		Implemented	-
S8.5	Public fill and construction waste shall be segregated and stored in different containers or skips to facilitate reuse or recycling of materials and their proper disposal.	All area/ During construction	Contractor(s)		✓		Implemented	-
S8.5	Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable.	All area/ During construction	Contractor(s)		✓		Implemented	-
S8.5	To reduce the potential dust and water quality impacts of site formation works, C&D materials will be wetted as quickly as possible to the extent practice after filling.	All area/ During construction	Contractor(s)		✓		Implemented	Air Pollution Control (Construction Dust) Regulation (Cap 311R); WPCO (Cap 358)
S8.5	Open stockpiles of excavated/ fill materials or construction wastes on-site should be covered with tarpaulin or similar fabric.	Land site/ During Construction, particularly dry season	Contractor(s)		✓		Implemented	Air Pollution Control (Construction Dust) Regulation (Cap 311R)
S8.5	Chemical waste container shall be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Chemical waste container shall have a capacity of less than 450 L unless the specifications have been approved by the EPD.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	
S8.5	A label in English and Chinese shall be displayed on the chemical container in accordance with instructions prescribed in Schedule 2 of the Regulations.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	

EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S8.5	Storage areas for chemical waste shall be enclosed on at least 3 sides.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	
S8.5	Storage areas for chemical waste shall have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	
S8.5	Storage areas for chemical waste shall have adequate ventilation.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	
S8.5	Storage areas for chemical waste shall be covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary).	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	
S8.5	Storage areas for chemical waste shall be arranged so that incompatible materials are appropriately separated.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	
S8.5	General refuse will be stored in enclosed bins or compaction units separately from construction and chemical wastes.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented after reminder	
S8.5	Adequate number of waste containers will be provided to avoid over-spillage of waste.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	DEVB TC(W) No. 8/2010 Enhanced Specification for Site Cleanliness and Tidiness.
S8.5	A reputable waste collector will be employed by the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily basis to minimise odour, pest and litter impacts.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented after reminder	-
S8.5	Recycling bins will be provided at strategic locations within the Site to facilitate recovery of recyclable materials (including aluminum can, waste paper, glass bottles and plastic bottles) from the Site. Materials recovered will be sold for recycling.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	-
S8.5	To avoid any odour and litter impact, accurate number of portable toilets will be provided for workers on-site.	All area/ During construction	Contractor(s)		✓		Implemented	-
S8.5	The burning of refuse on construction sites is prohibited by law.	All area/ During construction	Contractor(s)		✓		Implemented	Air Pollution Control Ordinance (Cap 311)

EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S8.7	To facilitate monitoring and control over the contractors' performance on waste management, a waste inspection and audit programme will be implemented throughout the construction phase.	All facilities/ During construction	ET/ IEC		✓		Implemented	-
Ecology								
S9.7	For slope mitigation works within the Clear Water Bay Country Park, to avoid tree felling and damages to trees, the exact locations of the flexible barrier foundation plates, soil nails and rock dowels can be adjusted during detailed design, and a setback distance from existing trees is recommended to be maintained as far as practical. A detailed specification describing the exact locations of the flexible barrier foundation plates, soil nails and rock dowels will be prepared to illustrate how the setback distance from existing trees would be implemented for tree avoidance.	Slope mitigation works area/ During detailed design/ During construction	Contractor(s)	✓	✓		Implemented	-
S9.7	Pruning of tree canopies along the alignment of the flexible barriers shall be limited to a minimum.	Slope mitigation works area/ During construction	Contractor(s)		✓		Implemented	-
S9.7	The alignment of flexible barriers shall be optimized to preserve all species of conservation interest and minimize the impact to the existing vegetation as far as practicable. All individuals of Marsdenia lachnostoma within the slope mitigation areas shall be retained in- situ, by positioning the alignment of flexible barrier at a minimum 1.5m in a radius away from these individuals.	Slope mitigation works area/ During detailed design/ During construction	Contractor(s)	✓	✓		Implemented	-
S9.7 and 9.10	At the detailed design stage prior to the commencement of the slope mitigation works, a vegetation survey shall be carried out at the slope mitigation areas within the Clear Water Bay Country Park to assess the condition and identify the location of each individual of Marsdenia lachnostoma and other flora species of conservation interest that may be directly affected by the construction works.	Slope mitigation works area/ During detailed design/ During construction	Contractor(s)	✓			Implemented	-
S9.7	Temporary fencing will be installed to fence off the concerned species either in groups of individually within the works area and in the close proximity to prevent from being damaged and disturbed during construction. A sign identifying the site shall be attached to the fence and flagging tape shall be attached to the individuals to visualize their locations.	Slope mitigation works area/ During construction	Contractor(s)		✓		Implemented	-

EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S9.7 and S9.10	A specification for fencing and demarcating individuals of Marsdenai lachnostoma (or other flora species of conservation interest, if found) adjacent to the proposed alignment of the flexible barriers will be prepared to protect the species.	Slope mitigation works area/ During construction	Contractor(s)		✓		Implemented	-
S9.7	Induction training shall also be provided to all site personnel in order to brief them on this flora of conservation interest including the locations and their importance.	Slope mitigation works area/ During construction	Contractor(s)		✓		Implemented	-
S9.7	The resident site supervisory staff will closely monitor the conditions of concerned individuals during construction of flexible barriers in the close proximity.	Slope mitigation works area/ During construction	Contractor(s)		✓		Implemented	-
S9.7	Erect fences along the boundary of the works area before the commencement of works to prevent vehicle movements and encroachment of personnel onto adjacent areas.	All area/ During construction	Contractor(s)		✓		Implemented	-
S9.7	Regularly check the work site boundaries to ensure that they are not breached and that damage does not occur to surrounding areas.	All area/ During construction	Contractor(s)/ ET		✓		Implemented after reminder	-
S9.7	Avoid any damage and disturbance, particularly those caused by filling and illegal dumping, to the surrounding habitats through proper management of waste disposal.	All area/ During construction	Contractor(s)		✓		Implemented	-
S9.7	Reinstate temporarily affected areas, particularly the habitats of plantation and shrubland-grassland immediately after completion of construction works, through on-site tree/shrub planting. The tree/shrub species will be chosen with reference to those in the surrounding area.	All area/ During construction	Contractor(s)		✓		To be Implemented	-
S9.7	Affected habitats within the Clear Water Bay Country Bay shall be reinstated by hydro-seeding and planting of climbers and native shrub seedlings where practical upon completion of the slope mitigation works.	All area/ During construction	Contractor(s)		✓		To be Implemented	-
Landscape & Visual								
S11.10 & 11.11	The construction area and area allowed for temporary structures, such as the contractor's office, will be minimized to a practical minimum. (MM1)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	-
S11.10 & 11.11	At the detailed design stage, the design team will seek to minimize the landscape footprint of the Project and above ground facilities, while satisfying all other requirements. (MM2)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	-

EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S11.10 & 11.11	Design principles will be adopted to take into account the surrounding area, particularly Clear Water Bay Country Park behind and the nearby waterfront, with due consideration given to: - green roofs where practical (i.e. without equipment on the roof); - roadside planting; - aesthetic treatment of all structures; - vertical greening; - screen planting along application site; and - landscape enhancement with amenity planting where practical including planting along the edge (site boundary) fence with native shrubs where feasible, to reduce their visual impact and blend them into the surrounding landscape. (MM3)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	--
S11.10 & 11.11	All trees within the Project Site or the potential slope mitigation works area will be carefully protected during construction according to DEVB TCW No. 10/2013 - Tree Preservation (MM4)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented after reminder	ETWB TCW No. 3/2006 - Tree Preservation.
S11.10 & 11.11	No tree within the Country Park will be felled. Trees within the Site unavoidably affected by the works will be transplanted where necessary and practical. For trees that need to be felled, compensatory planting will be provided to the satisfaction of relevant Government departments. A compensatory tree planting proposal including locations of tree compensation will be submitted to seek relevant government department's approval, in accordance with DEVB TC(W) No. 10/2013. (MM5)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	DEVB TC(W) No. 10/2013
S11.10 & 11.11	Any slope mitigation works necessary to address natural terrain hazards, will be minimized to minimize any potential environmental impact to the Country Park e.g. soil nailing and rock stabilization will aim to avoid existing trees e.g. should any restoration of vegetation be necessary, the best planting matrix with native species will be established, with the aim of resembling the existing vegetation. (MM6)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	N/A	-

EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S11.10 & 11.11	Dredging works for the installation of intake structures and outfall diffusers should be minimized to avoid or reduce any potential environmental impacts to as low as reasonably practicable (ALARP). The intake and outfall structures (e.g. intake openings and diffuser heads) will be prefabricated and transferred to site for installation. (MM7)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	-
S11.10 & 11.11	All night-time lighting will be reduced to a practical minimum both in terms of number of level and will be hooded and directional. (MM8) units and lux level and will be hooded and directional. (MM8)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	-
Landfill Gas Hazard								
S12.7	During all works, safety procedures should be implemented to minimise the risks of fires and explosions, asphyxiation of workers and toxicity effects resulting from contact with contaminated soil and groundwater.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	-
S12.7	During trenching and excavation as well as creation of confined spaces at near to or below ground level, precautions should be clearly laid down and rigidly Gas detection equipment and appropriate breathing apparatus should be available and used when entering confined spaces or trenches deeper than 1 meter.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	-
S12.7	The Contractor should make the workers are aware of potential hazards of working in confined spaces (any chamber, manhole or culvert which is large enough to permit access to personnel). Such work in confined spaces is controlled by the Factories and Industrial Undertakings (Confined Spaces) Regulations of the Factories and Industrial Undertakings Ordinance. Following the Safety Guide to Working in Confined Spaces ensures compliance with the above regulations.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	-
S12.7	Safety officers, specifically trained with regard to landfill gas and leachate related hazards and the appropriate actions to take in adverse circumstances, should be present on the site throughout the works, in particular, when works are undertaken below grade.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	-
S12.7	All personnel who work on site and all visitors to the site should be made aware of the possibility of ignition of gas in the vicinity of the works, the possible presence of contaminated water and the need to avoid physical contact with it.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	-

EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S12.7	Monitoring for landfill gas should be undertaken in all excavations, manholes, chambers (particularly during pipe jacking) and any confined spaces through the use of an intrinsically safe portable instrument, appropriately calibrated and capable of measuring the concentrations of methane, carbon dioxide and oxygen.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	-
S12.7	Monitoring frequency and areas to be monitored should be specified prior to commencement of groundwork, either by the Safety Officer, or by an appropriately qualified person. All measurements should be recorded and documented.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	-
S12.7	Proceed drilling with adequate care and precautions against the potential hazards which may be encountered.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	-
S12.7	Prior to the commencement of the site works, the drilling contractor should devise a 'method-of- working' statement covering all normal and emergency procedures (including but not limited to number of operatives, experience and special skills of operatives, normal method of operations, emergency procedures, supervisors responsibilities, storage and use of safety equipment, safety procedures and signs, barriers and guarding). The site supervisor and all operatives must be familiar with this statement.	All area/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	-
S12.7	Where below ground service entries are necessary to the Incoming Switchgear Room, 132 kV Substation and Chlorine Store (I) and (II), the entry point should be sealed to prevent gas entry. In addition, any below grade cable trenches entering the Incoming Switchgear Room and 132 kV Substation can become the pathway for landfill gas and hence gridded metal covers should be used.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	N/A	-
S12.7	It is recommended regular landfill gas monitoring should be carried out at the Incoming Switchgear Room, 132 kV Substation and Chlorine Store (I) and (II). The monitoring frequency will be monthly for the first year of operation. If the monitoring results show no sign of landfill gas migration, reduce the monitoring frequency to once every six months.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	N/A	-

EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S12.7	The manholes and utility pits within the Project Site and along the freshwater mains. Each manhole/ utility pit should be monitored with two measurements (at mid depth and base). Each measurement should be monitored for a minimum of 10 minutes. A steady reading and peak reading should be recorded at each manhole/ utility pit and for each measurement. The need for venting the manhole/ utility pit and further monitoring will be reviewed after the initial monitoring.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	-
S12.7	All construction, operation and maintenance personnel working on-site as well as visitors should be made aware of the hazards of landfill gas and its possible presence on-site. This should be achieved through a combination of posting warning signs in prominent places and also by access to detailed information on landfill gas hazards and the designs and procedural means by which these hazards are being minimized on-site.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	-





Note: D – Design stage C – Construction O – Operation

Appendix D


Water Quality Monitoring Graphical Presentation

- Appendix D.1 Weather Condition
- Appendix D.2 Key Activities Carried Out During the Reporting Quarter
- Appendix D.3 Other Factor Might Affect the Monitoring Results


Monitoring Location: CE

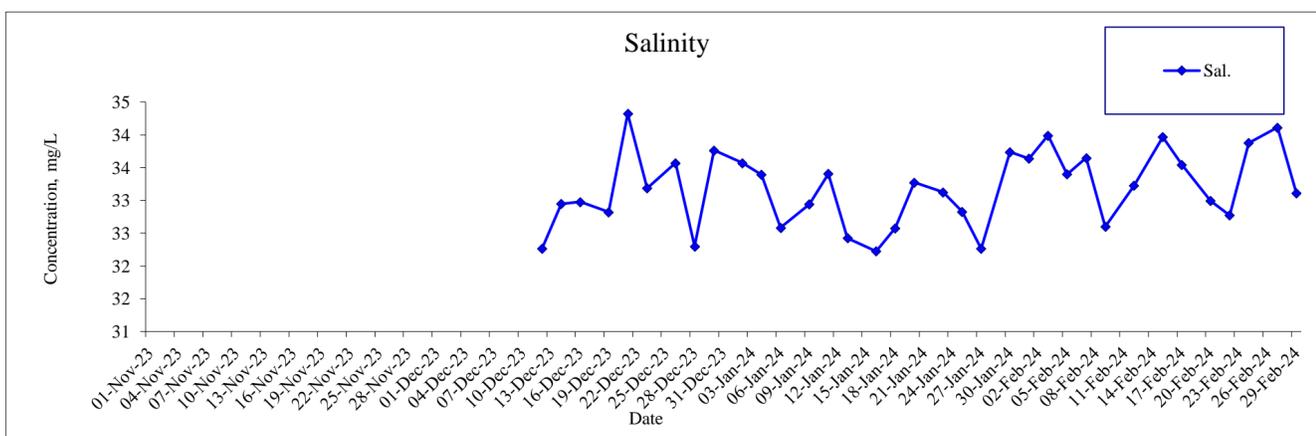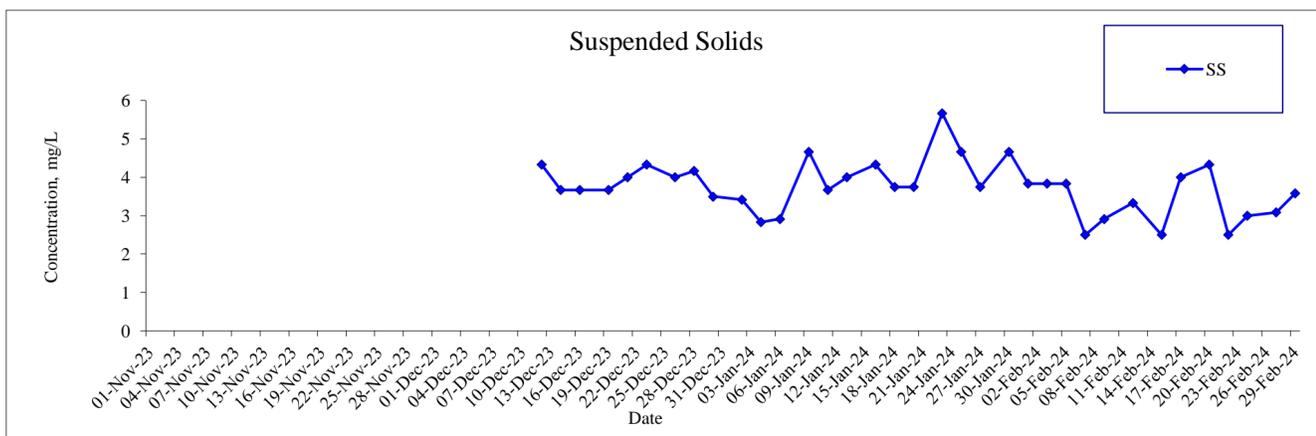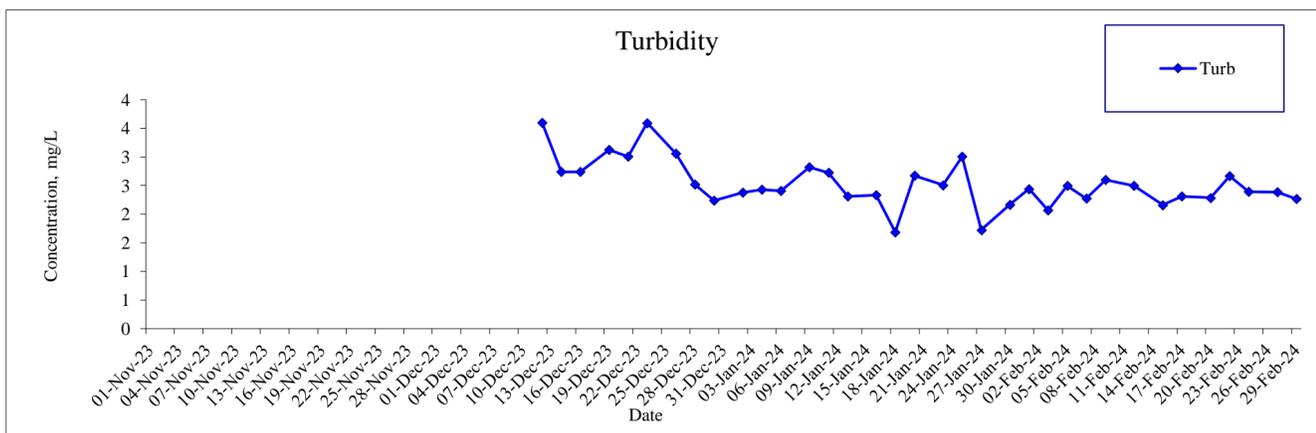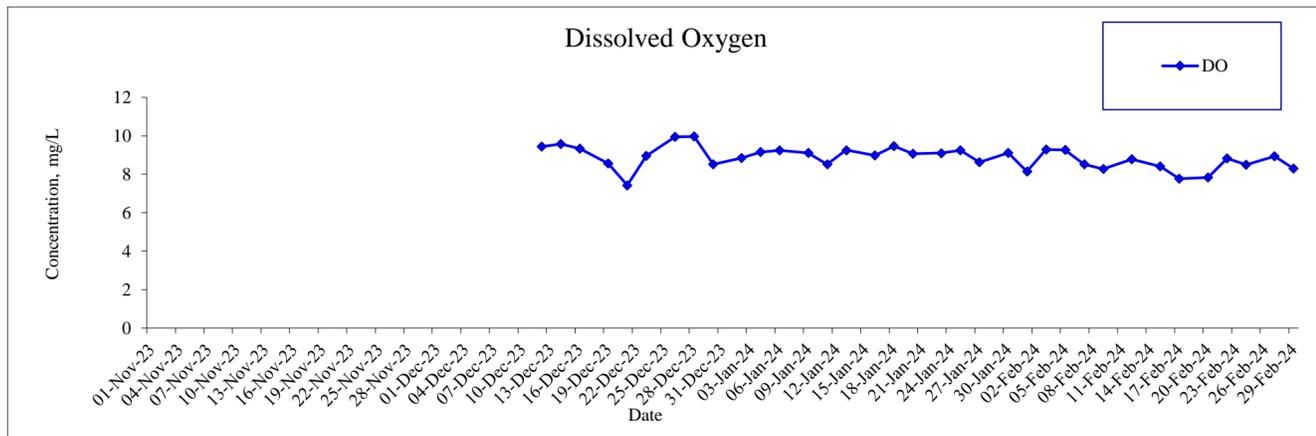

Monitoring Location: CE




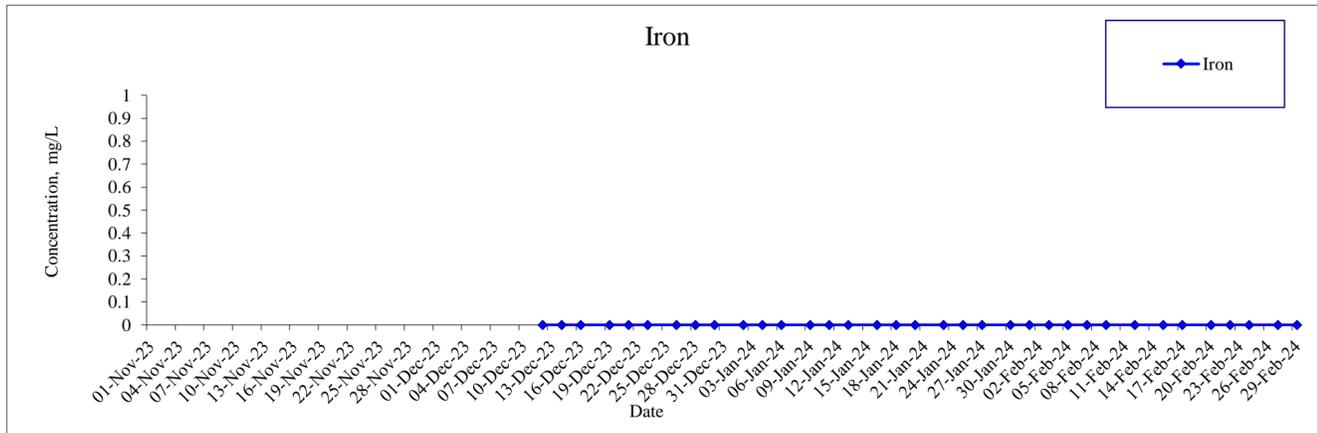


Remark: The lowest detection limit of the Iron is 0.1mg/L. All result of iron monitoring are lower than the detection limit.

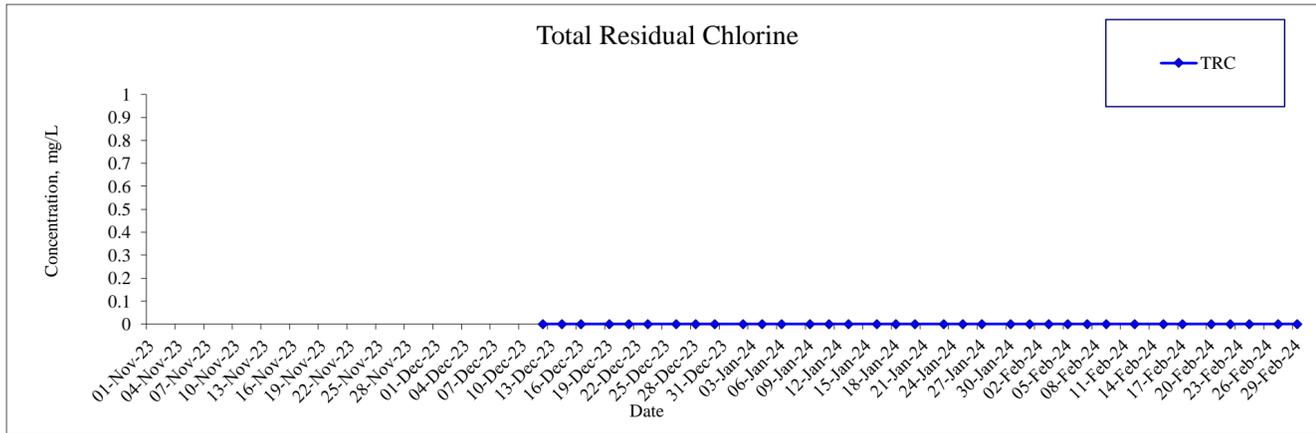


Remark: The lowest detection limit of the Total Residual Chlorine is 0.01mg/L. All result of Total Residual Chlorine monitoring are lower than the detection limit.


Monitoring Location: CF

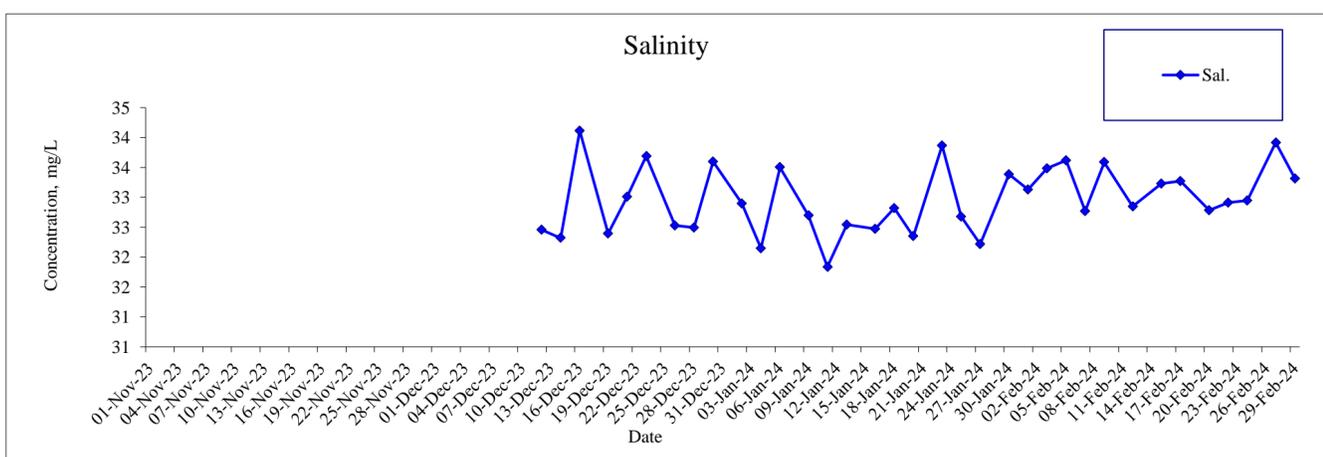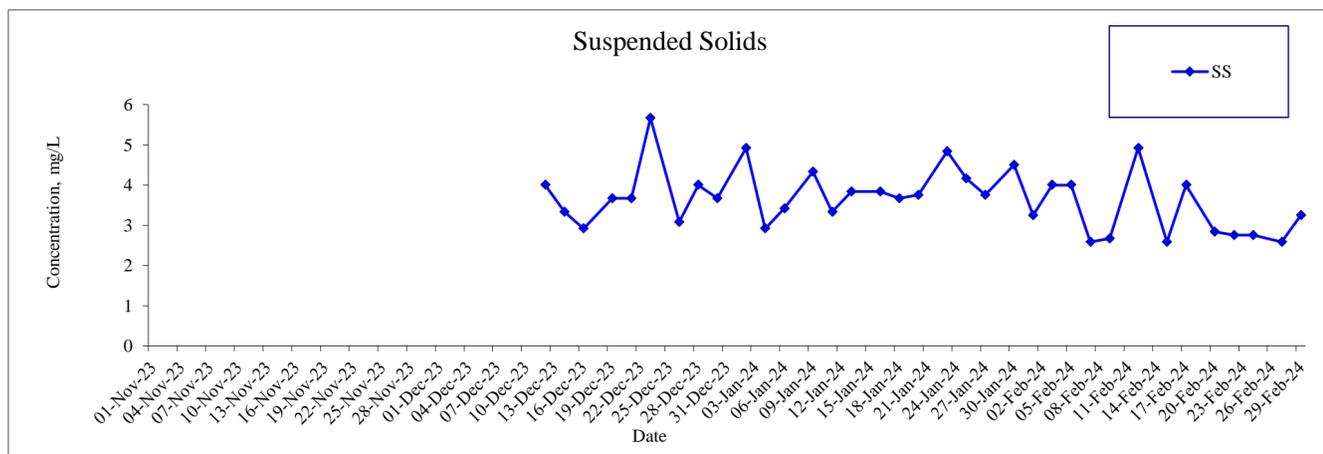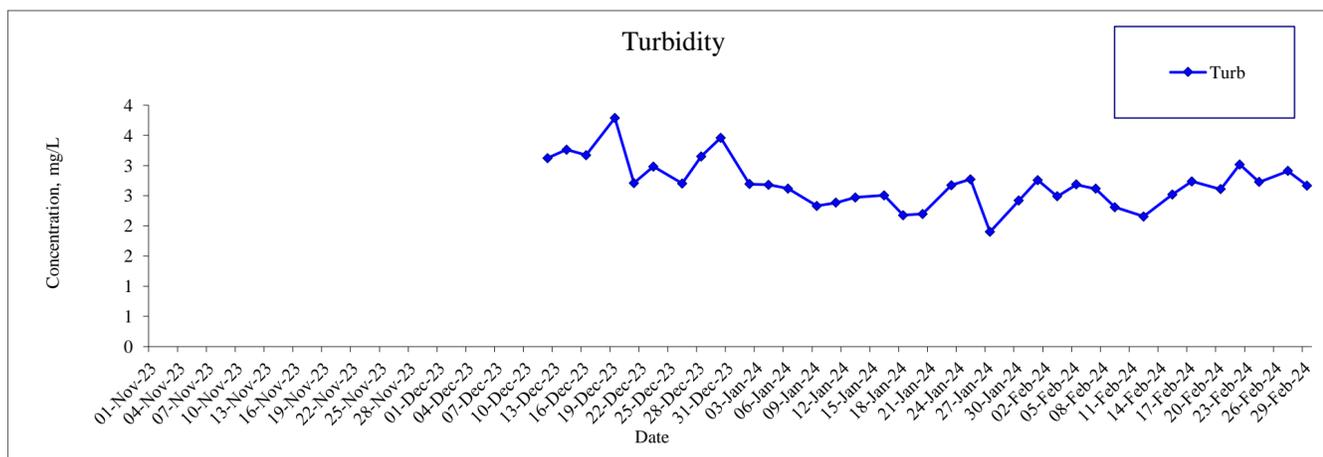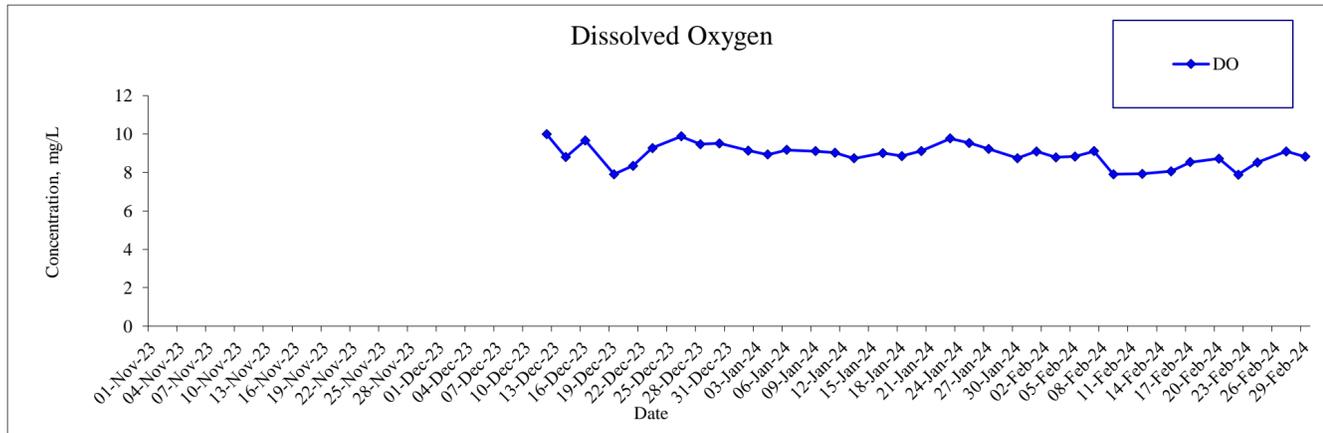

Monitoring Location: CF




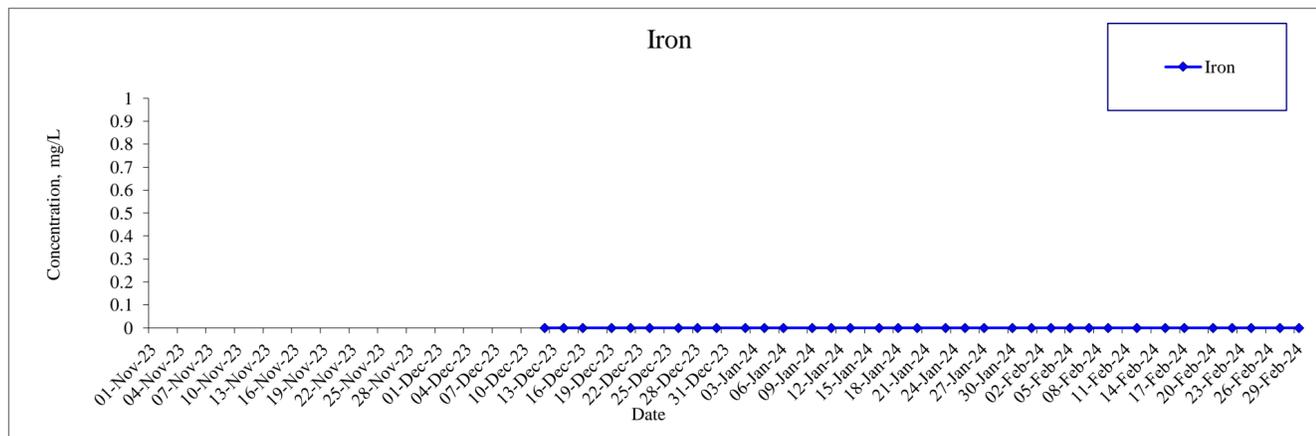


Remark: The lowest detection limit of the Iron is 0.1mg/L. All result of iron monitoring are lower than the detection limit.

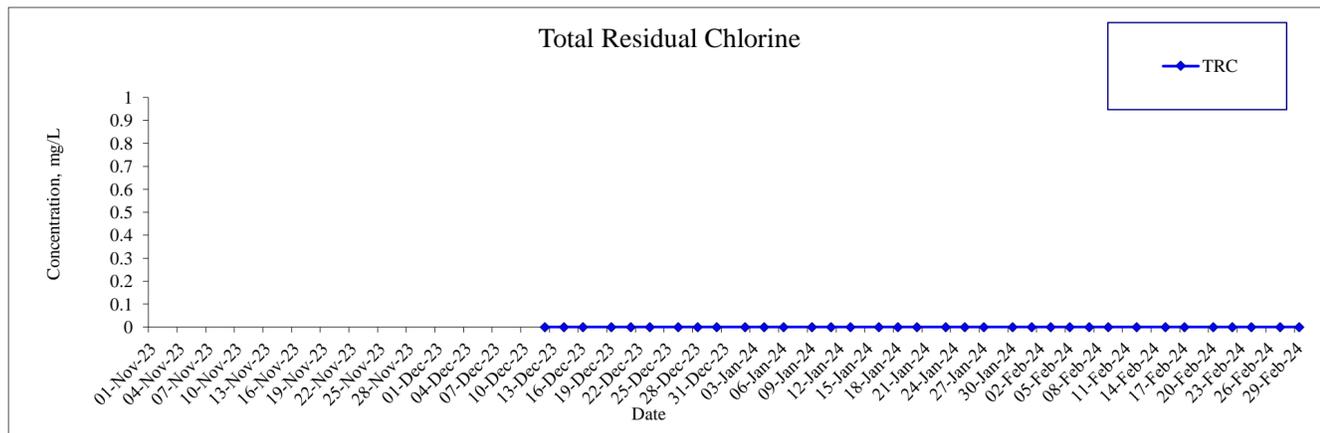


Remark: The lowest detection limit of the Total Residual Chlorine is 0.01mg/L. All result of Total Residual Chlorine monitoring are lower than the detection limit.


Monitoring Location: WSR1

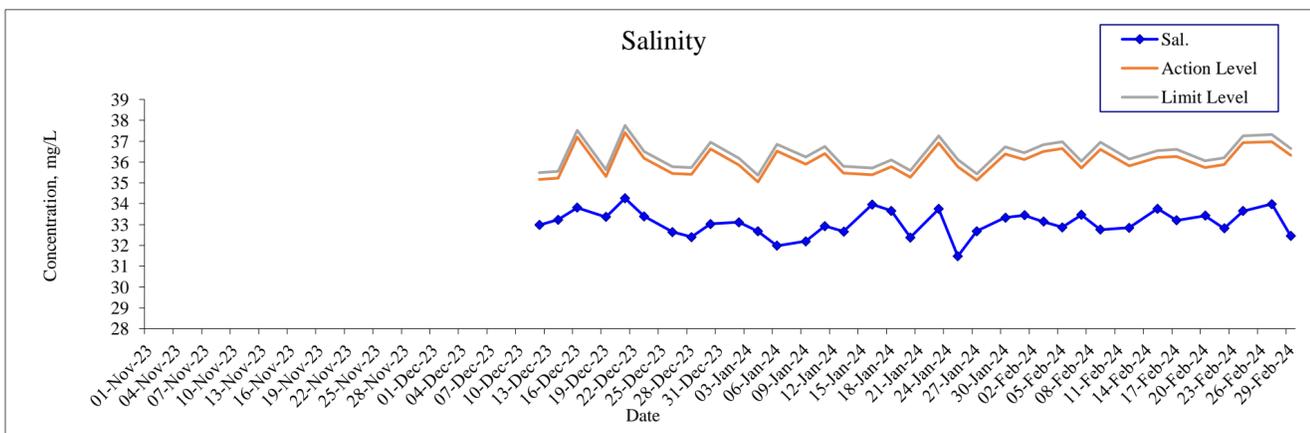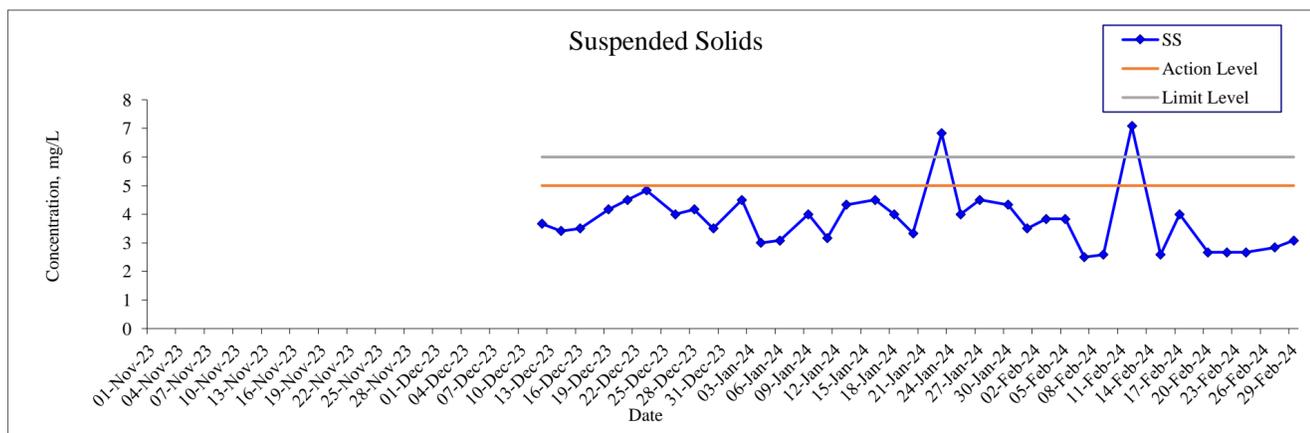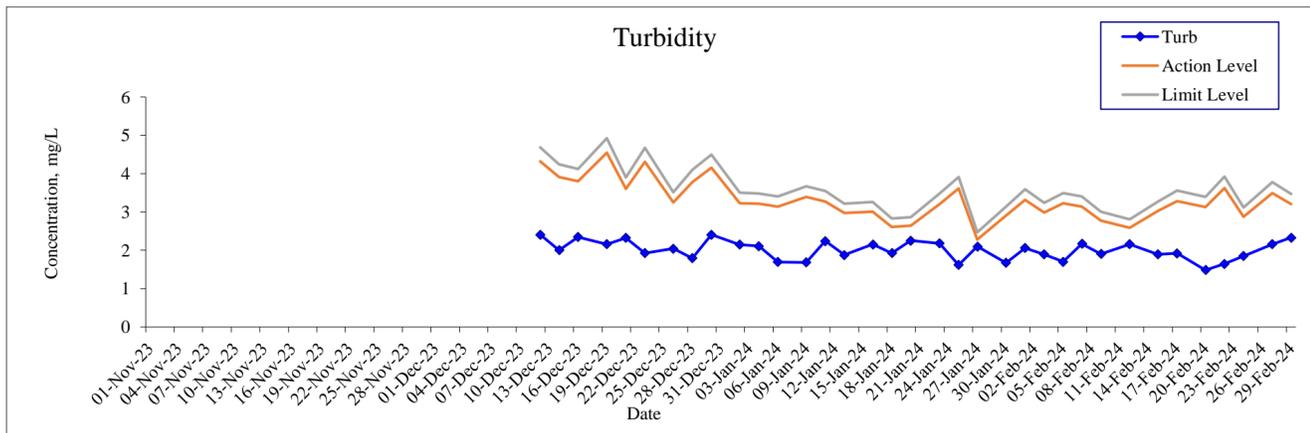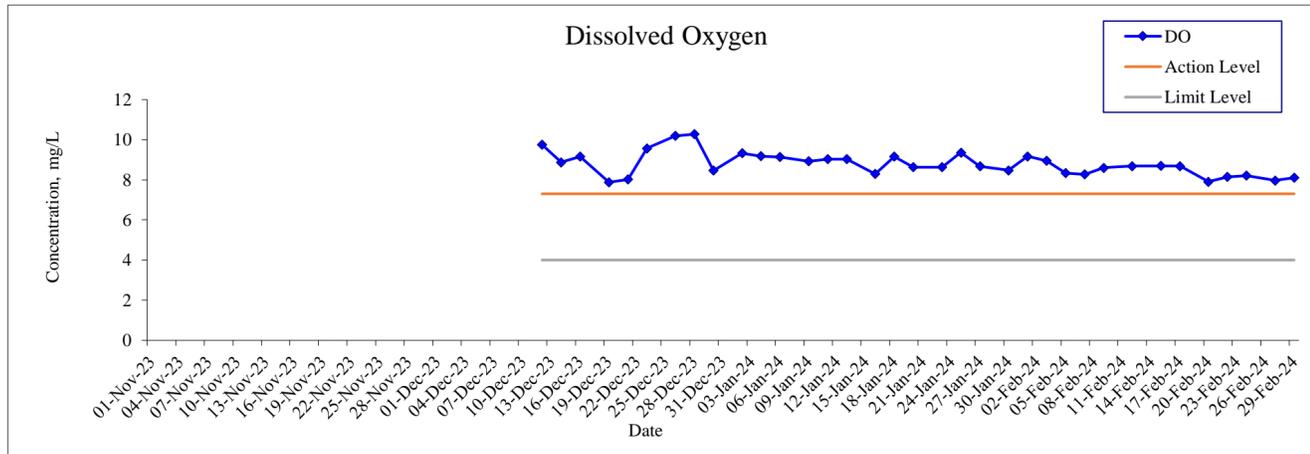

Monitoring Location: WSR1




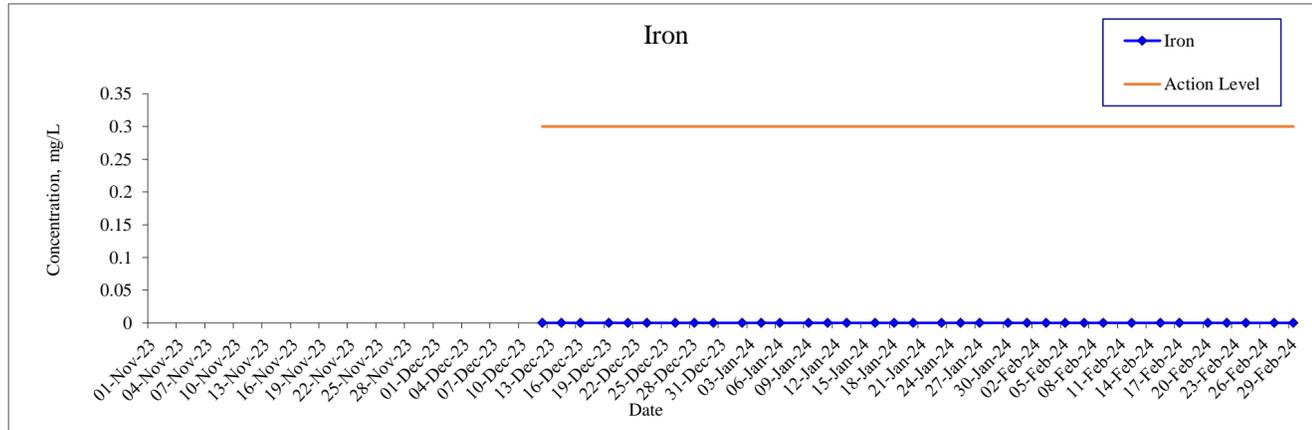


Remark: The lowest detection limit of the Iron is 0.1mg/L. All result of iron monitoring are lower than the detection limit.

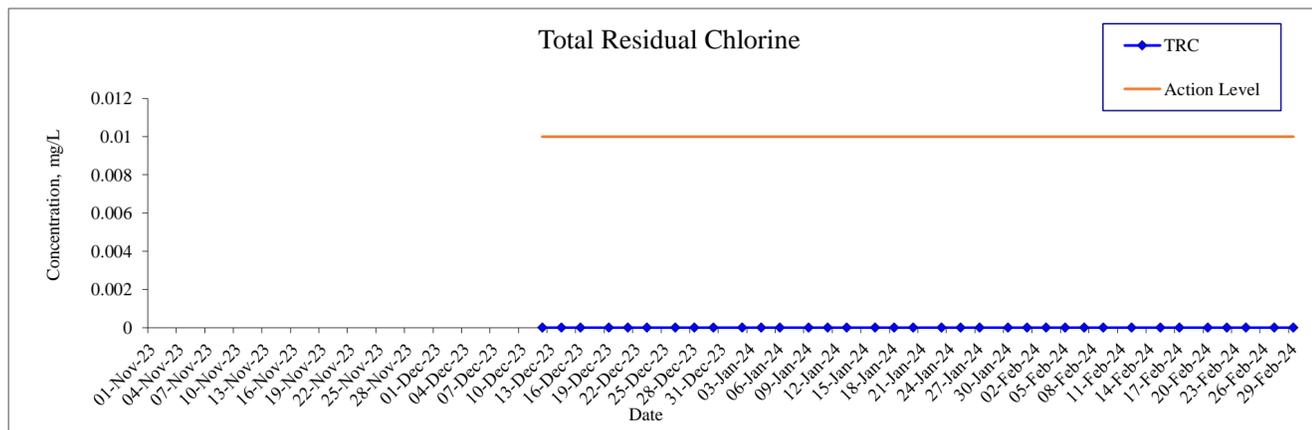


Remark: The lowest detection limit of the Total Residual Chlorine is 0.01mg/L. All result of Total Residual Chlorine monitoring are lower than the detection limit.


Monitoring Location: WSR2

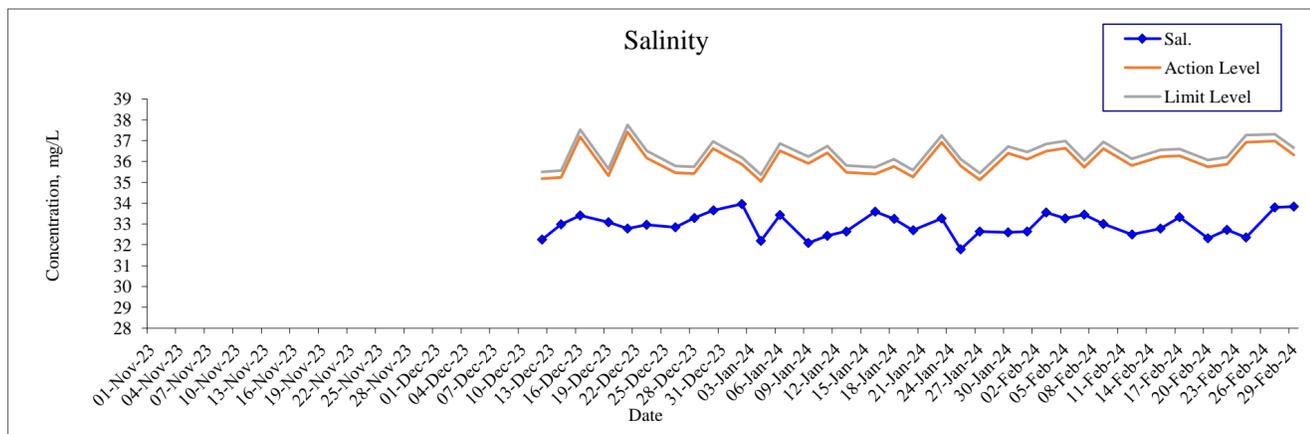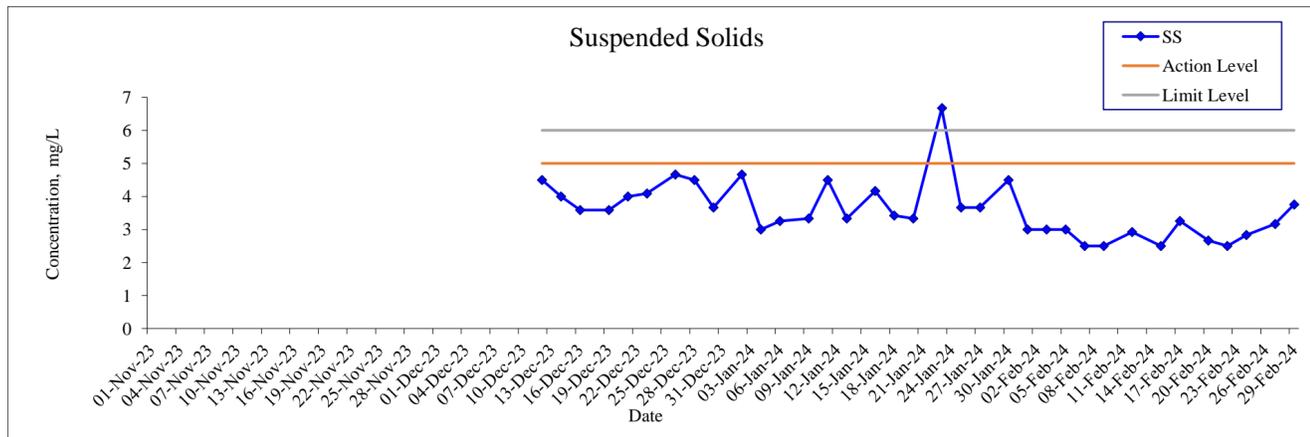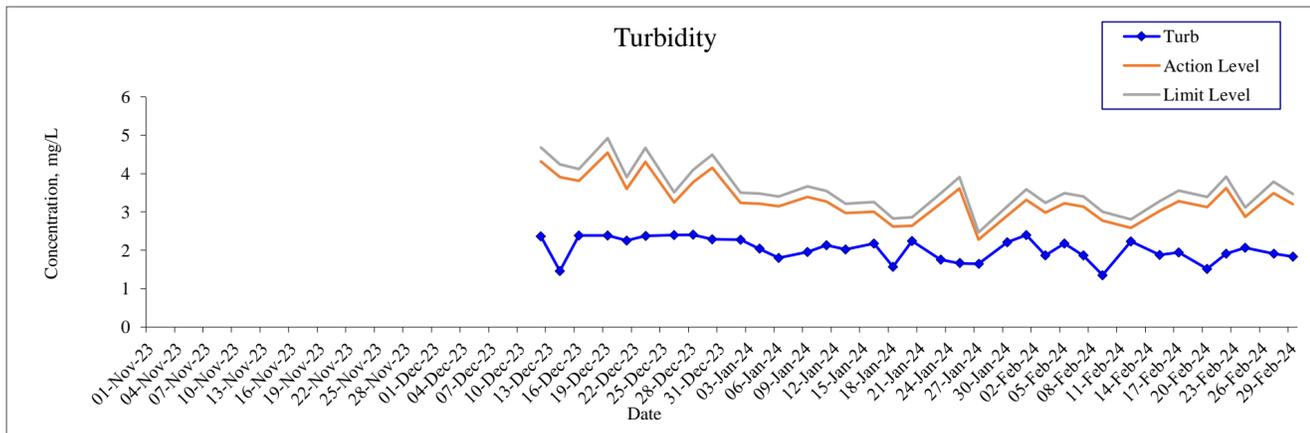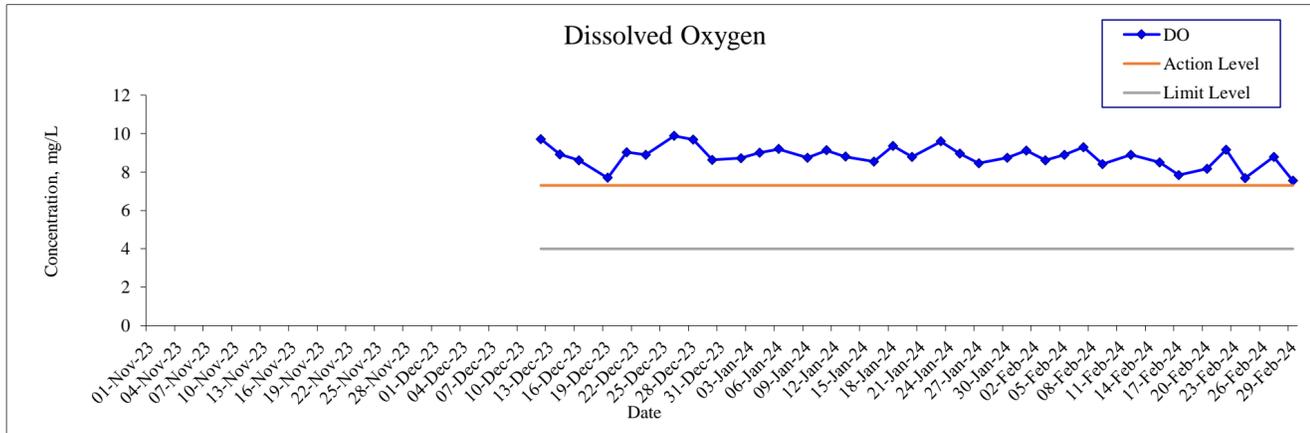

Monitoring Location: WSR2




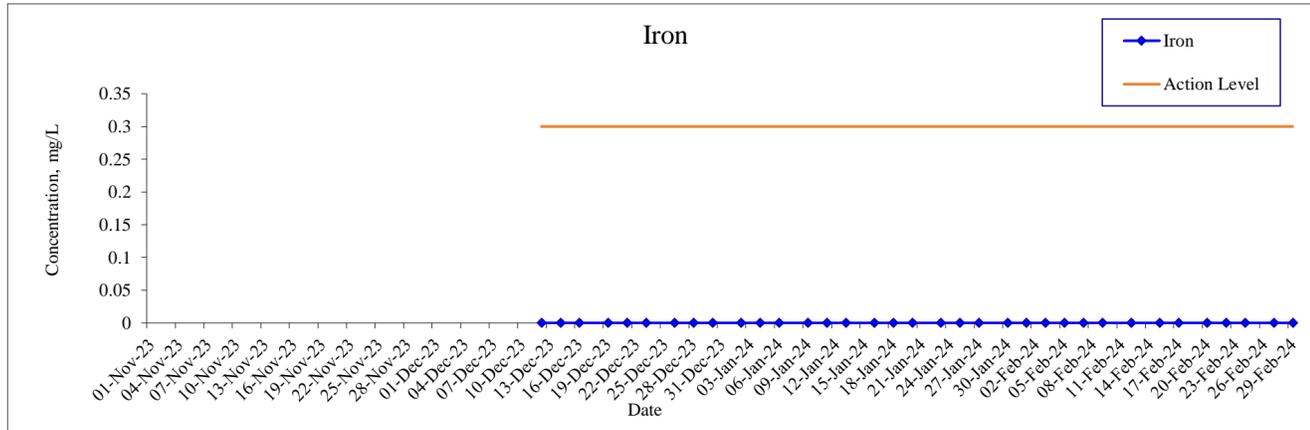


Remark: The lowest detection limit of the Iron is 0.1mg/L. All result of iron monitoring are lower than the detection limit.

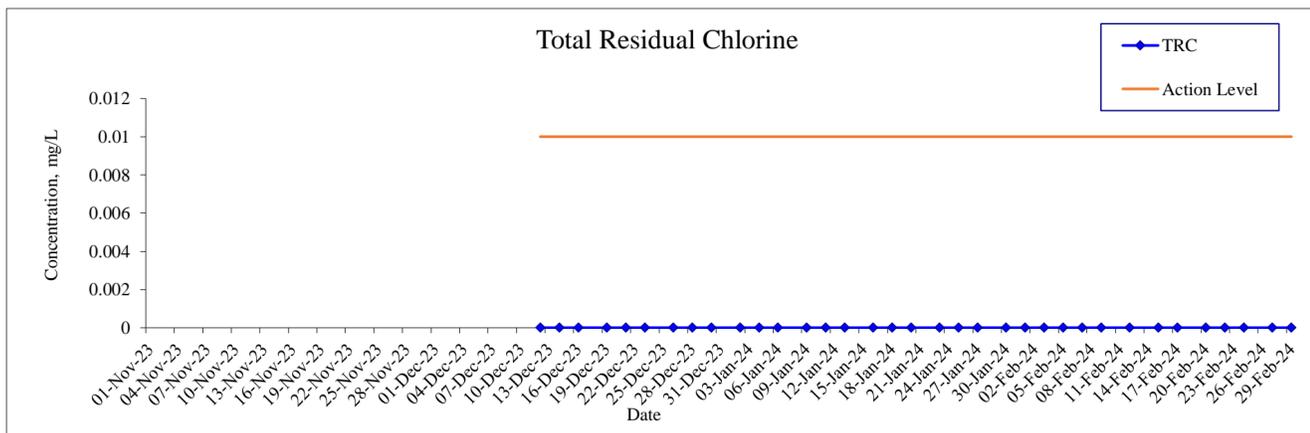


Remark: The lowest detection limit of the Total Residual Chlorine is 0.01mg/L. All result of Total Residual Chlorine monitoring are lower than the detection limit.


Monitoring Location: WSR3

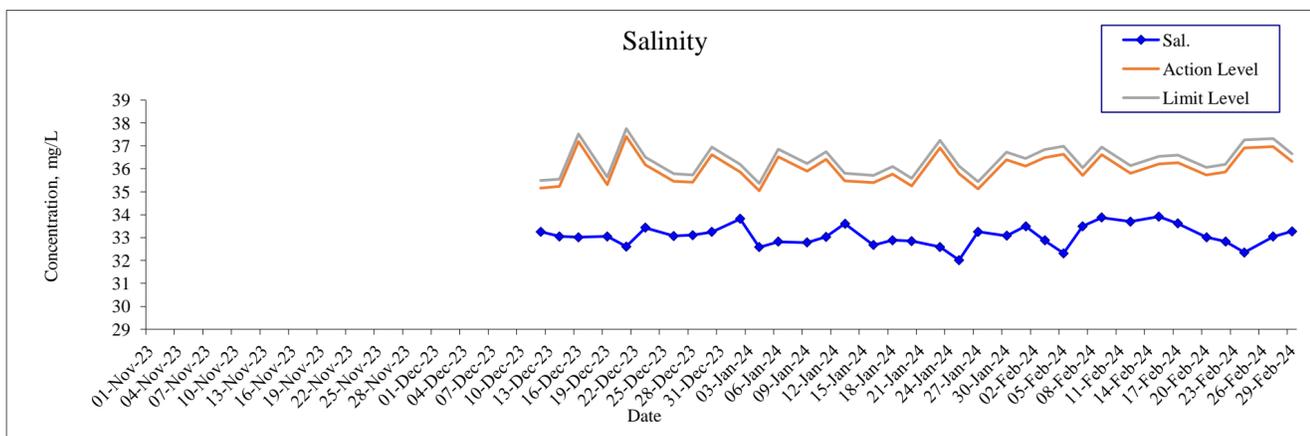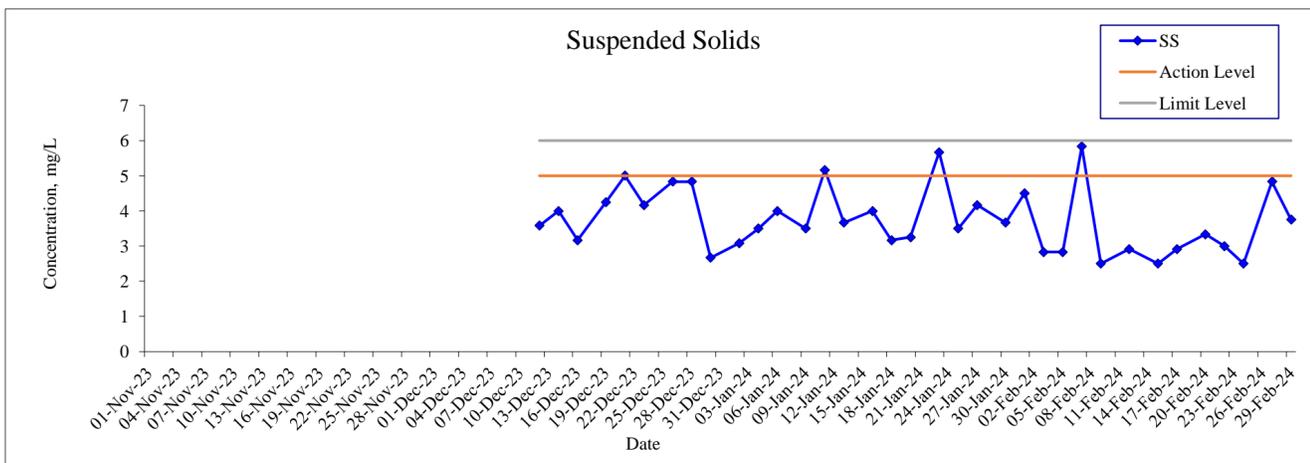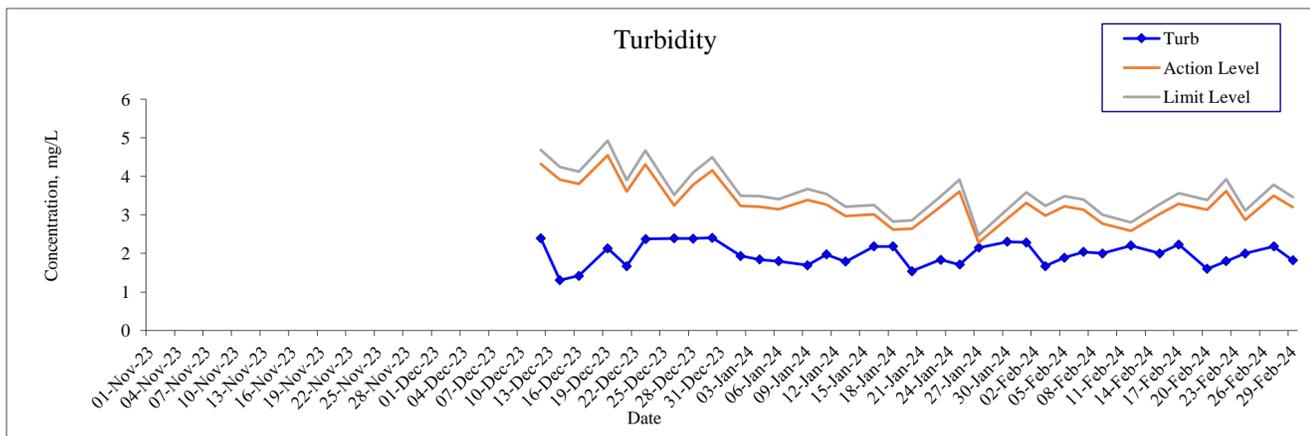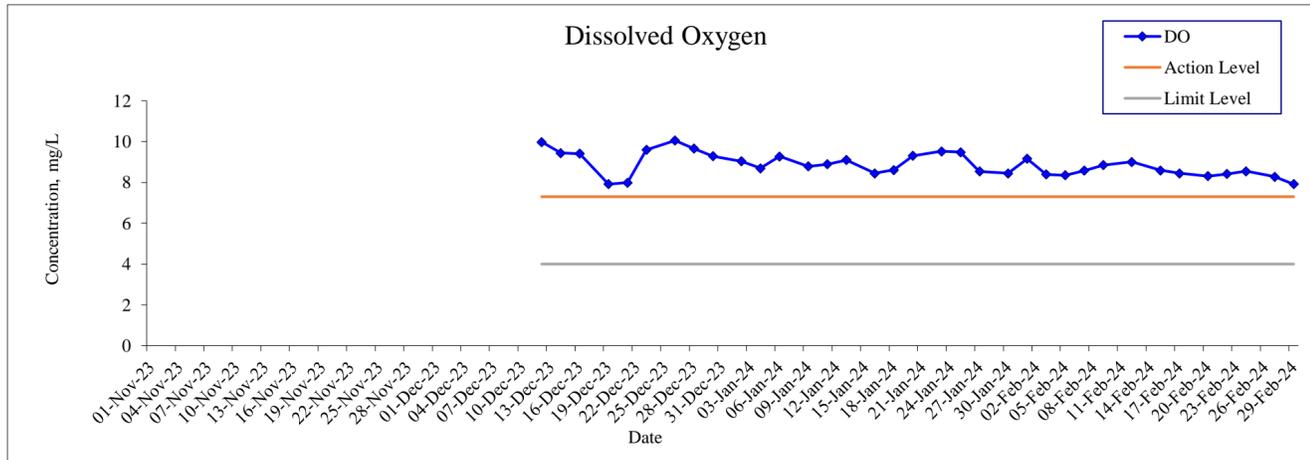

Monitoring Location: WSR3




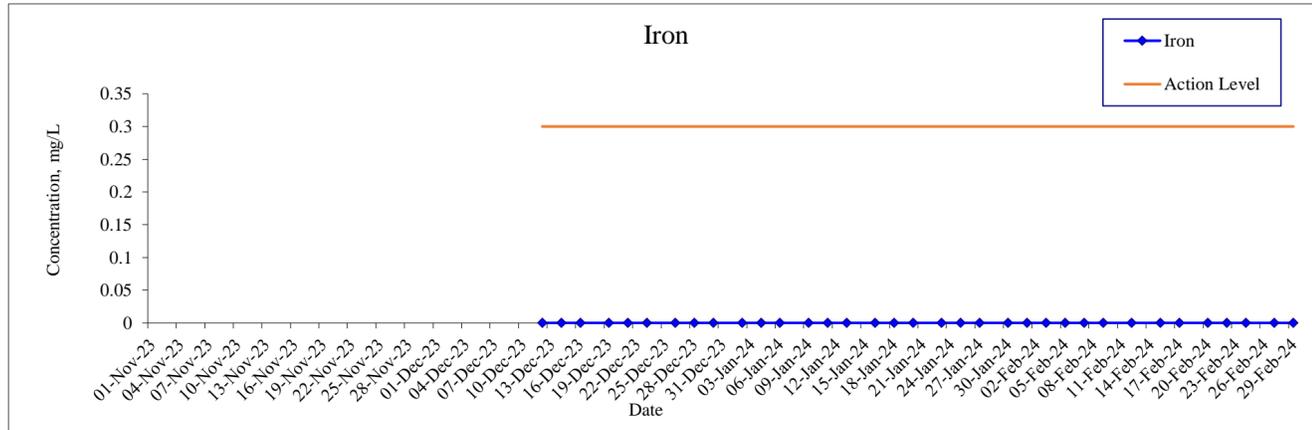


Remark: The lowest detection limit of the Iron is 0.1mg/L. All result of iron monitoring are lower than the detection limit.

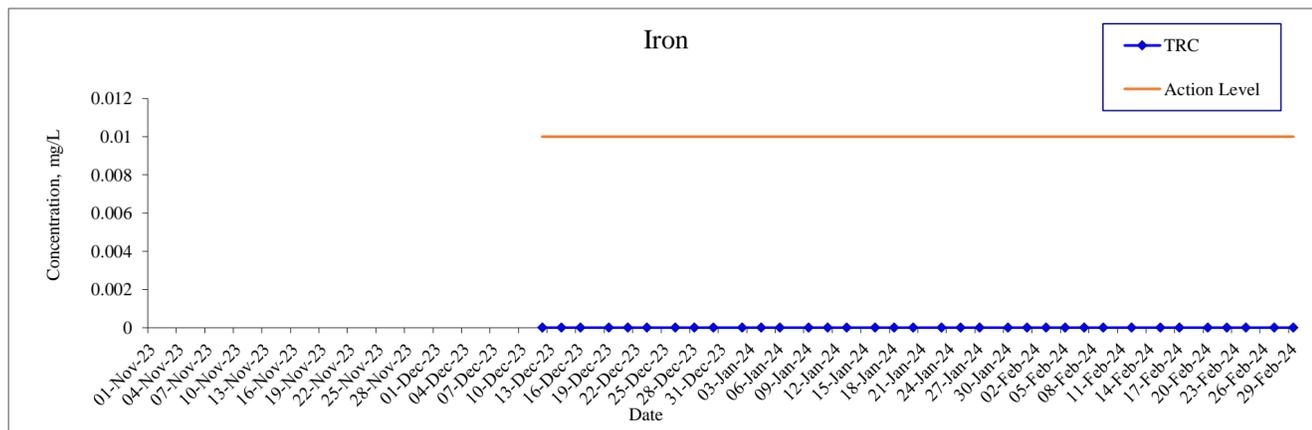


Remark: The lowest detection limit of the Total Residual Chlorine is 0.01mg/L. All result of Total Residual Chlorine monitoring are lower than the detection limit.


Monitoring Location: WSR4

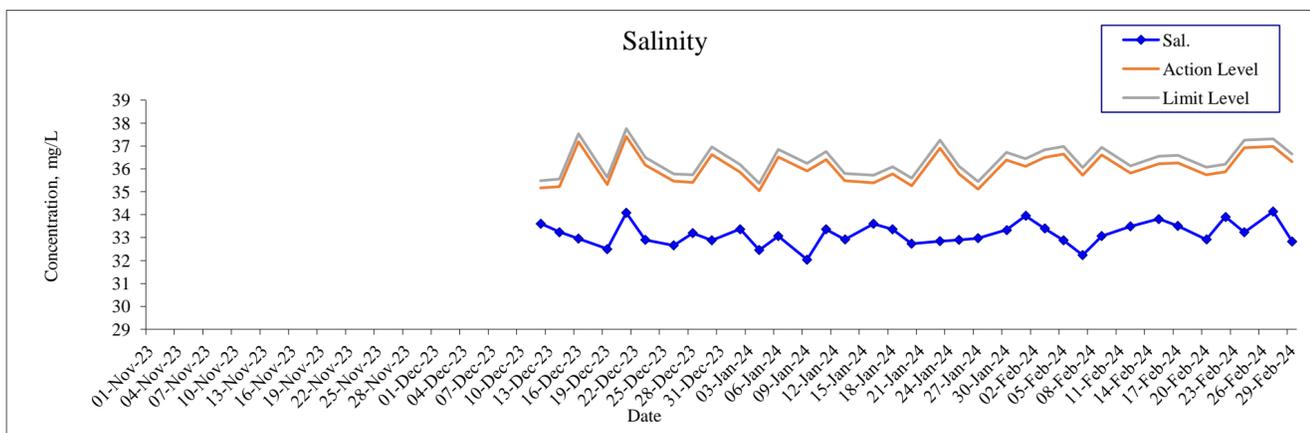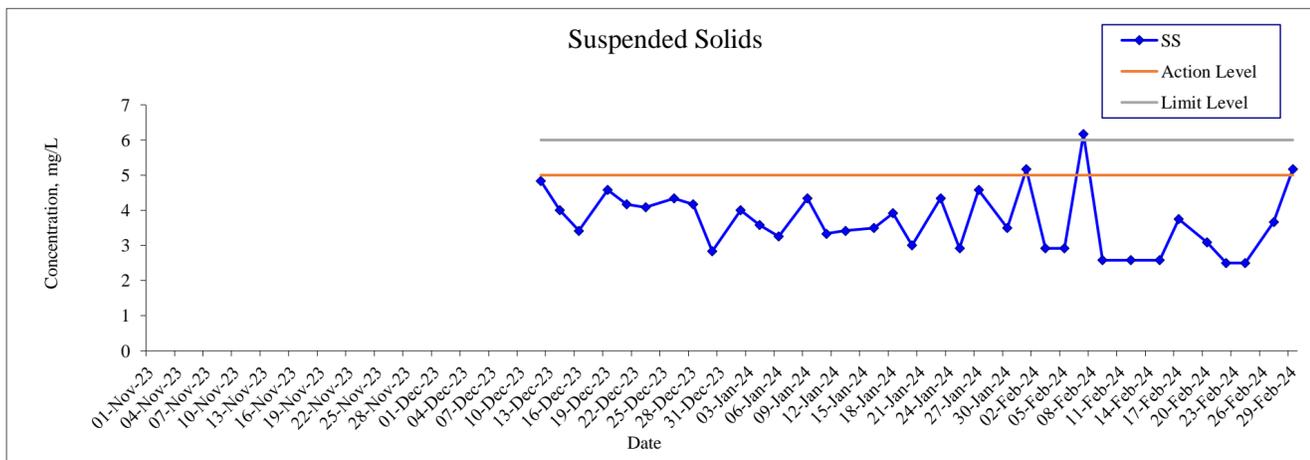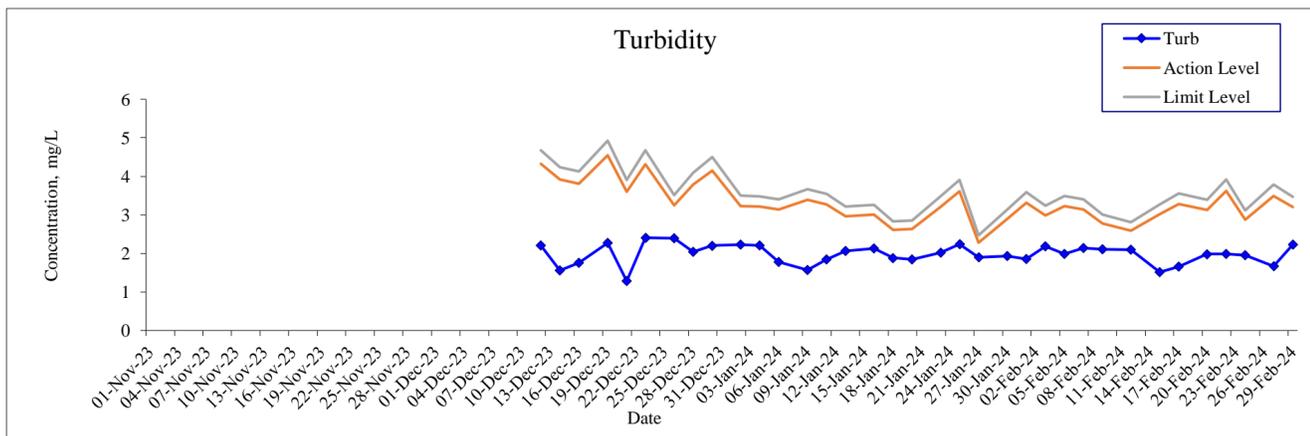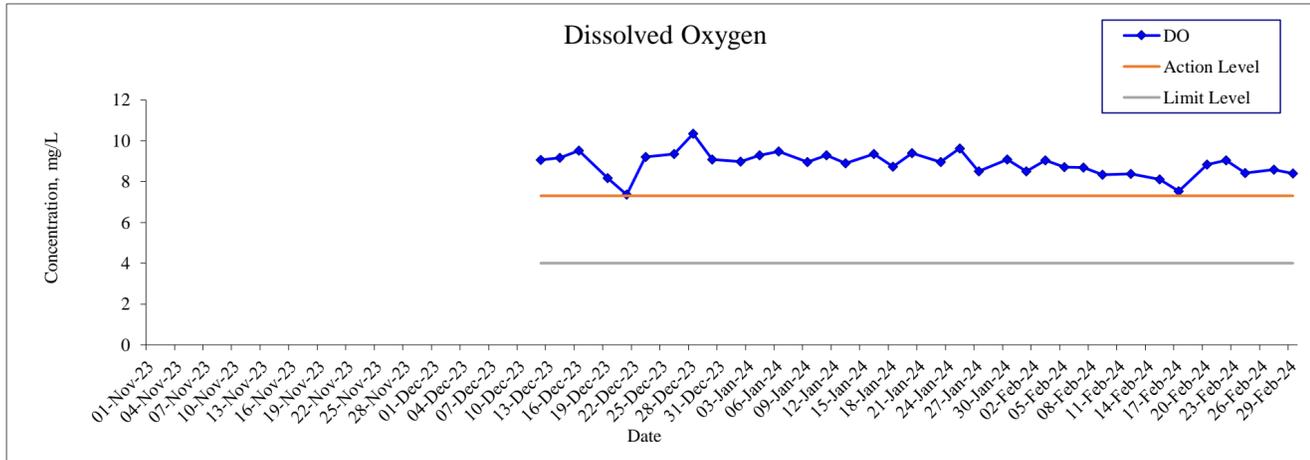

Monitoring Location: WSR4




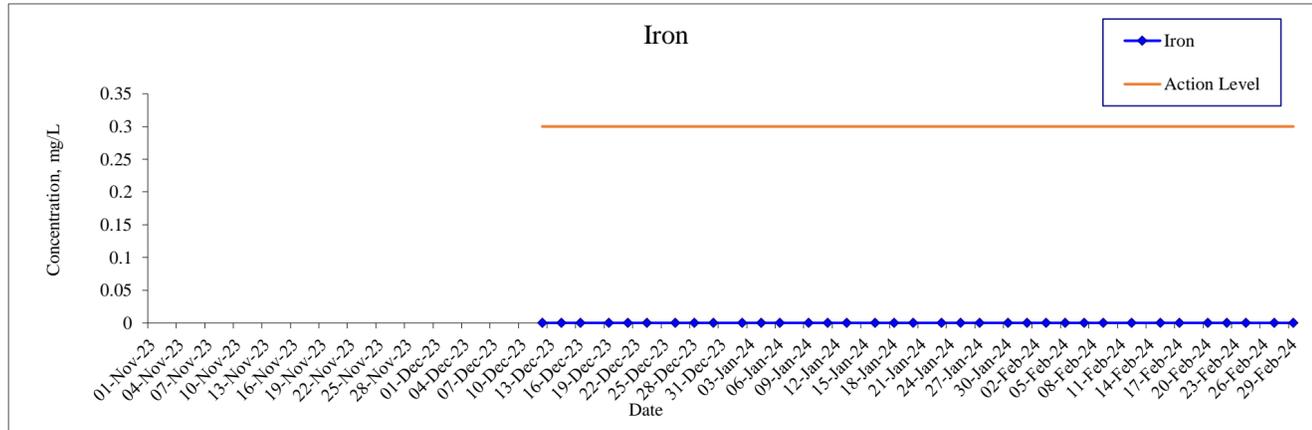


Remark: The lowest detection limit of the Iron is 0.1mg/L. All result of iron monitoring are lower than the detection limit.

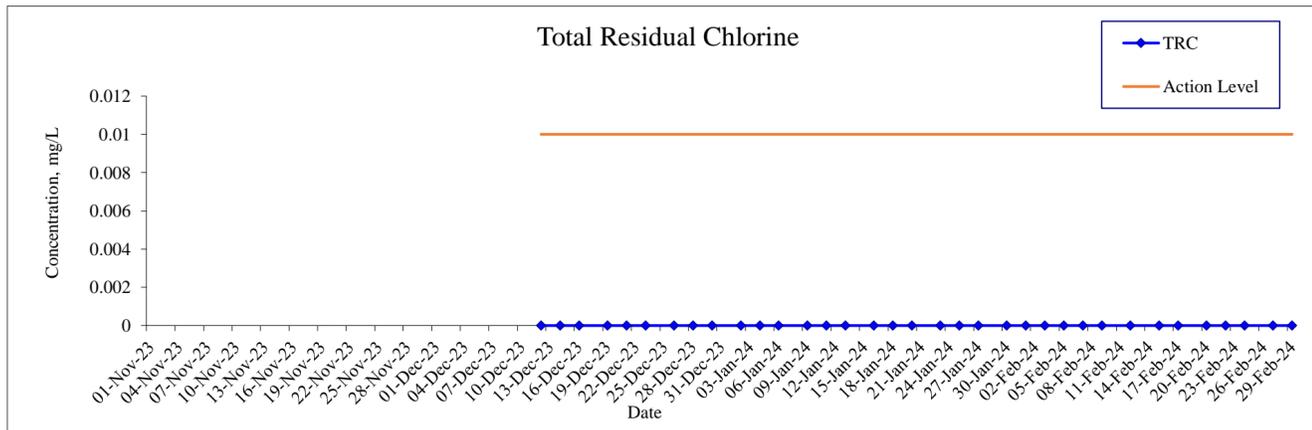


Remark: The lowest detection limit of the Total Residual Chlorine is 0.01mg/L. All result of Total Residual Chlorine monitoring are lower than the detection limit.


Monitoring Location: WSR16

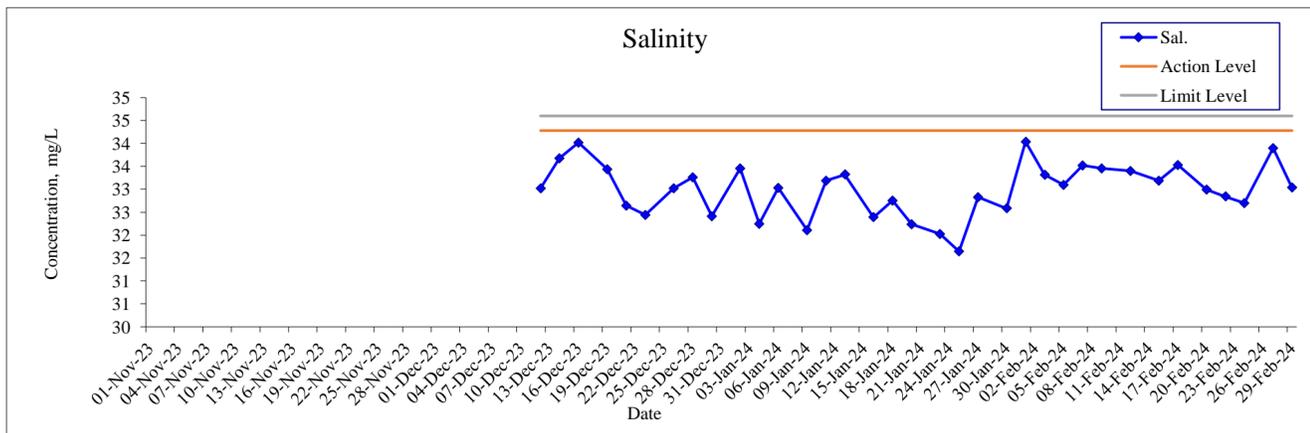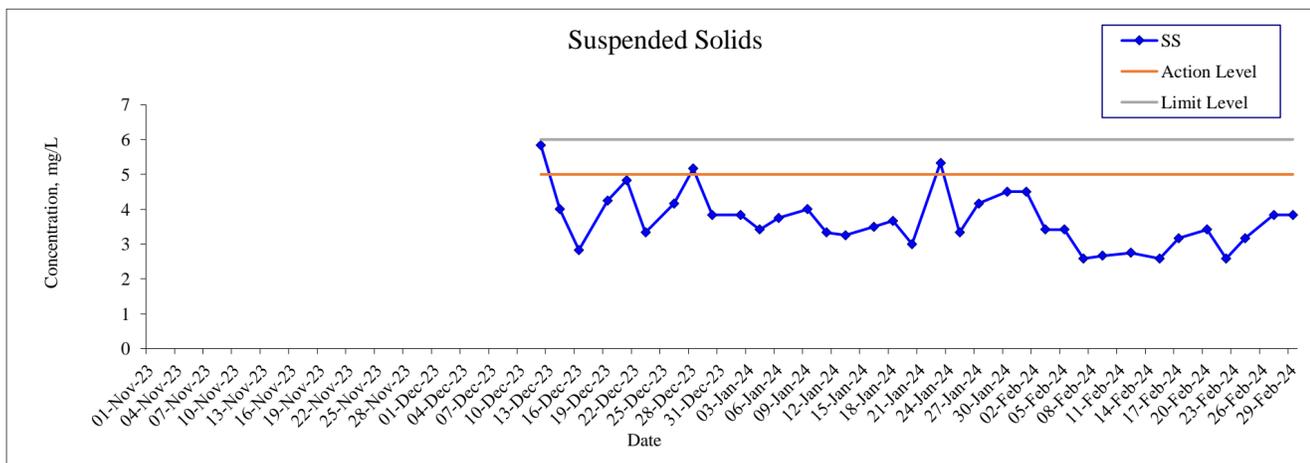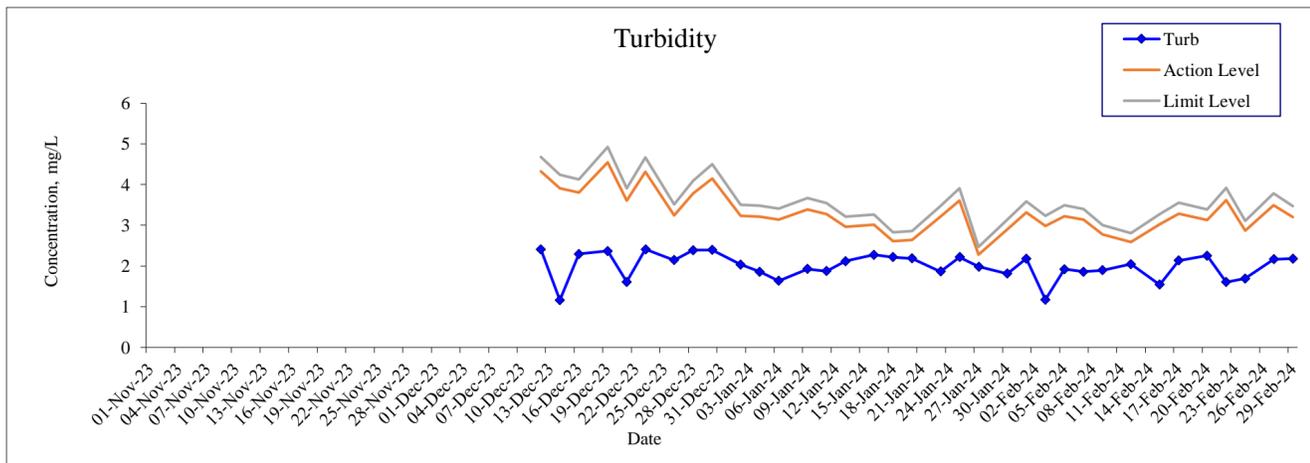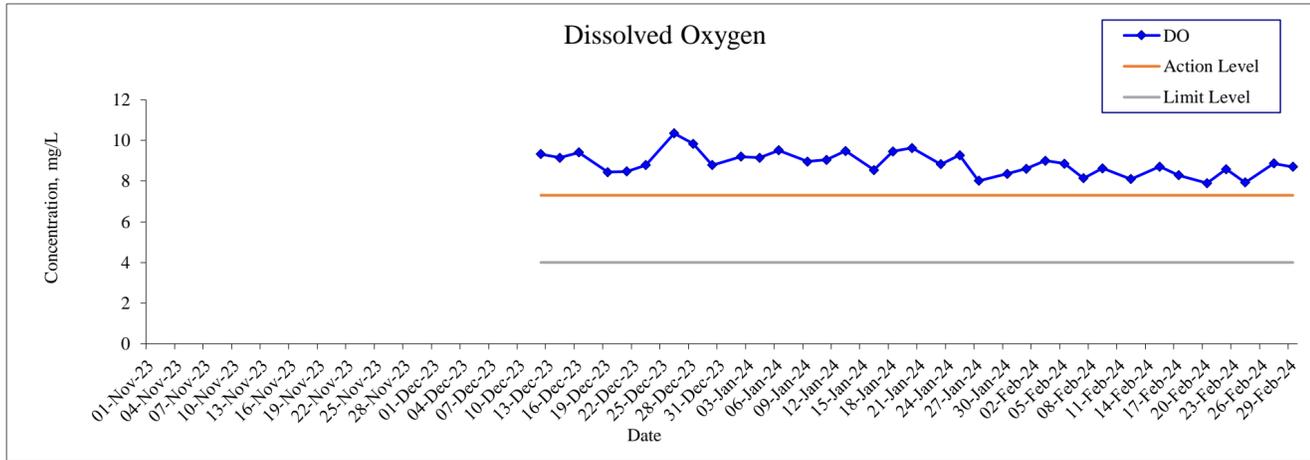

Monitoring Location: WSR16




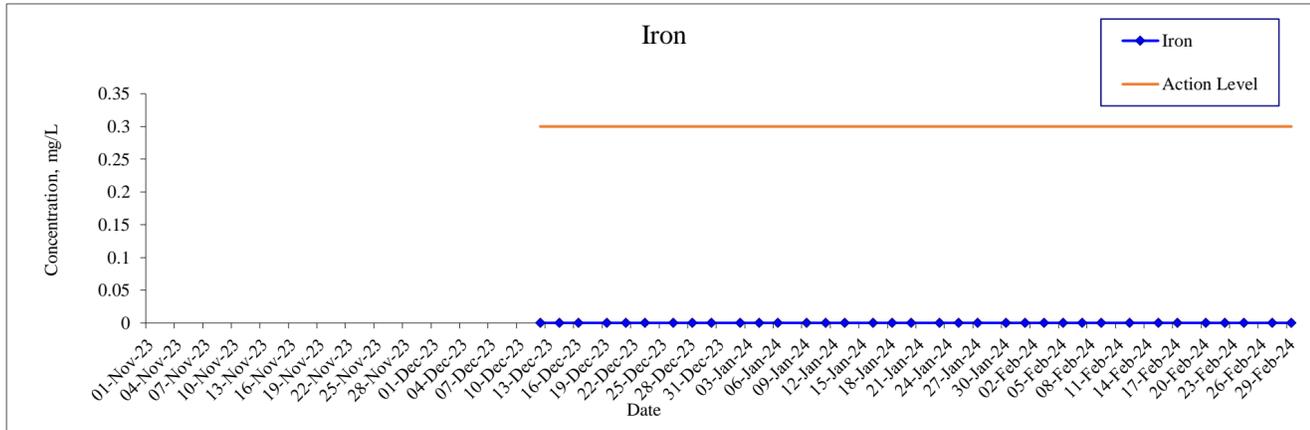


Remark: The lowest detection limit of the Iron is 0.1mg/L. All result of iron monitoring are lower than the detection limit.

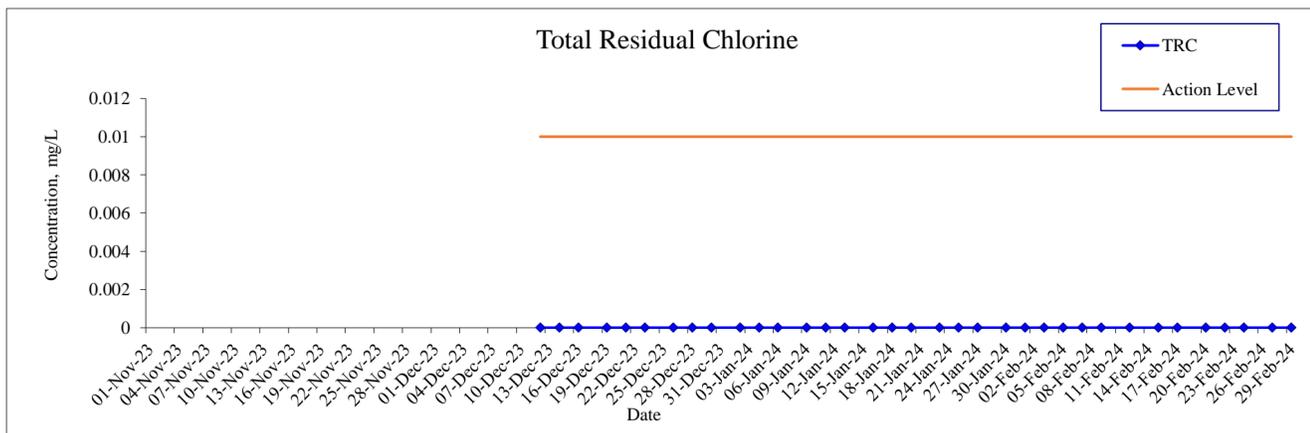


Remark: The lowest detection limit of the Total Residual Chlorine is 0.01mg/L. All result of Total Residual Chlorine monitoring are lower than the detection limit.


Monitoring Location: WSR33

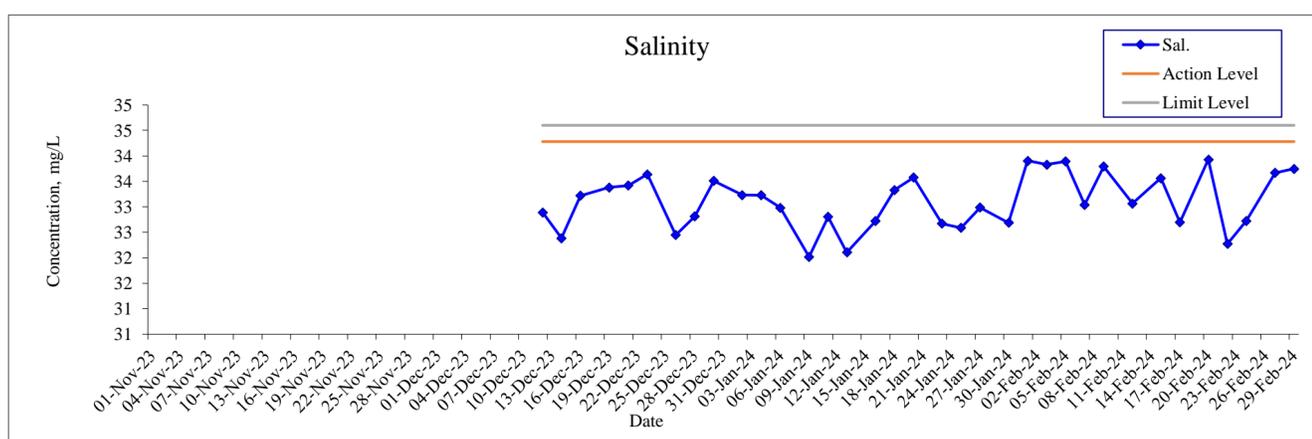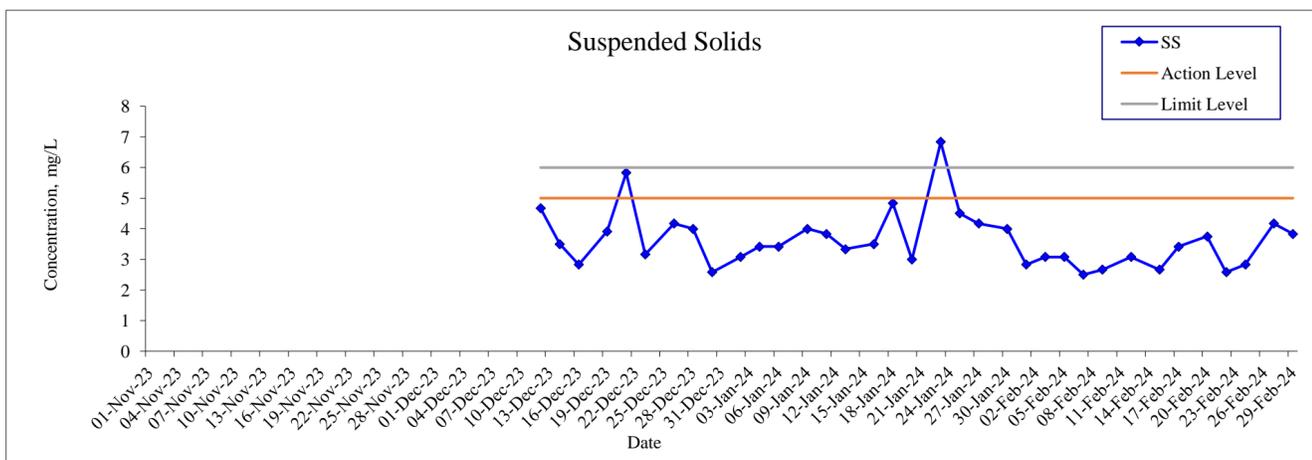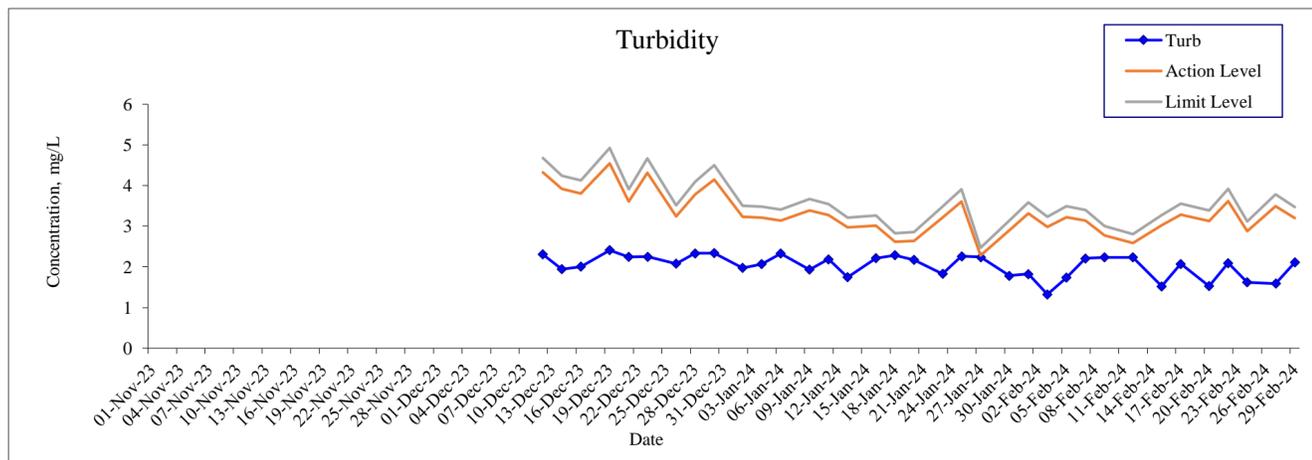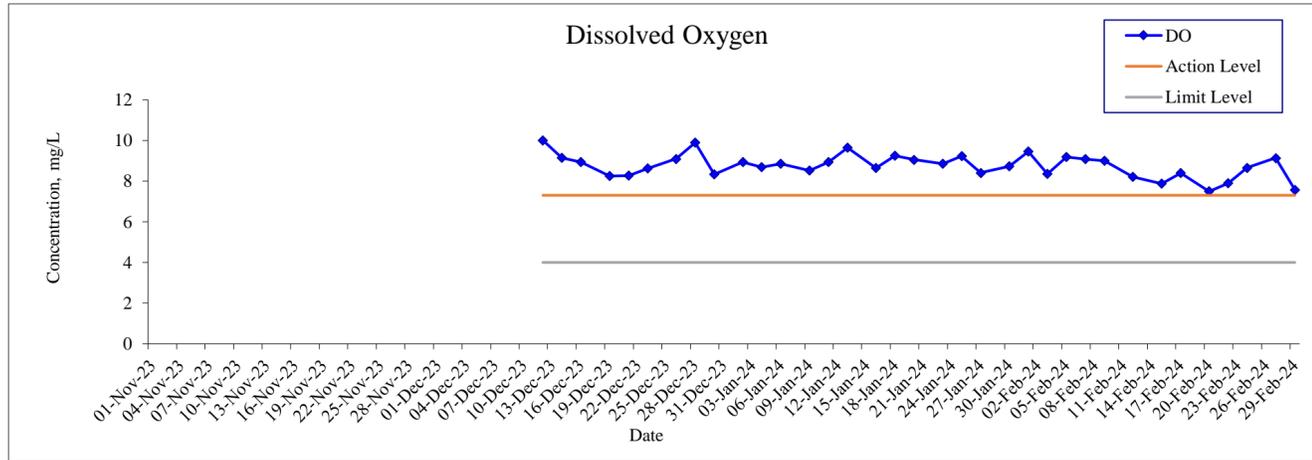

Monitoring Location: WSR33




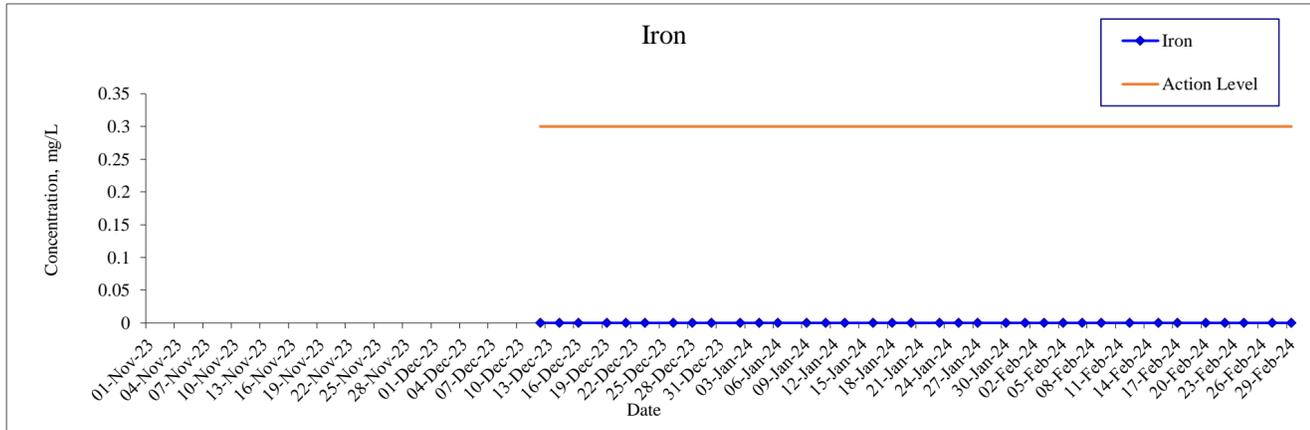


Remark: The lowest detection limit of the Iron is 0.1mg/L. All result of iron monitoring are lower than the detection limit.

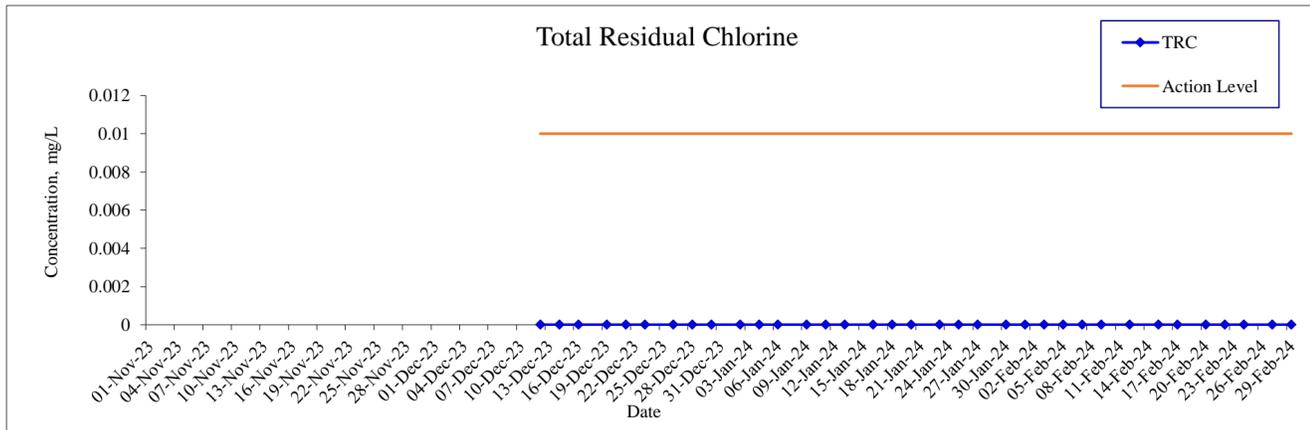


Remark: The lowest detection limit of the Total Residual Chlorine is 0.01mg/L. All result of Total Residual Chlorine monitoring are lower than the detection limit.


Monitoring Location: WSR36

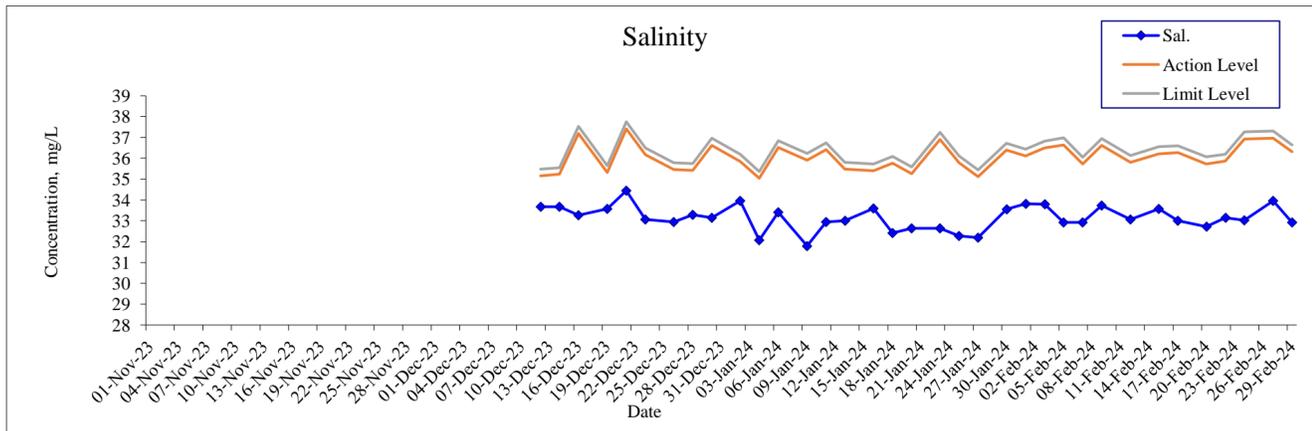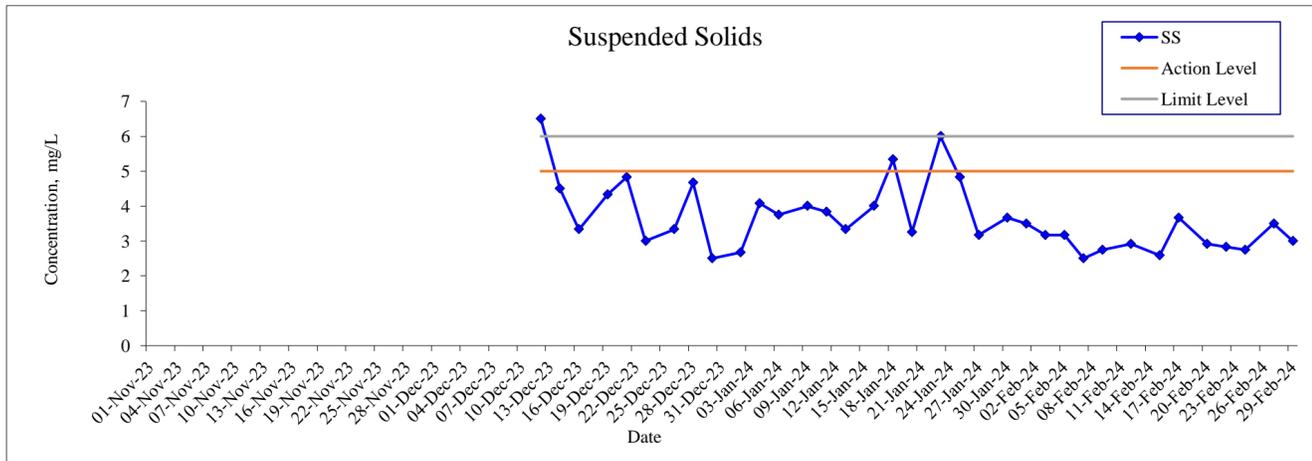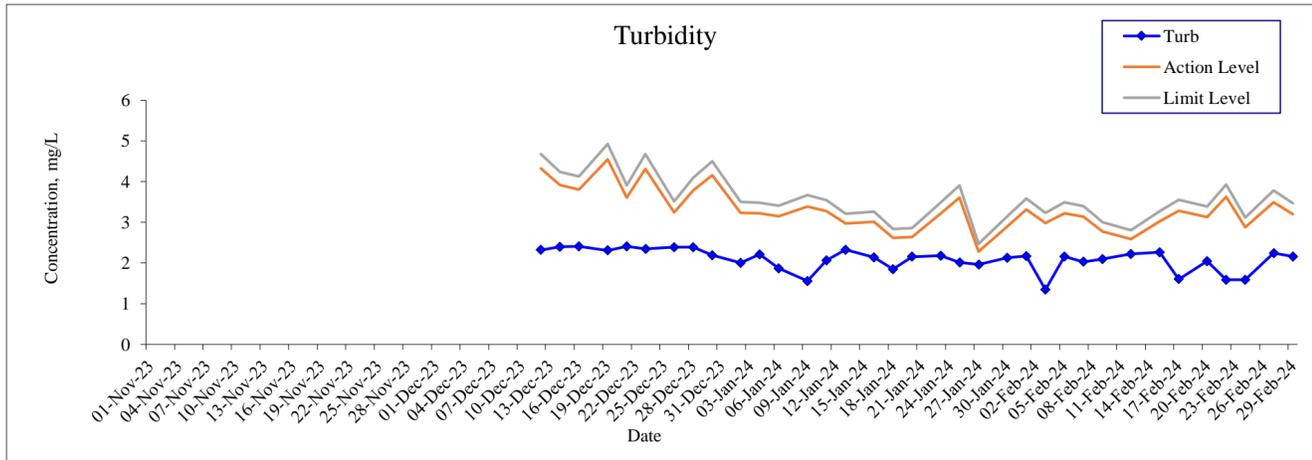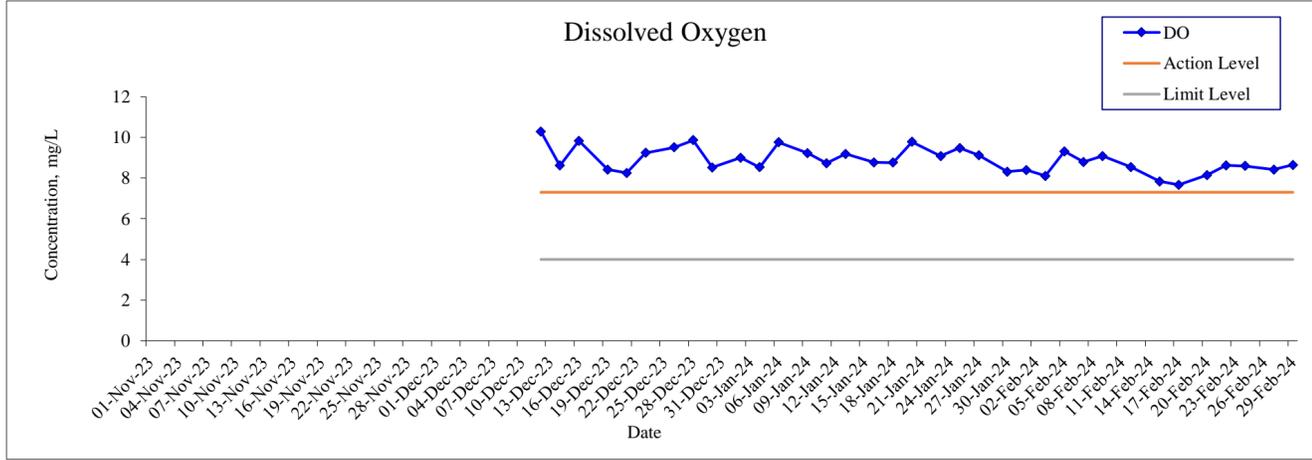

Monitoring Location: WSR36




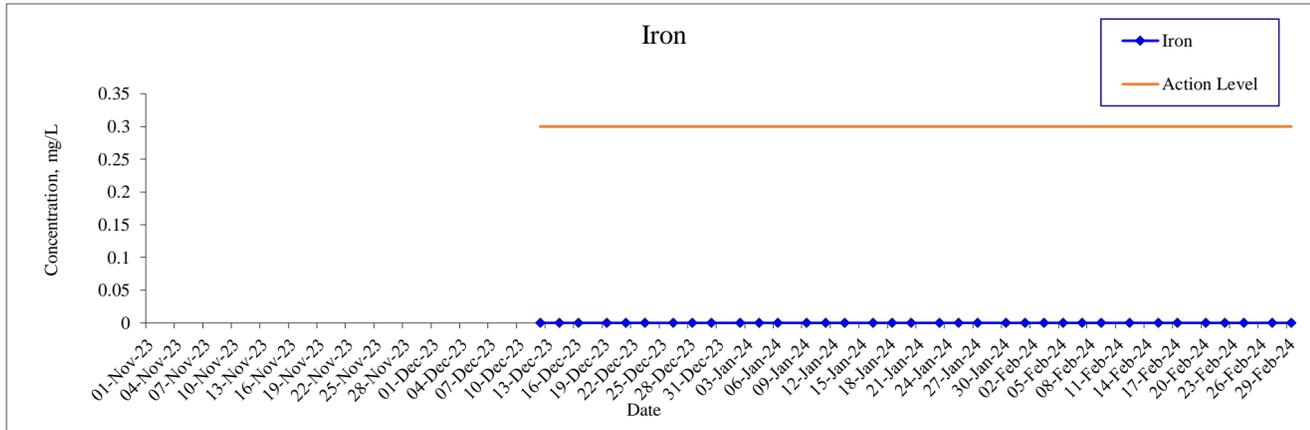


Remark: The lowest detection limit of the Iron is 0.1mg/L. All result of iron monitoring are lower than the detection limit.

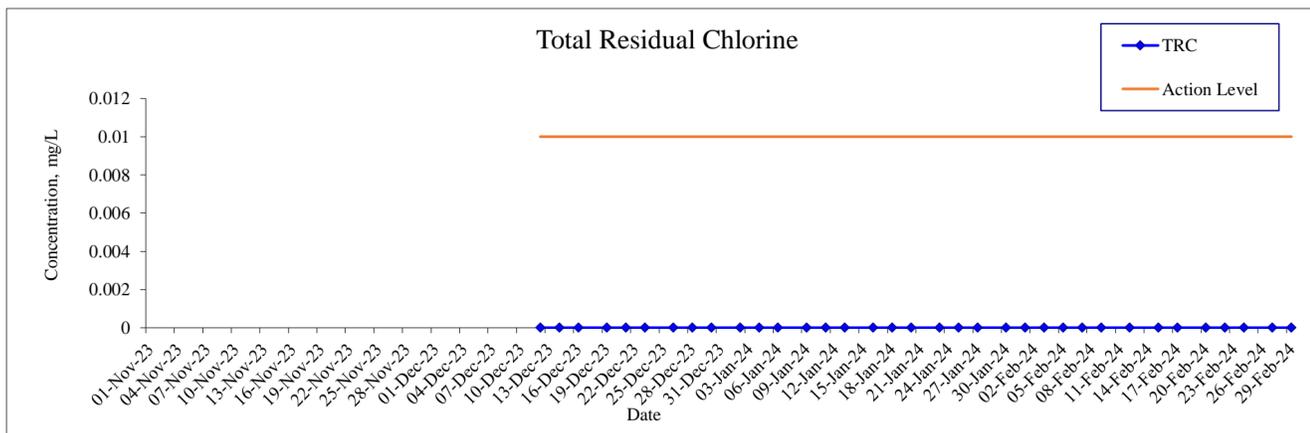


Remark: The lowest detection limit of the Total Residual Chlorine is 0.01mg/L. All result of Total Residual Chlorine monitoring are lower than the detection limit.


Monitoring Location: WSR37

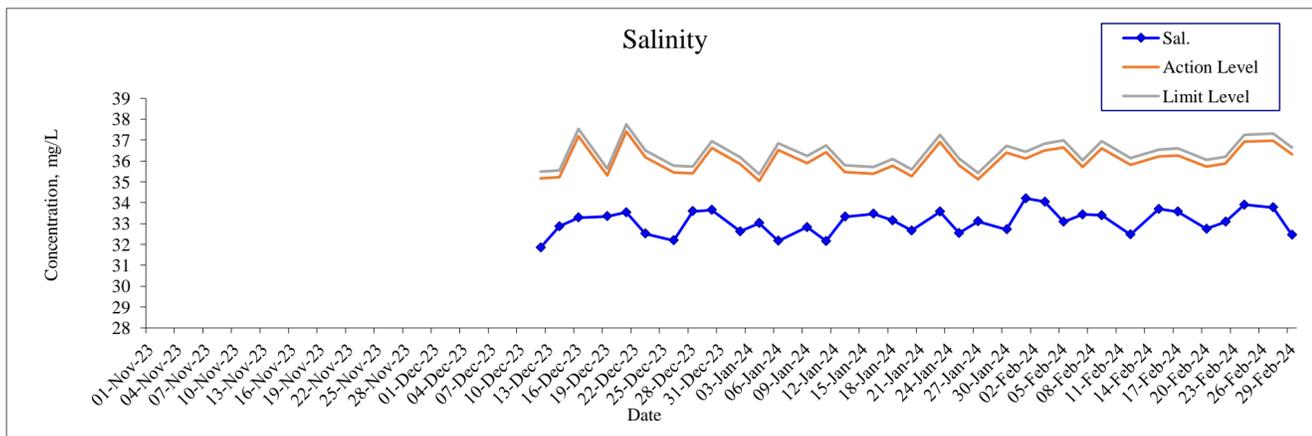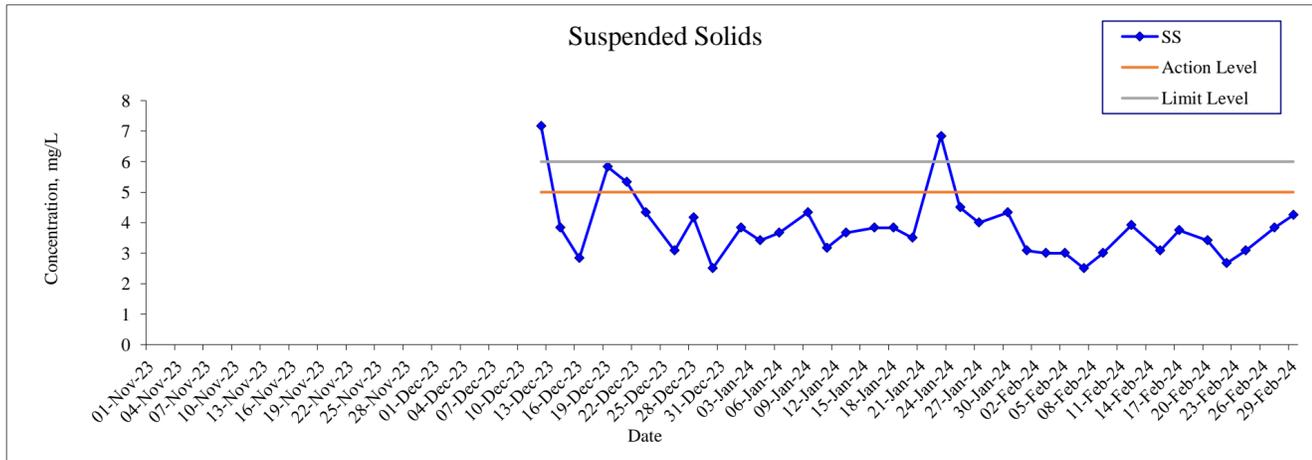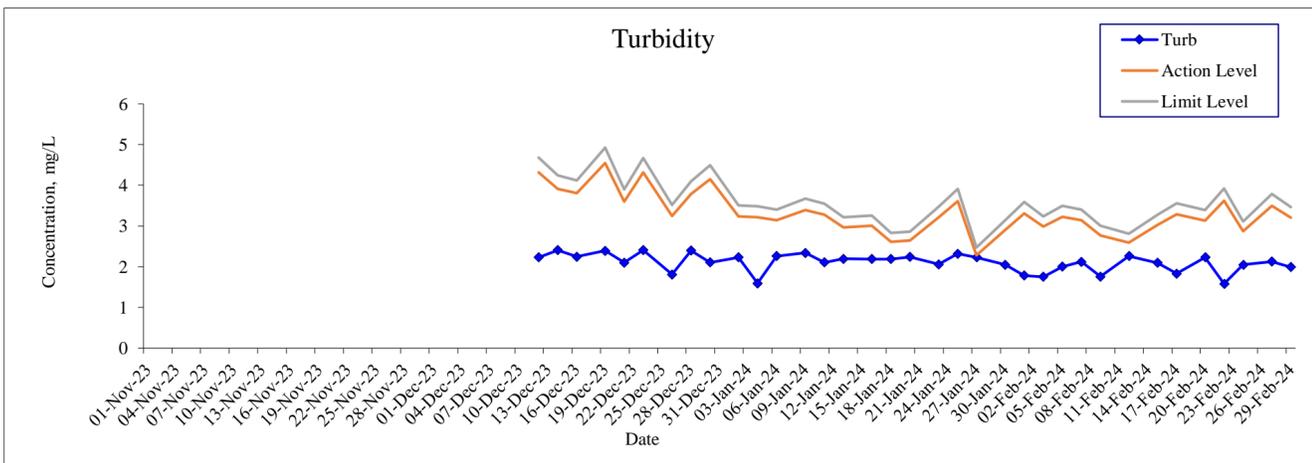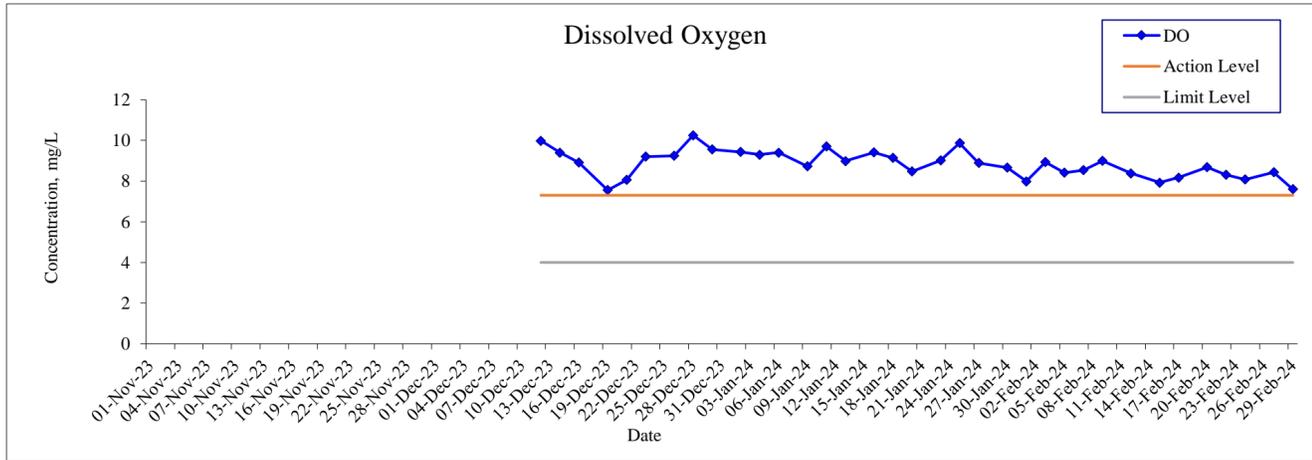

Monitoring Location: WSR37




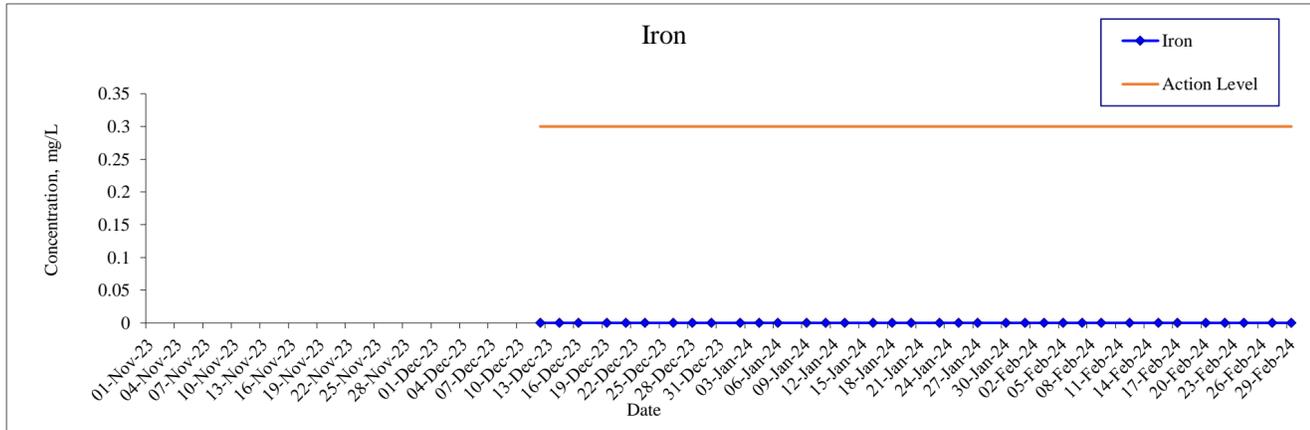


Remark: The lowest detection limit of the Iron is 0.1mg/L. All result of iron monitoring are lower than the detection limit.

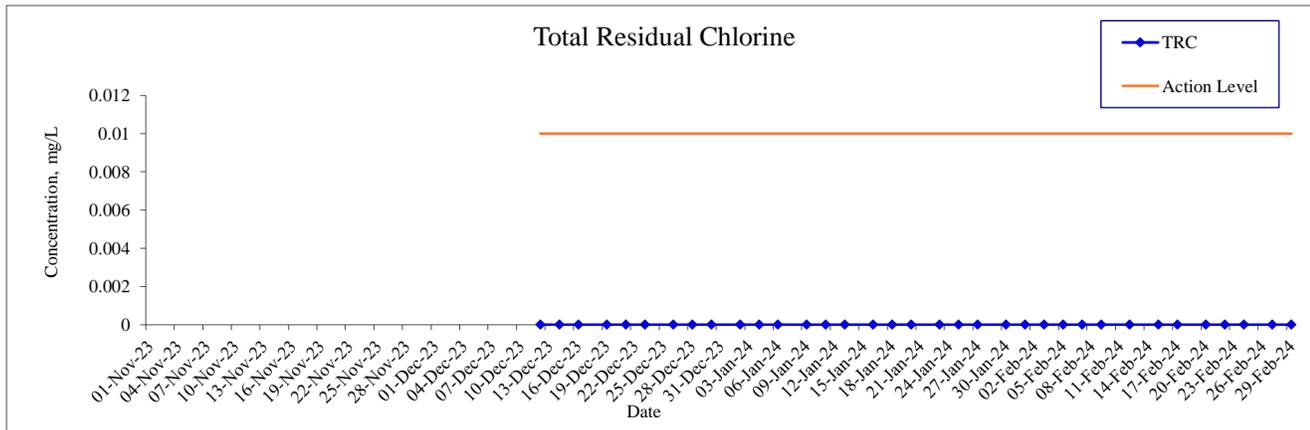


Remark: The lowest detection limit of the Total Residual Chlorine is 0.01mg/L. All result of Total Residual Chlorine monitoring are lower than the detection limit.


Monitoring Location: NF1

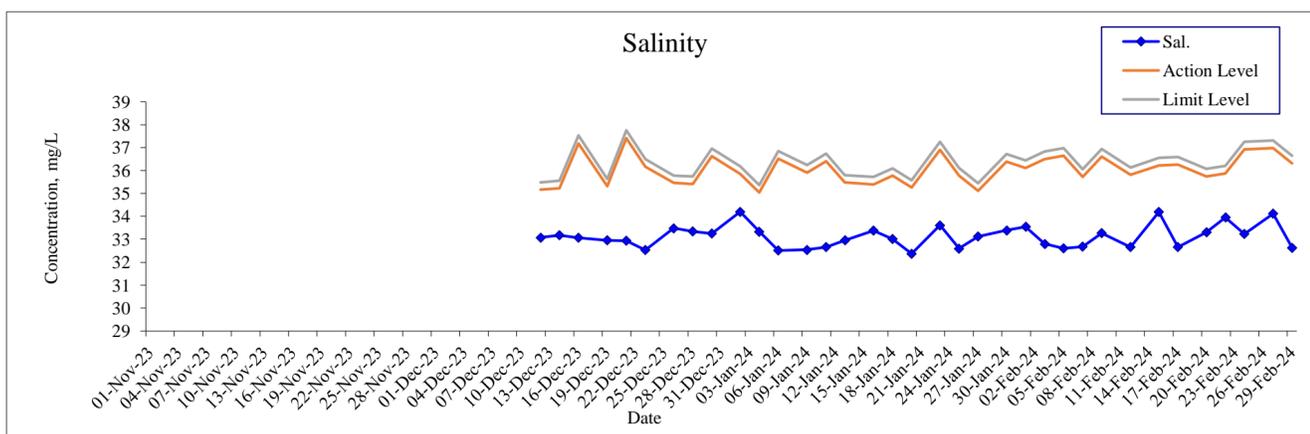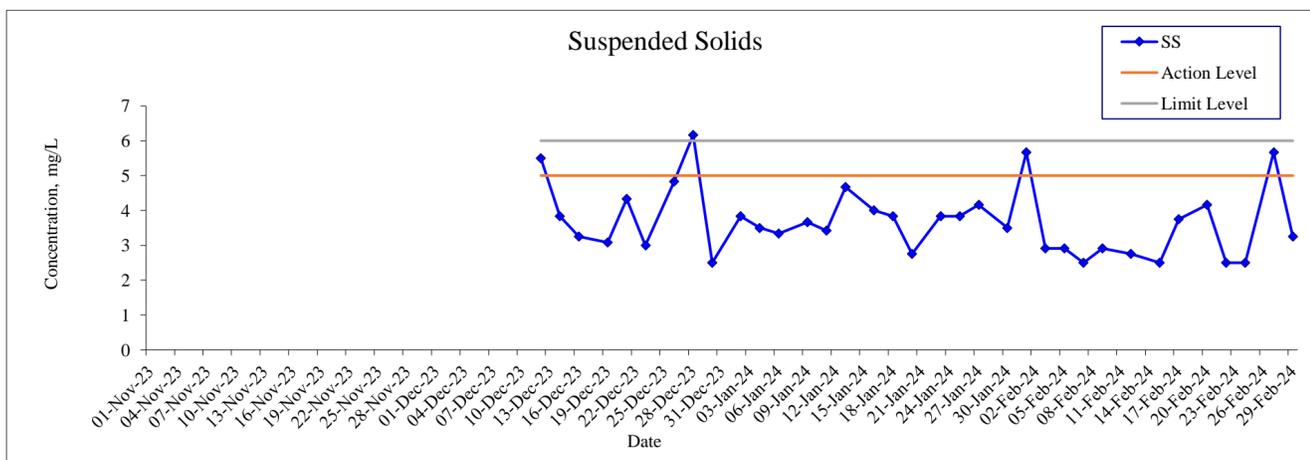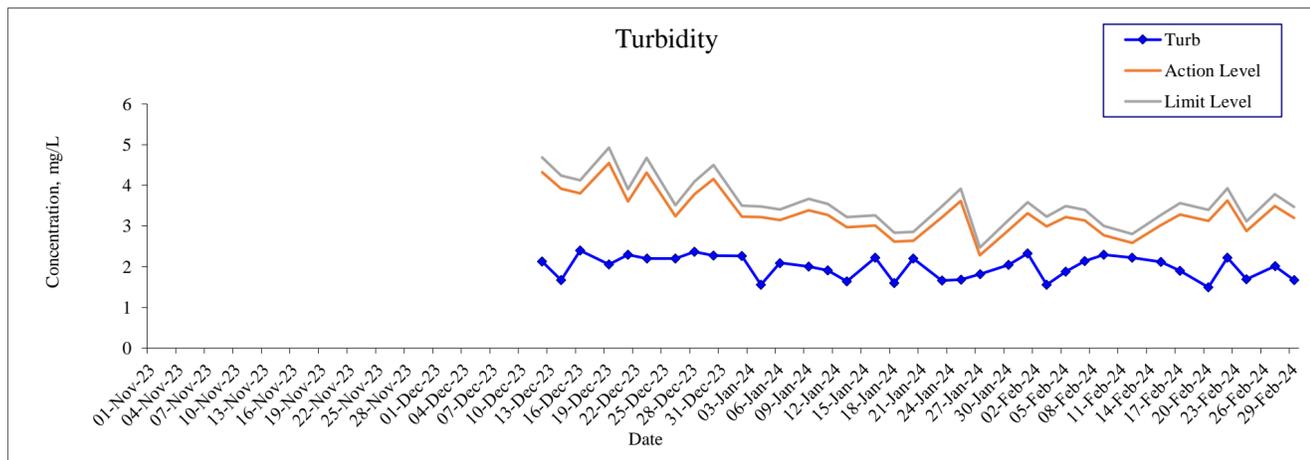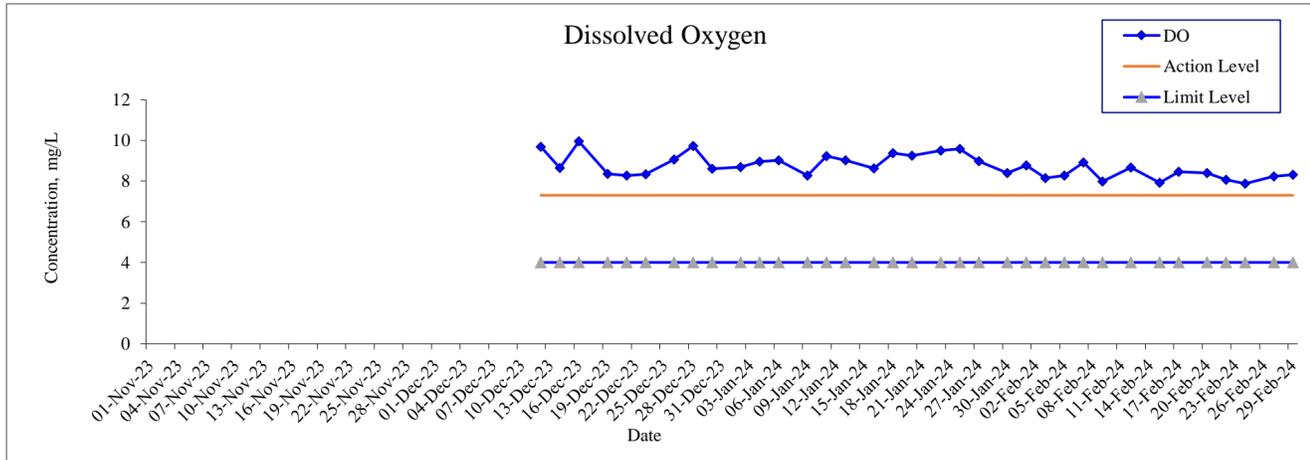

Monitoring Location: NF1




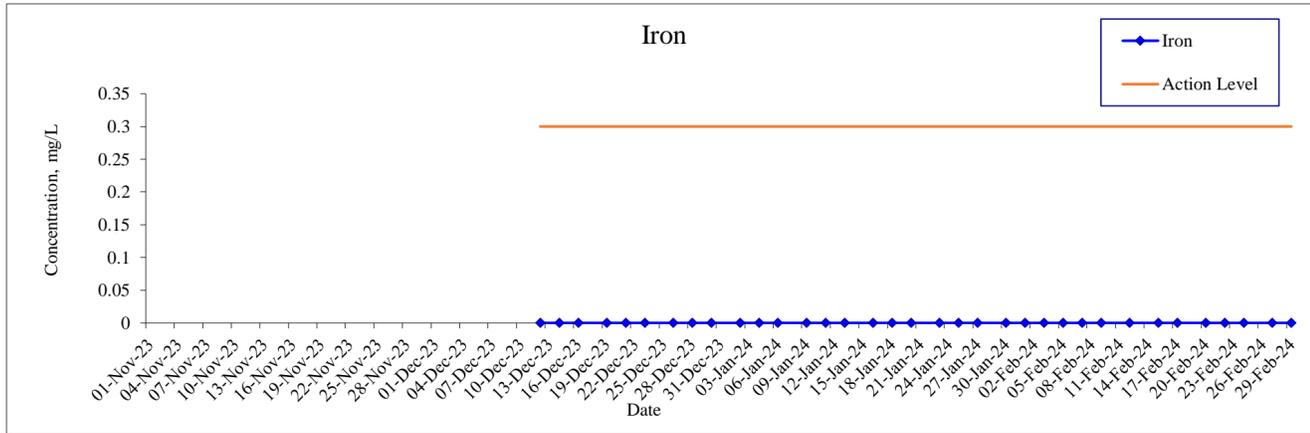


Remark: The lowest detection limit of the Iron is 0.1mg/L. All result of iron monitoring are lower than the detection limit.

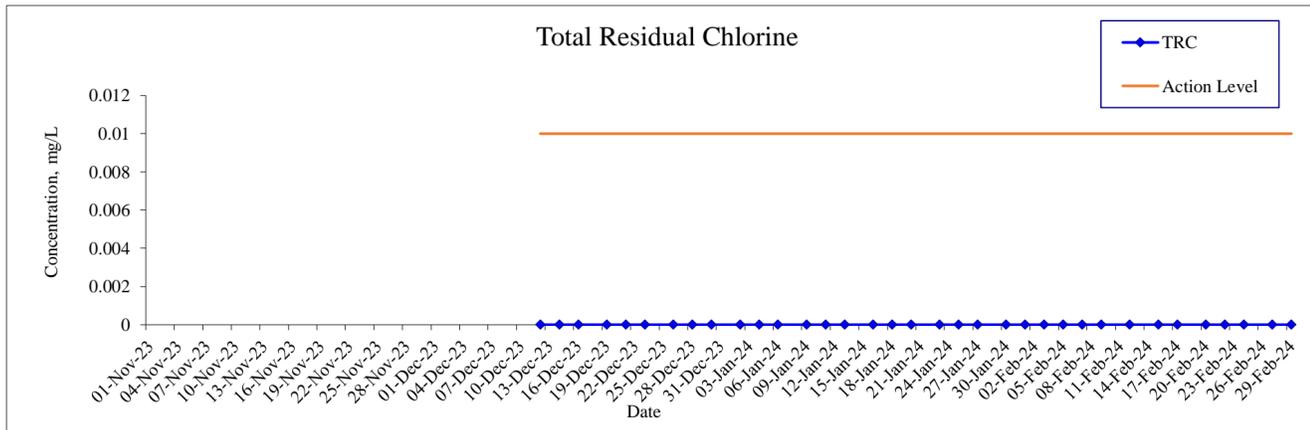


Remark: The lowest detection limit of the Total Residual Chlorine is 0.01mg/L. All result of Total Residual Chlorine monitoring are lower than the detection limit.


Monitoring Location: NF2

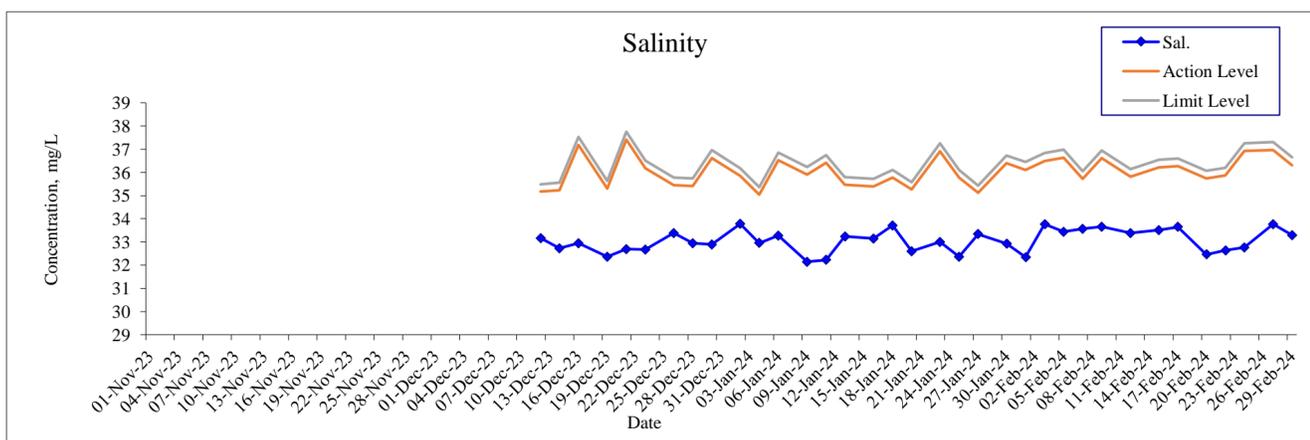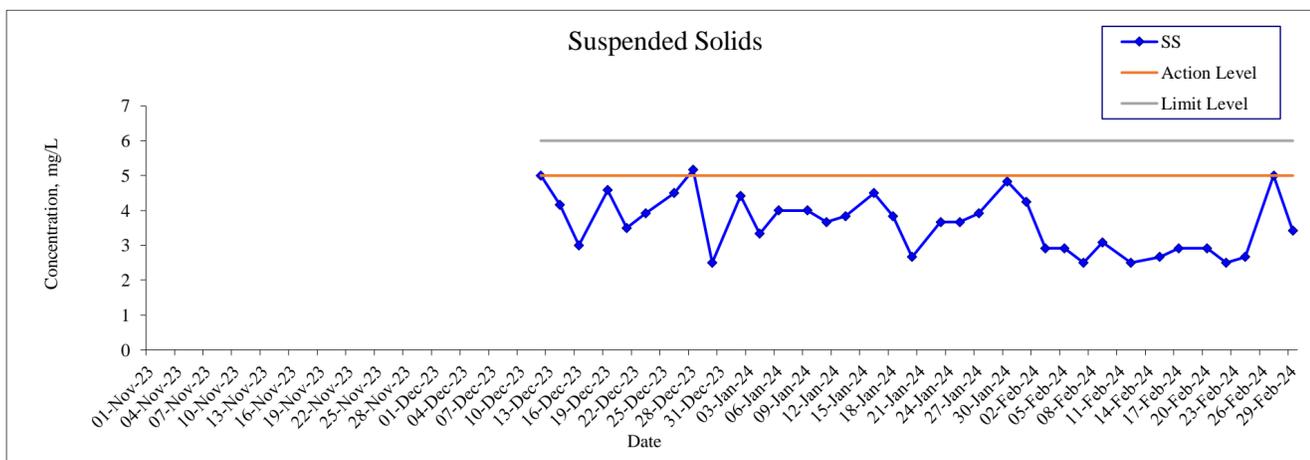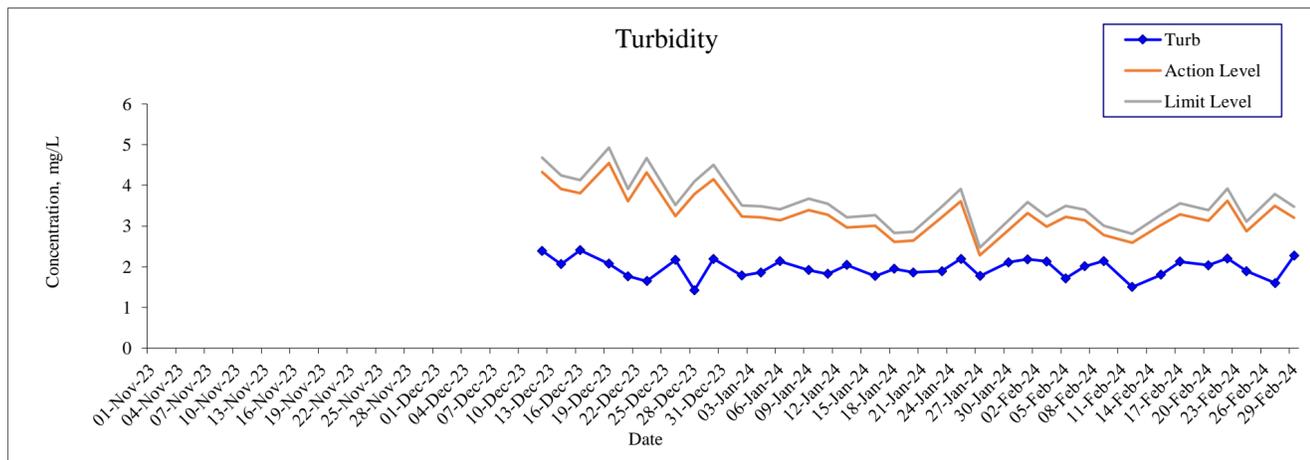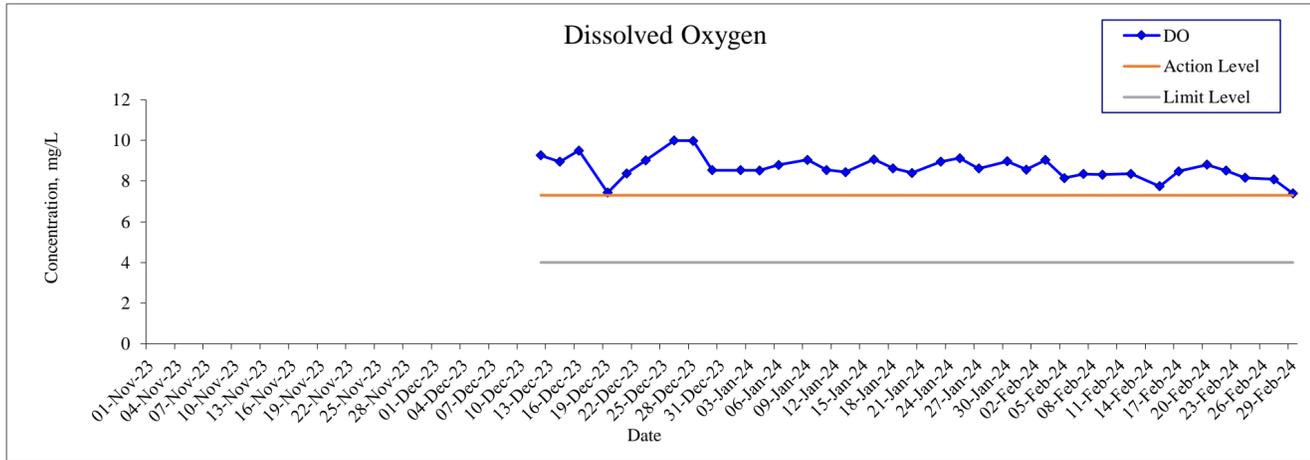

Monitoring Location: NF2




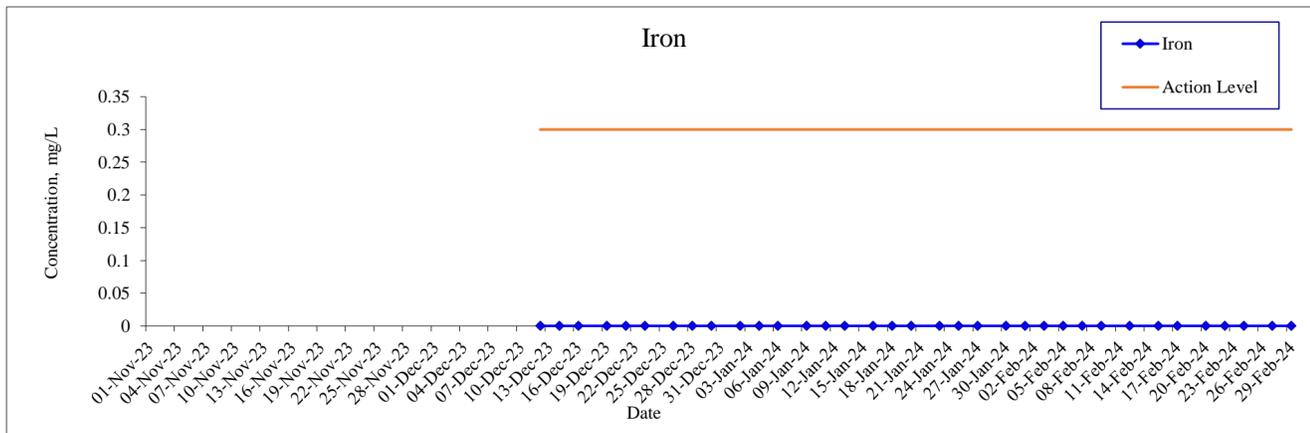


Remark: The lowest detection limit of the Iron is 0.1mg/L. All result of iron monitoring are lower than the detection limit.

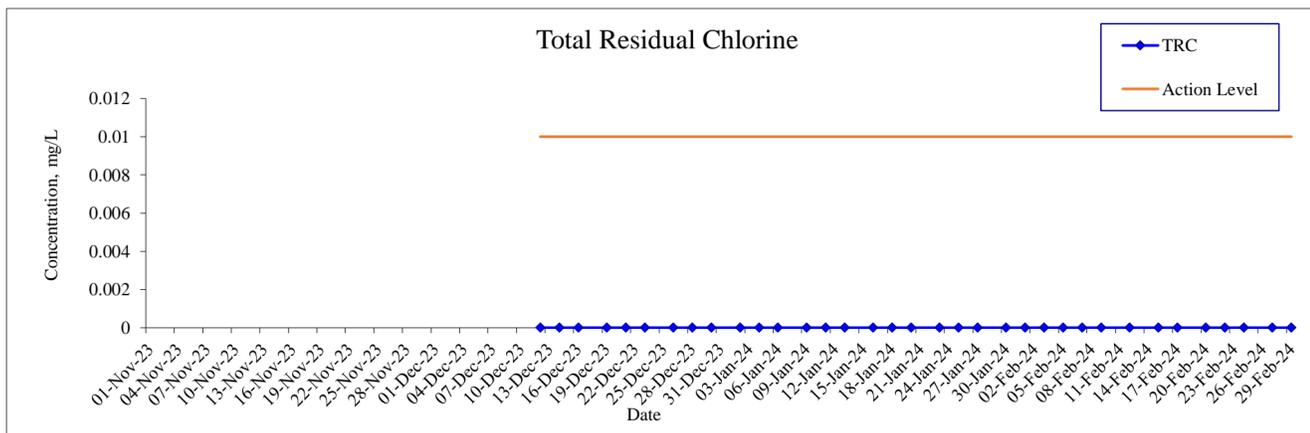


Remark: The lowest detection limit of the Total Residual Chlorine is 0.01mg/L. All result of Total Residual Chlorine monitoring are lower than the detection limit.


Monitoring Location: NF3

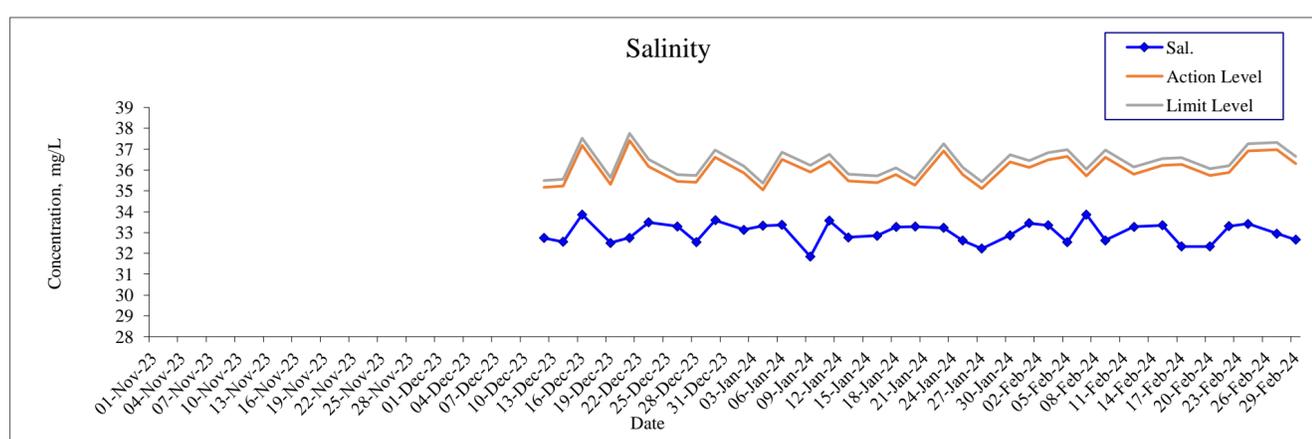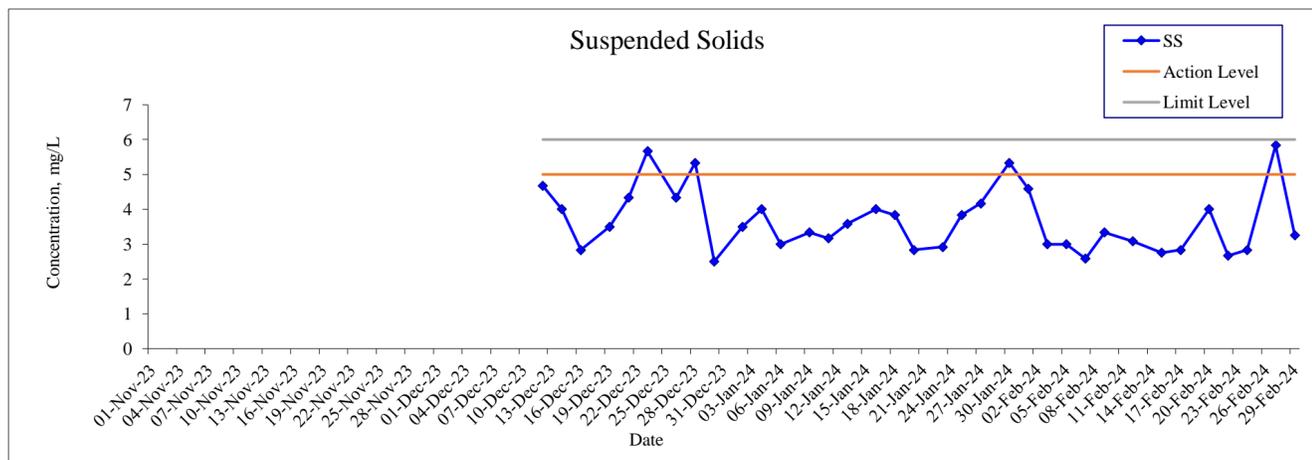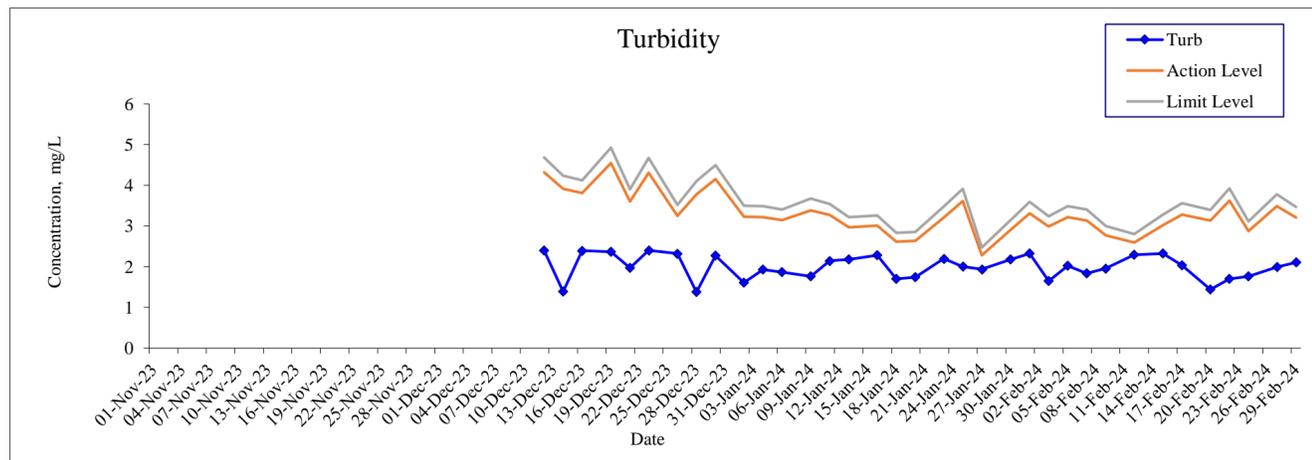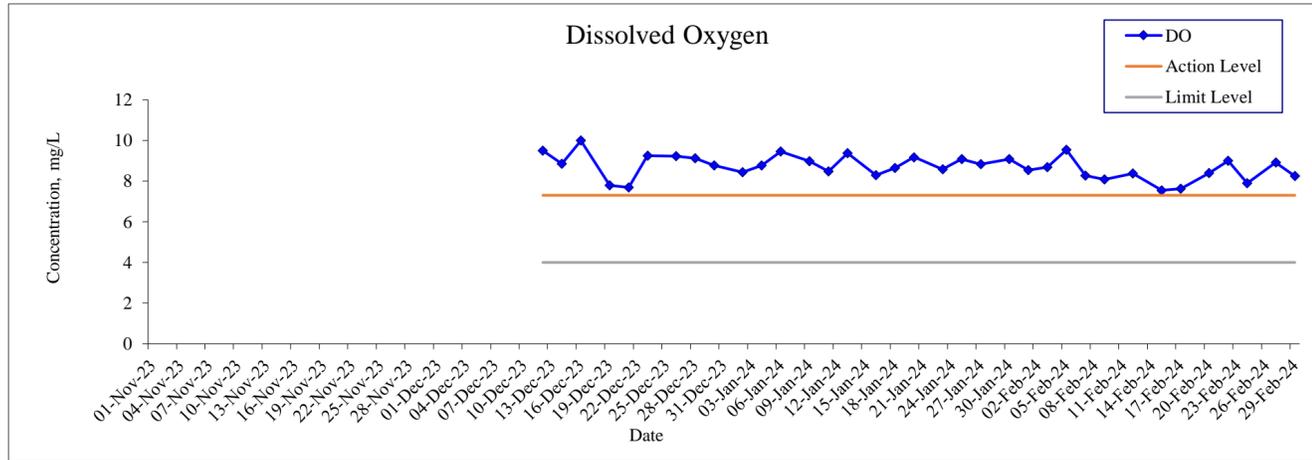

Monitoring Location: NF3

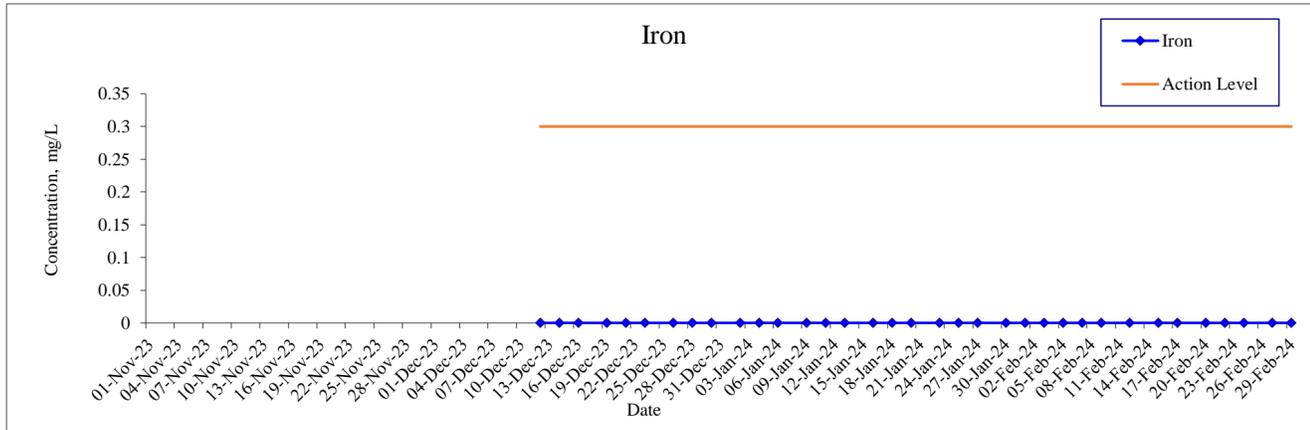

Remark: The lowest detection limit of the Iron is 0.1mg/L. All result of iron monitoring are lower than the detection limit.

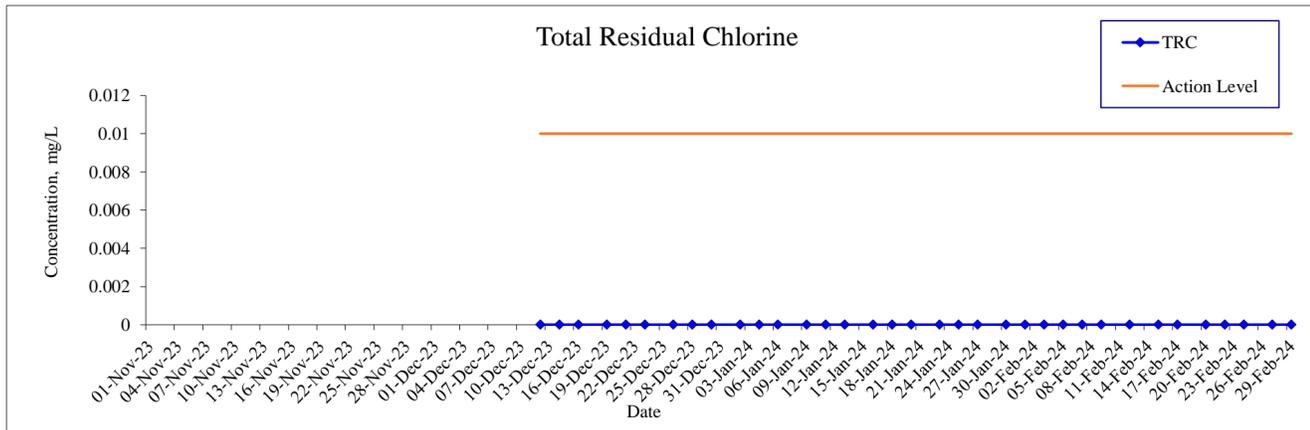

Remark: The lowest detection limit of the Total Residual Chlorine is 0.01mg/L. All result of Total Residual Chlorine monitoring are lower than the detection limit.

Appendix D.1

Weather Condition

Daily Extract of Meteorological Observations , November 2023

 Year Month

Day	Hong Kong Observatory								King's Park	Waglan Island [^]	
	Mean Pressure (hPa)	Air Temperature			Mean Dew Point (deg. C)	Mean Relative Humidity (%)	Mean Amount of Cloud (%)	Total Rainfall (mm)	Total Bright Sunshine (hours)	Prevailing Wind Direction (degrees)	Mean Wind Speed (km/h)
		Absolute Daily Max (deg. C)	Mean (deg. C)	Absolute Daily Min (deg. C)							
01	1017.7	29.1	25.8	23.6	19.7	70	36	0.0	10.3	070	27.8
02	1015.5	28.4	25.8	24.4	21.0	75	56	0.0	8.6	070	19.5
03	1013.6	29.1	26.0	24.3	21.7	78	42	0.0	9.8	080	13.8
04	1013.9	29.4	26.3	24.7	21.8	76	34	0.0	9.4	070	15.2
05	1014.4	30.1	26.7	25.0	22.1	77	38	0.0	8.9	050	12.3
06	1015.1	30.7	27.6	25.3	20.3	65	31	0.0	9.3	010	15.5
07	1016.5	26.8	25.9	25.3	19.9	70	80	0.0	0.3	070	36.0
08	1015.8	26.0	25.2	24.7	20.8	77	88	0.0	0.4	080	35.1
09	1015.4	27.3	25.7	24.8	22.2	81	88	Trace	1.3	070	29.6
10	1016.0	29.3	26.9	25.6	23.5	82	83	0.0	6.4	070	19.2
11	1017.7	26.5	25.3	24.8	22.6	85	88	2.5	0.0	080	39.2
12	1020.2	26.6	24.0	22.0	19.5	77	84	0.6	3.9	010	30.5
13	1022.7	25.2	22.0	20.3	15.6	67	79	0.0	6.0	360#	29.0#
14	1022.6	23.9	20.8	18.9	15.2	70	79	0.0	2.6	010#	19.4#
15	1021.7	25.2	22.8	20.7	17.2	71	67	0.0	8.8	070	32.4
16	1023.6	24.0	21.5	17.3	14.4	65	66	0.0	3.9	360	35.0
17	1023.9	21.9	18.8	15.6	3.5	37	9	0.0	10.1	360	41.2
18	1022.9	23.0	19.5	16.6	6.2	42	21	0.0	10.0	360	24.2
19	1020.9	23.3	20.5	18.5	12.3	59	42	0.0	9.1	070	14.3
20	1019.4	24.6	21.3	19.0	14.2	65	23	0.0	9.9	060	18.0
21	1017.5	24.6	22.0	20.3	16.1	70	18	0.0	9.9	080	24.0
22	1016.3	25.7	22.6	20.5	17.4	73	26	0.0	9.9	080	14.4
23	1016.4	26.3	23.0	20.5	17.9	74	42	0.0	9.8	010	6.4
24	1019.6	25.0	22.9	21.5	16.3	67	36	0.0	9.3	070	42.8
25	1021.0	24.3	21.9	20.0	15.1	66	19	0.0	9.9	070	41.0
26	1020.1	25.3	22.1	19.8	15.8	68	20	0.0	9.8	060	21.0
27	1018.1	26.7	23.0	20.2	16.4	68	14	0.0	9.6	010	6.0
28	1018.7	25.4	22.8	20.2	14.9	61	37	Trace	8.4	070	27.7
29	1018.7	24.0	22.7	21.2	17.6	73	85	0.2	0.6	070	30.7
30	1019.9	26.0	23.8	21.9	18.6	73	79	0.0	2.0	070	25.4
Mean/Total	1018.5	26.1	23.5	21.6	17.3	69	50	3.3	208.2	070	24.9
Climatological Normal [?]	1017.3	24.5	22.2	20.3	16.7	72	58	39.3	172.3	070	26.6

data incomplete

[^] Information of wind direction and wind speed for Waglan Island are based on automatic weather station data since August 1989

Trace means rainfall less than 0.05 mm

? 1991-2020 Climatological Normal, unless otherwise specified

Daily Extract of Meteorological Observations , December 2023

Back Year 2023 Month 12 Go

Day	Hong Kong Observatory								King's Park	Waglan Island [^]	
	Mean Pressure (hPa)	Air Temperature			Mean Dew Point (deg. C)	Mean Relative Humidity (%)	Mean Amount of Cloud (%)	Total Rainfall (mm)	Total Bright Sunshine (hours)	Prevailing Wind Direction (degrees)	Mean Wind Speed (km/h)
		Absolute Daily Max (deg. C)	Mean (deg. C)	Absolute Daily Min (deg. C)							
01	1021.5	23.2	21.5	19.6	15.5	69	85	0.0	2.9	010	30.0
02	1021.7	21.5	20.0	18.2	14.4	70	79	0.0	1.1	070	22.2
03	1020.4	23.3	21.4	20.1	16.4	73	87	Trace	2.1	070	23.4
04	1017.2	24.4	21.9	20.5	17.3	76	66	Trace	5.2	080	10.9
05	1015.6	24.1	21.7	19.7	16.7	73	57	0.0	9.5	360	5.8
06	1017.6	22.5	21.5	19.9	14.7	67	81	Trace	2.2	360	18.5
07	1017.8	25.1	21.0	18.4	9.1	47	30	0.0	9.7	360	19.8
08	1016.7	24.0	21.4	19.2	15.1	68	56	0.0	8.1	070	17.6
09	1014.6	24.9	22.9	21.6	19.3	80	80	0.0	6.5	060	14.9
10	1013.8	26.3	23.9	22.5	20.1	80	76	Trace	7.5	050	14.2
11	1014.6	27.3	24.2	22.3	21.5	85	68	0.3	2.7	040	5.1
12	1016.2	28.7	24.7	22.3	20.9	80	42	0.3	8.2	080	12.4
13	1019.4	23.2	22.3	21.6	19.1	82	93	Trace	0.2	070	31.8
14	1018.7	24.6	23.1	21.7	19.6	81	88	Trace	0.3	060	21.5
15	1016.3	26.9	24.4	23.2	20.9	81	79	0.0	7.5	050	12.0
16	1020.5	23.9	18.9	13.5	13.4	71	85	0.1	2.8	360	32.7
17	1024.9	15.2	13.4	11.4	7.9	69	88	0.0	0.0	010	30.8
18	1022.1	19.0	17.3	14.8	13.7	80	88	Trace	0.0	040	29.0
19	1021.2	19.0	16.8	14.7	12.4	75	72	0.0	3.2	350	22.2
20	1023.3	15.6	13.6	10.8	7.1	65	67	0.0	1.0	350	34.9
21	1027.1	12.3	10.9	9.8	4.6	65	86	0.0	0.0	350	39.8
22	1030.1	12.3	10.5	8.6	0.9	51	88	0.0	0.4	360	33.0
23	1029.9	13.3	11.0	8.1	2.9	58	64	0.2	1.8	360	30.3
24	1028.6	16.5	13.3	10.1	3.6	52	23	0.0	9.4	360	26.9
25	1026.7	18.2	14.9	12.1	4.8	51	50	0.0	9.4	360	24.8
26	1025.2	19.6	16.6	14.5	9.4	63	65	0.0	6.5	060	23.4
27	1024.0	21.8	18.7	16.6	11.1	62	88	Trace	2.5	040	16.4
28	1022.3	23.6	20.1	18.2	15.0	73	74	Trace	5.1	050	21.8
29	1021.1	21.0	19.4	18.3	15.7	79	72	0.0	5.8	060	29.5
30	1018.3	23.0	20.7	18.3	15.0	70	79	Trace	6.1	040	8.2
31	1018.0	25.7	21.8	19.0	16.7	73	59	0.0	8.3	040	8.4
Mean/Total	1020.8	21.6	19.1	17.1	13.4	70	71	0.9	136.0	360	21.7
Climatological Normal [?]	1020.1	20.4	18.2	16.2	12.4	70	57	28.8	161.6	010	26.4

[^] Information of wind direction and wind speed for Waglan Island are based on automatic weather station data since August 1989

Trace means rainfall less than 0.05 mm

? 1991-2020 Climatological Normal, unless otherwise specified

Daily Extract of Meteorological Observations , January 2024

Back Year 2024 Month 1 Go

Day	Hong Kong Observatory								King's Park	Waglan Island [^]	
	Mean Pressure (hPa)	Air Temperature			Mean Dew Point (deg. C)	Mean Relative Humidity (%)	Mean Amount of Cloud (%)	Total Rainfall (mm)	Total Bright Sunshine (hours)	Prevailing Wind Direction (degrees)	Mean Wind Speed (km/h)
		Absolute Daily Max (deg. C)	Mean (deg. C)	Absolute Daily Min (deg. C)							
01	1019.9	22.0	19.9	18.8	15.4	75	68	0.0	8.6	080	34.1
02	1019.1	20.5	18.7	17.8	14.3	76	59	0.0	3.1	070	26.0
03	1020.0	21.6	18.8	15.7	11.7	64	45	0.0	7.8	010	26.4
04	1020.9	19.6	17.0	15.4	10.8	67	29	0.0	8.8	050	22.8
05	1020.2	22.0	18.8	16.6	14.2	75	24	0.0	9.5	060	15.5
06	1020.1	23.8	20.2	17.8	15.6	76	34	0.0	9.3	030	6.8
07	1021.0	21.8	19.9	18.6	14.4	71	60	0.0	9.0	080	33.4
08	1019.6	20.6	19.1	17.7	14.1	73	70	Trace	6.6	070	30.9
09	1017.2	23.9	20.5	18.1	16.2	77	46	Trace	8.0	040	11.8
10	1018.6	23.2	20.3	17.9	13.7	67	33	0.0	9.0	010	19.0
11	1020.0	21.5	18.9	17.6	13.0	69	59	Trace	8.1	060	21.3
12	1019.1	21.8	18.9	17.1	14.2	75	53	0.0	7.7	060	16.0
13	1019.9	22.0	19.6	17.8	10.5	57	59	0.0	5.7	070	27.9
14	1021.1	23.8	20.7	18.5	11.2	56	48	0.0	5.4	050	22.0
15	1021.2	24.8	20.9	18.8	15.2	71	28	0.0	9.8	070	24.3
16	1022.1	20.5	18.7	17.5	14.1	75	74	0.0	5.7	070	38.5
17	1020.4	20.6	19.2	17.7	14.0	72	78	0.1	2.8	060	29.3
18	1017.7	24.2	21.2	19.1	16.3	74	47	0.0	8.3	050	20.6
19	1016.3	24.2	21.1	19.2	16.5	76	25	0.0	9.8	030	15.3
20	1016.3	24.6	21.4	19.5	16.8	75	50	0.0	7.9	360	12.3
21	1020.3	21.3	19.1	16.3	12.9	68	72	Trace	3.1	360	23.9
22	1023.3	18.5	15.0	9.8	10.0	72	88	0.5	0.0	360	36.4
23	1028.5	10.4	7.9	6.3	3.5	75	88	2.7	0.3	360	41.3
24	1029.2	12.5	9.2	6.5	1.6	59	87	0.0	4.4	360	25.5
25	1028.7	15.5	12.3	9.5	3.8	56	78	0.0	4.2	360	17.7
26	1027.3	17.8	15.0	13.1	7.6	61	84	0.0	5.1	040	22.2
27	1025.8	18.8	15.5	13.1	9.2	67	87	1.0	1.2	030	19.5
28	1026.4	15.7	13.7	11.7	11.0	83	87	2.4	0.1	040	20.1
29	1023.4	17.8	15.9	14.3	12.8	82	88	Trace	0.3	060	26.1
30	1020.7	20.2	18.3	16.8	16.2	88	88	Trace	0.2	050	19.8
31	1019.4	20.2	19.3	17.9	17.9	92	91	Trace	0.0	040	16.5
Mean/Total	1021.4	20.5	17.9	15.9	12.5	72	62	6.7	169.8	060	23.3
Climatological Normal [?]	1020.1	18.7	16.5	14.6	11.7	74	62	33.2	145.8	060	25.1

[^] Information of wind direction and wind speed for Waglan Island are based on automatic weather station data since August 1989

Trace means rainfall less than 0.05 mm

? 1991-2020 Climatological Normal, unless otherwise specified

Day	Hong Kong Observatory								King's Park	Waglan Island [^]	
	Mean Pressure (hPa)	Air Temperature			Mean Dew Point (deg. C)	Mean Relative Humidity (%)	Mean Amount of Cloud (%)	Total Rainfall (mm)	Total Bright Sunshine (hours)	Prevailing Wind Direction (degrees)	Mean Wind Speed (km/h)
		Absolute Daily Max (deg. C)	Mean (deg. C)	Absolute Daily Min (deg. C)							
01	1018.0	23.9	21.1	19.8	19.8	92	77	0.2	5.2	040	9.4
02	1017.6	25.7	21.7	18.6	19.6	88	73	Trace	7.0	060	15.5
03	1018.8	22.5	19.6	17.7	17.0	85	89	Trace	3.7	060	24.0
04	1017.3	20.5	19.8	19.3	18.5	92	88	Trace	0.1	030	14.9
05	1018.8	21.7	20.4	19.6	18.0	86	88	Trace	0.5	030	15.3
06	1019.6	20.3	19.1	18.0	16.7	86	88	0.6	1.5	070	28.6
07	1017.3	18.4	16.8	14.7	15.1	90	94	Trace	0.0	050	23.4
08	1018.8	14.8	13.0	11.6	10.4	84	88	2.2	0.0	360	22.8
09	1023.5	14.2	12.7	11.0	8.6	77	88	0.6	0.1	360	22.5
10	1026.5	18.6	14.4	11.3	9.4	72	55	0.5	4.4	360	18.4
11	1026.9	22.8	17.4	13.6	8.8	60	14	0.0	10.4	050	16.4
12	1025.8	21.2	18.1	15.5	8.6	55	20	0.0	10.5	070	34.1
13	1023.2	22.8	19.2	16.8	13.6	71	52	0.0	8.9	050	21.6
14	1020.2	25.1	21.0	18.3	17.0	78	56	0.0	10.5	030	11.7
15	1019.0	26.0	22.3	19.7	16.4	70	70	0.0	9.7	350	6.7
16	1019.7	22.0	20.4	19.4	16.2	77	60	Trace	6.2	080	22.3
17	1017.4	21.2	19.5	17.8	16.3	82	88	Trace	2.2	060	23.3
18	1015.2	23.6	21.6	19.9	19.4	87	85	0.0	2.4	040	11.5
19	1015.1	25.1	22.7	21.1	20.7	88	87	0.0	1.1	090	6.0
20	1014.7	26.0	23.9	22.0	21.6	87	83	0.0	4.1	100	9.2
21	1014.5	27.8	24.5	22.5	21.2	82	55	0.0	9.5	120	6.6
22	1016.6	25.2	23.6	22.4	21.2	87	71	0.0	2.8	080	6.0
23	1019.9	22.9	20.4	19.3	17.8	85	88	Trace	0.0	040	25.6
24	1021.1	21.6	18.8	17.5	13.9	73	88	Trace	1.2	020	18.2
25	1020.7	19.2	17.1	15.6	11.8	71	79	0.0	3.1	010	12.9
26	1021.1	21.1	18.2	16.8	13.9	76	86	Trace	1.5	040	20.5
27	1020.9	19.5	17.6	15.9	12.5	73	88	Trace	0.5	050	25.1
28	1018.0	19.3	18.3	17.5	15.8	85	91	Trace	0.0	070	31.2
29	1017.6	22.0	18.7	16.2	16.1	85	88	Trace	0.3	050	22.1
Mean/Total	1019.4	21.9	19.4	17.6	15.7	80	75	4.1	107.4	060	18.1
Climatological Normal [?]	1018.7	19.4	17.1	15.3	13.2	79	72	38.9	101.7	060	24.2

[^] Information of wind direction and wind speed for Waglan Island are based on automatic weather station data since August 1989

Trace means rainfall less than 0.05 mm

? 1991-2020 Climatological Normal, unless otherwise specified

Appendix D.2

Key Activities Carried Out During the Reporting Quarter

November 2023

<p>Administration Building</p> <ul style="list-style-type: none">• Carrying out the floor tiles works at G/F• External wall painting works• Construction of block work for pipe duct• Installation of building services, cable laying, electrical switchboard, testing and commissioning
<p>Chemical building</p> <ul style="list-style-type: none">• Installation of leakage collection pit cover• Underground utility construction work• Landscape work at roof• Defect rectification
<p>Main Electrical & Central Chiller Plant Building</p> <ul style="list-style-type: none">• Installation of chillers, building services, electrical switchboard and cable laying• Installation of Roof Tile for Fuel Tank Room
<p>ActiDAFF</p> <ul style="list-style-type: none">• Underground utility construction work• Installation of access opening cover• Construction of staircase no 2• Installation of mechanical equipment, piping system, installation of building services, electrical switchboards and cable laying, fiber-reinforced plastic cover Installation
<p>Product Water Storage Tank Building</p> <ul style="list-style-type: none">• Installation of Cat Ladders in Water Tank A• Sealing slab opening in water Tank A• Re-construction of Wall PW8 in Water Tank A• Installation of metal cladding, building services, cable laying, mechanical equipment, steel pipe• Underground utility construction
<p>OSCG Building</p> <ul style="list-style-type: none">• Protective Coating for dangerous goods Rooms• Placing Soil Mix at Roof• Installation of Metal Cladding (at East Side)• Installation of Roller Shutters and Window• Underground utility construction work• Installation of building services, mechanical equipment and cable laying, testing and commissioning
<p>Reverse Osmosis Building</p> <ul style="list-style-type: none">• Installation of building services, electrical switchboard, cable laying, Installation of mechanical equipment, steel pipe, GRP pipe, raised floor, testing and commissioning• Installation of metal cladding, handrailing, roller shutters, glass canopy and glass house• Underground utility construction work• Construction of RC External Wall for Male Toilet
<p>Post Treatment Building</p>

- Installation of building services, Installation of mechanical equipment and piping system, Pressure Test
- Underground utility construction work
- Installation of Cat Ladders in Water Tanks and Metal Cladding
- Placing Soil Mix at Roof

Inspection corridor

- Installation of building services, Lift installation
- Construction of roof tiling works and staircases no. 2
- Installation of Movement Joints and glass window

CO2 Tanks

- Installation of pipes and electrical wiring, testing and commissioning

Combined Shaft and Pump room

- Finishing, Grating; window; louvre installation

Other

- Watermain works at CLP 132 kV Substation
- Staircases construction; Steel Bridge assembly and installation at elevated walkway
- Road Construction, Footpath Construction, Landscape Construction, Irrigation System Construction, Water Pressure Test for Fire Services and Plumbing System in Zone A, B, C
- Structure Construction, steel fence erection of Wave Deflector Wall at seawall area

December 2023

Administration Building

- Landscaping works on roof of building.
- External wall aluminum features installation
- Finishing works for doghouse.
- Installation of building services, cable laying, electrical switchboard, Pressure Test, electrical switchboard, testing and commissioning

Chemical building

- Landscape work at roof
- Construction of hose reel cabinet.
- Defect rectification

Main Electrical & Central Chiller Plant Building

- Installation of Roof Tile for Fuel Tank Room
- Minor Installation of building services, electrical switchboard, cable laying, pressure test

ActiDAFF

- Underground utility construction work
- Installation of access opening covers for filtered water tank
- Carrying out finishing works for staircase no. 3
- Minor Installation of mechanical equipment, piping system, building services, electrical switchboards and cable laying, fiber-reinforced plastic cover Installation

Product Water Storage Tank Building

- Water Test in Tank A
- Waterproofing work at Roof Slab on Tank A
- Tank A water test and defect rectification
- Installation of building services, cable laying, Installation of mechanical equipment, steel pipe, Pressure Test

OSCG Building

- Installation of Railing on Brine Maker Tank
- Protective Coating for dangerous goods Rooms
- Installation of building services, mechanical equipment and cable laying, Lightning Installation, testing and commissioning

Reverse Osmosis Building

- Installation of Handrailings
- Installation of Glass House
- Installation of building services, electrical switchboard, cable laying, Photovoltaic Panel. Minor Installation of mechanical equipment and raised floor, testing and commissioning
- Underground utility construction work

Post Treatment Building

- Installation of Cat Ladders in Water Tanks
- Placing Soil Mix at Roof
- Curb Construction for Rescue Opening at Water Tanks
- Installation of building services, mechanical equipment and piping system, Pressure Test

Inspection corridor

- Construction of roof tiling works
- Installation of steel balustrade at roof
- Installation of Movement Joints
- Installation of glass window
- Installation of building services, Lift Installation

CO2 Tanks

- Tank surface cleaning, testing and commissioning

Combined Shaft and Pump room

- Internal finishing, defect rectification

Guard House

- Installation of Building Services
- Workshop construction work

Other

- Glass Roof and Glass Canopy installation at elevated walkway
- Security Fence footing construction work
- Manhole 5 Glass Reinforced Plastic Pipe Installation work
- Underground utility rectification work
- Road Construction
- Traffic signage work
- Footpath Construction
- Landscape Construction
- Landscape planting work
- Irrigation System Construction
- Slope work – Shotcreting; Rock anchor installation, Rock break
- Water Pressure Test for Fire Services and Plumbing System
- Traffic signage work

January 2024

<p>Administration Building</p> <ul style="list-style-type: none">• Carrying out the floor tiles works at G/F• External wall painting works• Construction of block work for pipe duct• Installation of building services, cable laying, electrical switchboard, testing and commissioning
<p>Chemical building</p> <ul style="list-style-type: none">• Installation of leakage collection pit cover• Underground utility construction work• Landscape work at roof• Defect rectification
<p>Main Electrical & Central Chiller Plant Building</p> <ul style="list-style-type: none">• Installation of chillers, building services, electrical switchboard and cable laying• Installation of Roof Tile for Fuel Tank Room
<p>ActiDAFF</p> <ul style="list-style-type: none">• Underground utility construction work• Installation of access opening cover• Construction of staircase no 2• Installation of mechanical equipment, piping system, installation of building services, electrical switchboards and cable laying, fiber-reinforced plastic cover Installation
<p>Product Water Storage Tank Building</p> <ul style="list-style-type: none">• Installation of Cat Ladders in Water Tank A• Sealing slab opening in water Tank A• Re-construction of Wall PW8 in Water Tank A• Installation of metal cladding, building services, cable laying, mechanical equipment, steel pipe• Underground utility construction
<p>OSCG Building</p> <ul style="list-style-type: none">• Protective Coating for dangerous goods Rooms• Placing Soil Mix at Roof• Installation of Metal Cladding (at East Side) and Roller Shutters and Window• Underground utility construction work• Installation of building services, mechanical equipment and cable laying, testing and commissioning
<p>Reverse Osmosis Building</p> <ul style="list-style-type: none">• Installation of building services, electrical switchboard, cable laying, Installation of mechanical equipment, steel pipe, Glass Reinforced Plastic pipe, raised floor, testing and commissioning• Installation of metal cladding, handrailing, roller shutters, glass canopy and glass house• Underground utility construction work• Construction of Reinforced Concrete External Wall for Male Toilet

Post Treatment Building

- Installation of building services, Installation of mechanical equipment and piping system, Pressure Test
- Underground utility construction work
- Installation of Cat Ladders in Water Tanks
- Installation of Metal Cladding
- Placing Soil Mix at Roof

Inspection corridor

- Installation of building services, Lift installation
- Construction of roof tiling works and staircases no. 2
- Installation of Movement Joints and glass window

CO2 Tanks

- Installation of pipes and electrical wiring, testing and commissioning

Combined Shaft and Pump room

- Finishing, Grating; window; louvre installation

Other

- Watermain works at CLP 132 kV Substation
- Staircases construction; Steel Bridge assembly and installation at elevated walkway
- Road Construction, Footpath Construction, Landscape Construction, Irrigation System Construction, Water Pressure Test for Fire Services and Plumbing System in Zone A, B, C
- Structure Construction, steel fence erection of Wave Deflector Wall at seawall area

February 2024

<p>Administration Building</p> <ul style="list-style-type: none">• Sealing up wall opening• External wall painting works• Construction of block work for pipe duct.• Installation of glass door for laboratory• Minor Installation of building services, cable laying and termination, Photovoltaic Panel Installation, Testing & Commissioning
<p>Chemical building</p> <ul style="list-style-type: none">• Installation of Irrigation system• Construction of hose reel cabinet.• Defect rectification
<p>Main Electrical & Central Chiller Plant Building</p> <ul style="list-style-type: none">• Installation of Roof Tile for Fuel Tank Room• Minor Installation of building services, electrical switchboard, cable laying, pressure test
<p>ActiDAFF</p> <ul style="list-style-type: none">• Underground utility construction work• Installation of drainpipe on corridor• Minor Installation of mechanical equipment, installation of building services, Minor cable laying and termination, Installation of Lightning System, Installation of Fiber Reinforced Polymer Cover Installation, Testing & Commissioning
<p>Product Water Storage Tank Building</p> <ul style="list-style-type: none">• Underground utility construction work• Water Test in Tank A and defect rectification• Waterproofing work at Roof Slab on Tank A• Tank A water test and defect rectification• Installation of building services, cable laying and termination, Testing & Commissioning
<p>OSCG Building</p> <ul style="list-style-type: none">• Installation of Railing on Brine Maker Tank• Protective Coating for dangerous goods Rooms• Installation of building services, mechanical equipment and cable laying and termination, testing and commissioning
<p>Reverse Osmosis Building</p> <ul style="list-style-type: none">• Placing Soil Mix at Roof• Installation of Glass House• Underground utility construction work• Installation of building services, electrical switchboard of cable laying and termination, Minor Installation of mechanical equipment and raised floor, testing and commissioning, Photovoltaic Panel Installation

Post Treatment Building

- Installation of Cat Ladders in Irrigation Tanks
- Placing Soil Mix at Roof
- Curb Construction for Rescue Opening at Water Tanks
- Minor Installation of building services, Minor Installation of mechanical equipment, Cable laying and termination, Pressure Test

Inspection corridor

- Construction of roof tiling
- Internal decoration and finishing works
- Installation of building services, Lift Installation

CO2 Tanks

- Tank surface cleaning, testing and commissioning

Combined Shaft and Pump room

- CCTV Installation, Installation of Lightning System, Minor building services Installation, testing and commissioning
- Internal finishing, defect rectification

Guard House

- Installation of Building Services
- Workshop construction work
- Architectural Builders Works and Finishes

Other

- Master meter Room Architectural Builders Works and Finishes
- Open Channel and Wave deflector Wall
- Glass Roof and Glass Canopy installation at elevated walkway
- Security Fence footing construction work
- Manhole 5 Glass Reinforced Plastic Pipe Installation work
- Underground utility rectification work
- Road Construction
- Traffic signage work
- Footpath Construction
- Landscape Construction
- Landscape planting work
- Irrigation System Construction
- Slope work – Shotcreting; Rock anchor installation, Rock break
- Water Pressure Test for Fire Services and Plumbing System
- Open Channel and Wave deflector Wall
- Traffic signage work

Appendix D.3

Other Factor Might Affect the Monitoring Results

Other Factors might affect the monitoring results			
Reporting Period			
Nov 2023	Dec 2023	Jan 2024	Feb 2024
--	N/A	N/A	N/A

Appendix E

Summary of Exceedances

Table E1 Summary of Exceedance in Dec 2023

Date	Station	Tide	SS Level (mg/L)	Action Level	Limit Level
12/12/2023	WSR16	Ebb	5.83	Y	Y
	WSR36	Ebb	6.50	Y	Y
	NF1	Ebb	7.17	Y	Y
	NF2	Ebb	5.50	Y	N
14/12/2023	WSR36	Flood	4.50	Y	Y
	NF2	Flood	4.17	Y	N
16/12/2023	WSR1	Flood	3.50	Y	N
	WSR2	Flood	3.58	Y	N
19/12/2023	WSR4	Flood	4.58	Y	N
	WSR37	Flood	5.83	Y	Y
	NF2	Flood	4.58	Y	N
21/12/2023	WSR1	Flood	4.00	Y	N
	WSR2	Flood	4.67	Y	Y
	WSR3	Flood	4.83	Y	Y
	WSR4	Flood	4.33	Y	Y
	WSR16	Flood	4.17	Y	Y
	WSR33	Flood	4.17	Y	Y
	NF1	Flood	4.83	Y	Y
	NF2	Flood	4.50	Y	Y
23/12/2023	NF3	Ebb	5.67	Y	Y
26/12/2023	WSR1	Flood	4.00	Y	N
	WSR2	Flood	4.67	Y	Y
	WSR3	Flood	4.83	Y	Y
	WSR4	Flood	4.33	Y	Y
	WSR16	Flood	4.17	Y	Y
	WSR33	Flood	4.17	Y	Y
	NF1	Flood	4.83	Y	Y
	NF2	Flood	4.50	Y	Y
	NF3	Flood	4.33	Y	Y
26/12/2023	WSR3	Flood	4.83	Y	Y
	WSR16	Flood	5.17	Y	Y
	NF1	Flood	6.17	Y	Y
	NF2	Flood	5.17	Y	Y
	NF3	Flood	5.33	Y	Y

Table E2 Summary of Exceedance in Jan 2024

Date	Station	Tide	SS Level (mg/L)	Action Level	Limit Level
04/01/2024	WSR3	Flood	3.50	Y	N
	WSR36	Flood	4.08	Y	Y
	NF1	Flood	3.50	Y	N
	NF3	Flood	4.00	Y	Y
11/01/2024	WSR2	Ebb	4.50	Y	N
	WSR3	Ebb	5.17	Y	Y
13/01/2024	NF1	Flood	4.67	Y	N
18/01/2024	WSR33	Flood	4.83	Y	Y
	WSR36	Flood	5.33	Y	Y
23/01/2024	WSR1	Ebb	6.83	Y	Y
	WSR2	Ebb	6.67	Y	Y
	WSR3	Ebb	5.67	Y	N
	WSR16	Ebb	5.33	Y	N
	WSR33	Ebb	6.83	Y	Y
	WSR36	Ebb	6.00	Y	Y
	WSR37	Ebb	6.83	Y	Y
30/01/2024	NF3	Flood	5.33	Y	N

Table E3 Summary of Exceedance in Feb 2024

Date	Station	Tide	SS Level (mg/L)	Action Level	Limit Level
01/02/2024	WSR3	Flood	4.50	Y	Y
	WSR4	Flood	5.17	Y	Y
	WSR16	Flood	4.50	Y	Y
	NF1	Flood	5.67	Y	Y
	NF2	Flood	4.25	Y	Y
	NF3	Flood	4.58	Y	Y
07/02/2024	WSR2	Flood	4.50	Y	Y
	WSR3	Flood	5.17	Y	Y
09/02/2024	NF3	Flood	4.50	Y	N
12/02/2024	WSR1	Flood	5.67	Y	Y
20/02/2024	WSR16	Flood	3.42	Y	N
	WSR33	Flood	3.75	Y	Y
	WSR37	Flood	3.42	Y	N
	NF1	Flood	4.17	Y	Y
	NF3	Flood	4.00	Y	Y
27/02/2024	WSR2	Flood	3.17	Y	N
	WSR3	Flood	4.83	Y	Y
	WSR4	Flood	3.67	Y	Y
	WSR16	Flood	3.83	Y	Y
	WSR33	Flood	4.17	Y	Y
	WSR36	Flood	3.50	Y	Y
	WSR37	Flood	3.83	Y	Y
	NF1	Flood	5.67	Y	Y
	NF2	Flood	5.00	Y	Y
NF3	Flood	5.83	Y	Y	
29/02/2024	WSR4	Flood	5.17	Y	Y
	WSR27	Flood	4.25	Y	Y

Appendix F

Waste Flow Table

Contract No. 13/WSD/17

Environmental Management Plan for Design, Build and Operate First Stage of Tseung Kwan O Desalination Plant

Appendix F - Monthly Summary Waste Flow Table

Name of Department: WSD

Contract No.: 13/WSD/17

Monthly Summary Waste Flow Table for 2023 (year)

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)
Jan	3383.820	0.000	0.000	0.000	3383.820	0.000	0.000	0.000	0.000	0.000	143.690
Feb	0.000	0.000	0.000	0.000	0.000	0.002	0.138	0.010	0.000	0.000	115.880
Mar	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	205.410
Apr	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	255.720
May	2088.990	0.000	0.000	0.000	2088.990	0.000	0.000	0.000	0.000	0.000	202.270
Jun	1955.240	0.000	0.000	0.000	1955.240	0.000	0.000	0.0017	0.000	0.000	189.680
Sub-total	7428.050	0.000	0.000	0.000	7428.050	0.002	0.138	0.012	0.000	0.000	1112.650
Jul	121.060	0.000	0.000	0.000	121.060	0.008	0.150	0.042	0.000	0.000	186.110
Aug	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	168.220
Sep	762.550	0.000	0.000	0.000	762.550	0.000	148.944	0.000	0.000	0.000	172.440
Oct	568.600	0.000	0.000	0.000	568.600	0.000	18.574	0.010	0.000	0.000	185.010
Nov	15.430	0.000	0.000	0.000	15.430	0.000	0.000	0.000	0.000	0.000	116.960
Dec	215.220	0.000	0.000	0.000	215.220	0.000	0.000	0.000	0.000	0.000	79.680
Total	9110.910	0.000	0.000	0.000	9110.910	0.010	167.806	0.064	0.000	0.000	2021.070

Notes:

- (1) The performance targets are given in Section 1.69 of Specification B
- (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- (3) Plastics refer to plastic bottles/containers, plastic sheets/ foam from packaging material

Contract No. 13/WSD/17

Environmental Management Plan for Design, Build and Operate First Stage of Tseung Kwan O Desalination Plant

Appendix F - Monthly Summary Waste Flow Table

Name of Department: WSD

Contract No.: 13/WSD/17

Monthly Summary Waste Flow Table for 2024 (year)

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)
Jan	4978.345	0.000	0.000	4667.745	310.600	0.000	0.000	0.000	0.000	0.000	77.800
Feb	*22448.146	0.000	0.000	21883.006	*565.140	0.000	0.000	0.000	0.000	0.000	*39.580
Mar											
Apr											
May											
Jun											
Sub-total	27426.491	0.000	0.000	26550.751	875.740	0.000	0.000	0.000	0.000	0.000	117.380
Jul											
Aug											
Sep											
Oct											
Nov											
Dec											
Total	27426.491	0.000	0.000	26550.751	875.740	0.000	0.000	0.000	0.000	0.000	117.380

Notes:

- (1) The performance targets are given in Section 1.69 of Specification B
 - (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
 - (3) Plastics refer to plastic bottles/containers, plastic sheets/ foam from packaging material
- *The record in EPD Transaction Records system was up to 22/02/2024, the data from 23/02 to 29/02 will be updated in next reporting period.

Appendix G

Complaint Log

Table G1 Statistical Summary of Environmental Complaints

Reporting Period	Environmental Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
1 December 2023 - 29 February 2024	1	2	Noise

Table G2 Statistical Summary of Environmental Summons

Reporting Period	Environmental Summons Statistics		
	Frequency	Cumulative	Details
1 December 2023 - 29 February 2024	0	0	N/A

Table G3 Statistical Summary of Environmental Prosecution

Reporting Period	Environmental Prosecution Statistics		
	Frequency	Cumulative	Details
1 December 2023 - 29 February 2024	0	0	N/A

Appendix H

Event/ Action Plan for Water Quality Exceedance

Table G1 Event and Action Plan for Water Quality Monitoring

Event	Action ET	IEC	Contractor(s)	ER
Action Level being exceeded by one sampling day	<ol style="list-style-type: none"> Repeat <i>in situ</i> measurement on the next day of exceedance to confirm findings; Check monitoring data, plant, equipment and Contractor(s)'s working methods; Identify source(s) of impact and record in notification of exceedance; Inform IEC, Contractor(s) and ER. 	<ol style="list-style-type: none"> Check monitoring data submitted by ET and Contractor(s)'s working methods; Inform EPD. 	<ol style="list-style-type: none"> Confirm receipt of notification of exceedance in writing; Check plant and equipment and rectify unacceptable practice 	<ol style="list-style-type: none"> Confirm receipt of notification of exceedance in writing.
Action Level being exceeded by two or more consecutive sampling days	<ol style="list-style-type: none"> Repeat <i>in situ</i> measurement on the next day of exceedance to confirm findings; Check monitoring data, plant, equipment and Contractor(s)'s working methods; Identify source(s) of impact and record in notification of exceedance; Inform IEC, Contractor(s) and ER; Discuss with IEC and Contractor(s) on additional mitigation measures and ensure that they are implemented 	<ol style="list-style-type: none"> Check monitoring data submitted by ET and Contractor(s)'s working methods; Inform EPD; Discuss with ET and Contractor(s) on additional mitigation measures and advise ER accordingly; Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> Confirm receipt of notification of exceedance in writing; Check plant and equipment and rectify unacceptable practice; Consider changes of working methods; Discuss with ET and IEC on additional mitigation measures and propose them to ER within 3 working days; Implement the agreed mitigation measures. 	<ol style="list-style-type: none"> Confirm receipt of notification of exceedance in writing; Discuss with the IEC on the proposed additional mitigation measures and agree on the mitigation measures to be implemented. Ensure additional mitigation measures are properly implemented.
Limit Level being exceeded by one sampling day	<ol style="list-style-type: none"> Repeat <i>in situ</i> measurement on the next day of exceedance to confirm findings; Check monitoring data, plant, equipment and Contractor(s)'s working methods; Identify source(s) of impact and record in notification of exceedance; Inform IEC, Contractor(s) and ER; Discuss with IEC and Contractor(s) on additional mitigation measures and ensure that they are implemented 	<ol style="list-style-type: none"> Check monitoring data submitted by ET and Contractor(s)'s working methods; Inform EPD; Discuss with ET and Contractor(s) on additional mitigation measures and advise ER accordingly; Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> Confirm receipt of notification of exceedance in writing; Check plant and equipment and rectify unacceptable practice; Critically review the need to change working methods; Discuss with ET and IEC on additional mitigation measures and propose them to ER within 3 working days; Implement the agreed mitigation measures. 	<ol style="list-style-type: none"> Confirm receipt of notification of exceedance in writing; Discuss with the IEC on the proposed additional mitigation measures and agree on the mitigation measures to be implemented. Ensure additional mitigation measures are properly implemented. Request Contractor(s) to critically review the working methods.
Limit Level being exceeded by two or more consecutive sampling days	<ol style="list-style-type: none"> Repeat <i>in situ</i> measurement on the next day of exceedance to confirm findings; Check monitoring data, plant, equipment and Contractor(s)'s working methods; Identify source(s) of impact and record in notification of exceedance; Inform IEC, Contractor(s) and ER; Discuss with IEC and Contractor(s) on additional mitigation measures and ensure that they are implemented 	<ol style="list-style-type: none"> Check monitoring data submitted by ET and Contractor(s)'s working methods; Inform EPD; Discuss with ET and Contractor(s) on additional mitigation measures and advise ER accordingly; Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> Confirm receipt of notification of exceedance in writing; Check plant and equipment and rectify unacceptable practice; Critically review the need to change working methods; Discuss with ET and IEC on additional mitigation measures and propose them to ER within 3 working days; Implement the agreed mitigation measures. As directed by ER, slow down or stop all or part of the marine construction works/ production volume of the desalination plant until no exceedance of Limit Level. 	<ol style="list-style-type: none"> Confirm receipt of notification of exceedance in writing; Discuss with the IEC on the proposed additional mitigation measures and agree on the mitigation measures to be implemented. Ensure additional mitigation measures are properly implemented. Request Contractor(s) to critically review the working methods; Consider and instruct, if necessary, the Contractor(s) to slow down or to stop all or part of the marine construction works/ production volume of the desalination plant until no exceedance of Limit Level.

Notes : ET = Environmental Team, IEC = Independent Environmental Checker; ER = Engineering Representatives
 The above actions should be taken within 1 working day after the exceedance is identified during operation phase.

Appendix I

Event/ Action Plan for Construction Noise Exceedance

Table E1 Event and Action Plan for Construction Noise Monitoring

Event	Action			
	ET	IEC	ER	Contractor
Action Level	<ol style="list-style-type: none"> 1. Carry out investigation to identify the source and cause of the complaint/ exceedance(s) 2. Notify IEC, ER, and Contractor and report the results of investigation to the Contractor; ER and the IEC 3. Discuss with the Contractor and IEC for remedial measures required 4. If the complaint is related to the Project, conduct additional monitoring for checking mitigation effectiveness and report the findings and results to the IEC, ER and the Contractor 	<ol style="list-style-type: none"> 1. Review the analyzed results submitted by the ET 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly 3. Supervise the implementation of remedial measures 	<ol style="list-style-type: none"> 1. Confirm receipt of Notification of Exceedance in writing 2. Require Contractor to propose remedial measures for the analysed noise problem 3. Ensure remedial measures are properly implemented 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposals, if required, to the IEC and ER 2. Implement noise mitigation proposals.
Limit Level	<ol style="list-style-type: none"> 1. Carry out investigation to identify the source and cause of the exceedance 2. Notify IEC, ER, Project Proponent, EPD and Contractor 3. Repeat measurements to confirm findings 4. Provide investigation report to IEC, ER, EPD and Contractor he causes of the exceedances 5. If the exceedance is related to the Project, assess effectiveness by additional monitoring. 6. Report the remedial action implemented and the additional monitoring results to IEC, EPD, ER and Contractor 7. If exceedance stops, cease additional monitoring 	<ol style="list-style-type: none"> 1. Review the analyzed results submitted by the ET 2. Discuss the potential remedial measures with ER, ET Leader and Contractor 3. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly 4. Supervise the implementation of remedial measures 	<ol style="list-style-type: none"> 1. Confirm receipt of Notification of Exceedance in writing 2. Require the Contractor to propose remedial measures for the analysed noise problem 3. Ensure remedial measures are properly implemented 4. If exceedance continues, consider what activity of the work is responsible and instruct the Contractor; in agreement with the Project Proponent, to stop that activity of work until the exceedance is abated 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance 2. Submit proposals for remedial actions to IEC and ER within 3 working days of notification 3. Implement the agreed proposals 4. Resubmit proposals if problem still not under control 5. Stop the relevant activity of works as determined by the Project Proponent until the exceedance is abated

Notes : ET = Environmental Team, IEC = Independent Environmental Checker; ER = Engineering Representatives

Appendix J

Event/ Action Plan for Pre-Operation Phase Coral Monitoring Exceedance

Table E3 Event and Action Plan for Pre-Operation Phase Coral Monitoring

Event	Action			
	ET Leader	IEC	SOR **	Contractor
Action Level Exceedance	<ol style="list-style-type: none"> 1. Check monitoring data 2. Inform the IEC, SOR and Contractor of the findings; 3. Increase the monitoring to at least once a month to confirm findings; 4. Propose mitigation measures for consideration 	<ol style="list-style-type: none"> 1. Discuss monitoring with the ET and the Contractor; 2. Review proposals for additional monitoring and any other measures submitted by the Contractor and advise the SOR accordingly. 	<ol style="list-style-type: none"> 1. Discuss with the IEC additional monitoring requirements and any other measures proposed by the ET; 2. Make agreement on the measures to be implemented. 	<ol style="list-style-type: none"> 1. Inform the SOR and confirm notification of the non-compliance in writing; 2. Discuss with the ET and the IEC and propose measures to the IEC and the SOR; 3. Implement the agreed measures.
Limit Level Exceedance	<ol style="list-style-type: none"> 1. Undertake Steps 1-4 as in the Action Level Exceedance. If further exceedance of Limit Level, propose enhancement measures for consideration. 	<ol style="list-style-type: none"> 1. Discuss monitoring with the ET and the Contractor; 2. Review proposals for additional monitoring and any other measures submitted by the Contractor and advise the SOR accordingly. 	<ol style="list-style-type: none"> 1. Discuss with the IEC additional monitoring requirements and any other measures proposed by the ET; 2. Make agreement on the measures to be implemented. 	<ol style="list-style-type: none"> 1. Inform the SOR and confirm notification of the non-compliance in writing; 2. Discuss with the ET and the IEC and propose measures to the IEC and the SOR; 3. Implement the agreed measures.

Remark: ** The "SOR" is equivalent to the "ER" as defined in the EM&A Manual of the Project
